

## **PROJECT PROGRESS REPORT OF THE PROJECTS**

**TAKEN UP BY**

**PROJECT MANAGEMENT UNIT**

**REBUILD KERALA INITIATIVE**

*Date: 31<sup>st</sup> December 2022*


## Contents

|   |    |
|---|----|
| 1. INTRODUCTION.....  | 3  |
| 2. OVERVIEW OF STATUS OF WORKS – AS WISE .....                              | 4  |
| 3. CONSOLIDATED AS WISE STATUS .....  | 5  |
| 4. OVERVIEW OF STATUS OF WORKS – DISTRICT WISE.....                         | 6  |
| 5. DISTRICT WISE STATUS OF PROJECTS .....                                   | 7  |
| 6. SOME PROJECT PHOTOS.....   | 8  |
| 7. GO(Rt) No 485/2019/P&EA dated 15/11/2019 (266.03) – Pathanamthitta ..... | 12 |
| 8. GO(Rt) No 485/2019/P&EA dated 15/11/2019 (266.03) – Idukki .....         | 14 |
| 9. GO(Rt) No 485/2019/P&EA dated 15/11/2019 (266.03) – Wayanad .....        | 16 |
| 10. G.O. (Rt.) No.224/2020/P&EA, TVM, Dated 26/05/2020 (53.136Cr) .....     | 18 |
| 11. G.O. (Rt.)No. 115/2020/P&EA, TVM, Dated 28/02/2020 (4.75 C).....        | 20 |
| 12. G.O.(Rt)No.1389/2020/LSGD Dated,TVM, 23/07/2020 (1.605 Cr) .....        | 21 |
| 13. G.O. (Rt.) No.404/2020/P&EA, TVM, Dated 23/10/2020 (40 Cr) .....        | 22 |
| 14. GO (Rt) No. 62/2021/P&EA , Dated 03/02/2021 (42.32 Cr) .....            | 23 |
| 15. G.O.(Rt)No.348/2021/P&EA, 15.08.2021 (30.91 Cr) .....                   | 25 |
| 16. G.O.(Rt)No.18/2022/P&EA, 07.01.2022 (49.34 Cr) .....                    | 26 |
| 17. G.O.(Rt)No.300/2022/P&EA, .....   | 28 |
| 18. DETAILS OF WORKS IN ALAPPUZHA DISTRICT .....                            | 41 |
| 19. DETAILS OF WORKS IN PATHANAMTHITTA DISTRICT .....                       | 45 |
| 20. DETAILS OF WORKS IN KOTTAYAM DISTRICT .....                             | 48 |
| 21. DETAILS OF WORKS IN IDUKKI DISTRICT.....                                | 50 |
| 22. DETAILS OF WORKS IN ERNAKULAM DISTRICT.....                             | 53 |
| 23. DETAILS OF WORKS IN THRISSUR DISTRICT .....                             | 56 |
| 24. DETAILS OF WORKS IN WAYANAD DISTRICT .....                              | 57 |
| 25. LIST OF BRIDGES FOR WHICH DPR TO BE PREPARED .....                      | 61 |

## 1. INTRODUCTION

Between June 1 and 19 August 2018, our State of Kerala went through the worst ever floods in history since 1924. One sixth of the State's population — about 5.4 million of us, Keralites — were affected. The floods and the accompanying landslides were catastrophic in terms of loss of lives, livelihoods, property and infrastructure. Govt: of Kerala addressed the phenomena in a comprehensive and systematic way by formulating REBUILD KERALA DEVELOPMENT PROGRAMME, a Resilient Recovery Policy Framework and Action Plan for Shaping Kerala's Resilient, Risk-Informed Development and Recovery from 2018 Floods . The key sectors identified in the RKDP are:, Integrated Water Resource Management, Water Supply, Sanitation, Urban, Roads and Bridges, Transportation, Forestry, Agriculture, Animal Husbandry and Dairy Development, Fisheries, Livelihoods and Land. RURAL ROADS which are back bone to the rural economy were drastically affected by the flood and are given due consideration by Kerala Government. As a part of Rebuild Kerala Initiative, the Government constituted a Project Management Unit (PMU) under Local Self Government Department for the effective management of projects assigned to the department.


## 2. OVERVIEW OF STATUS OF WORKS – AS WISE

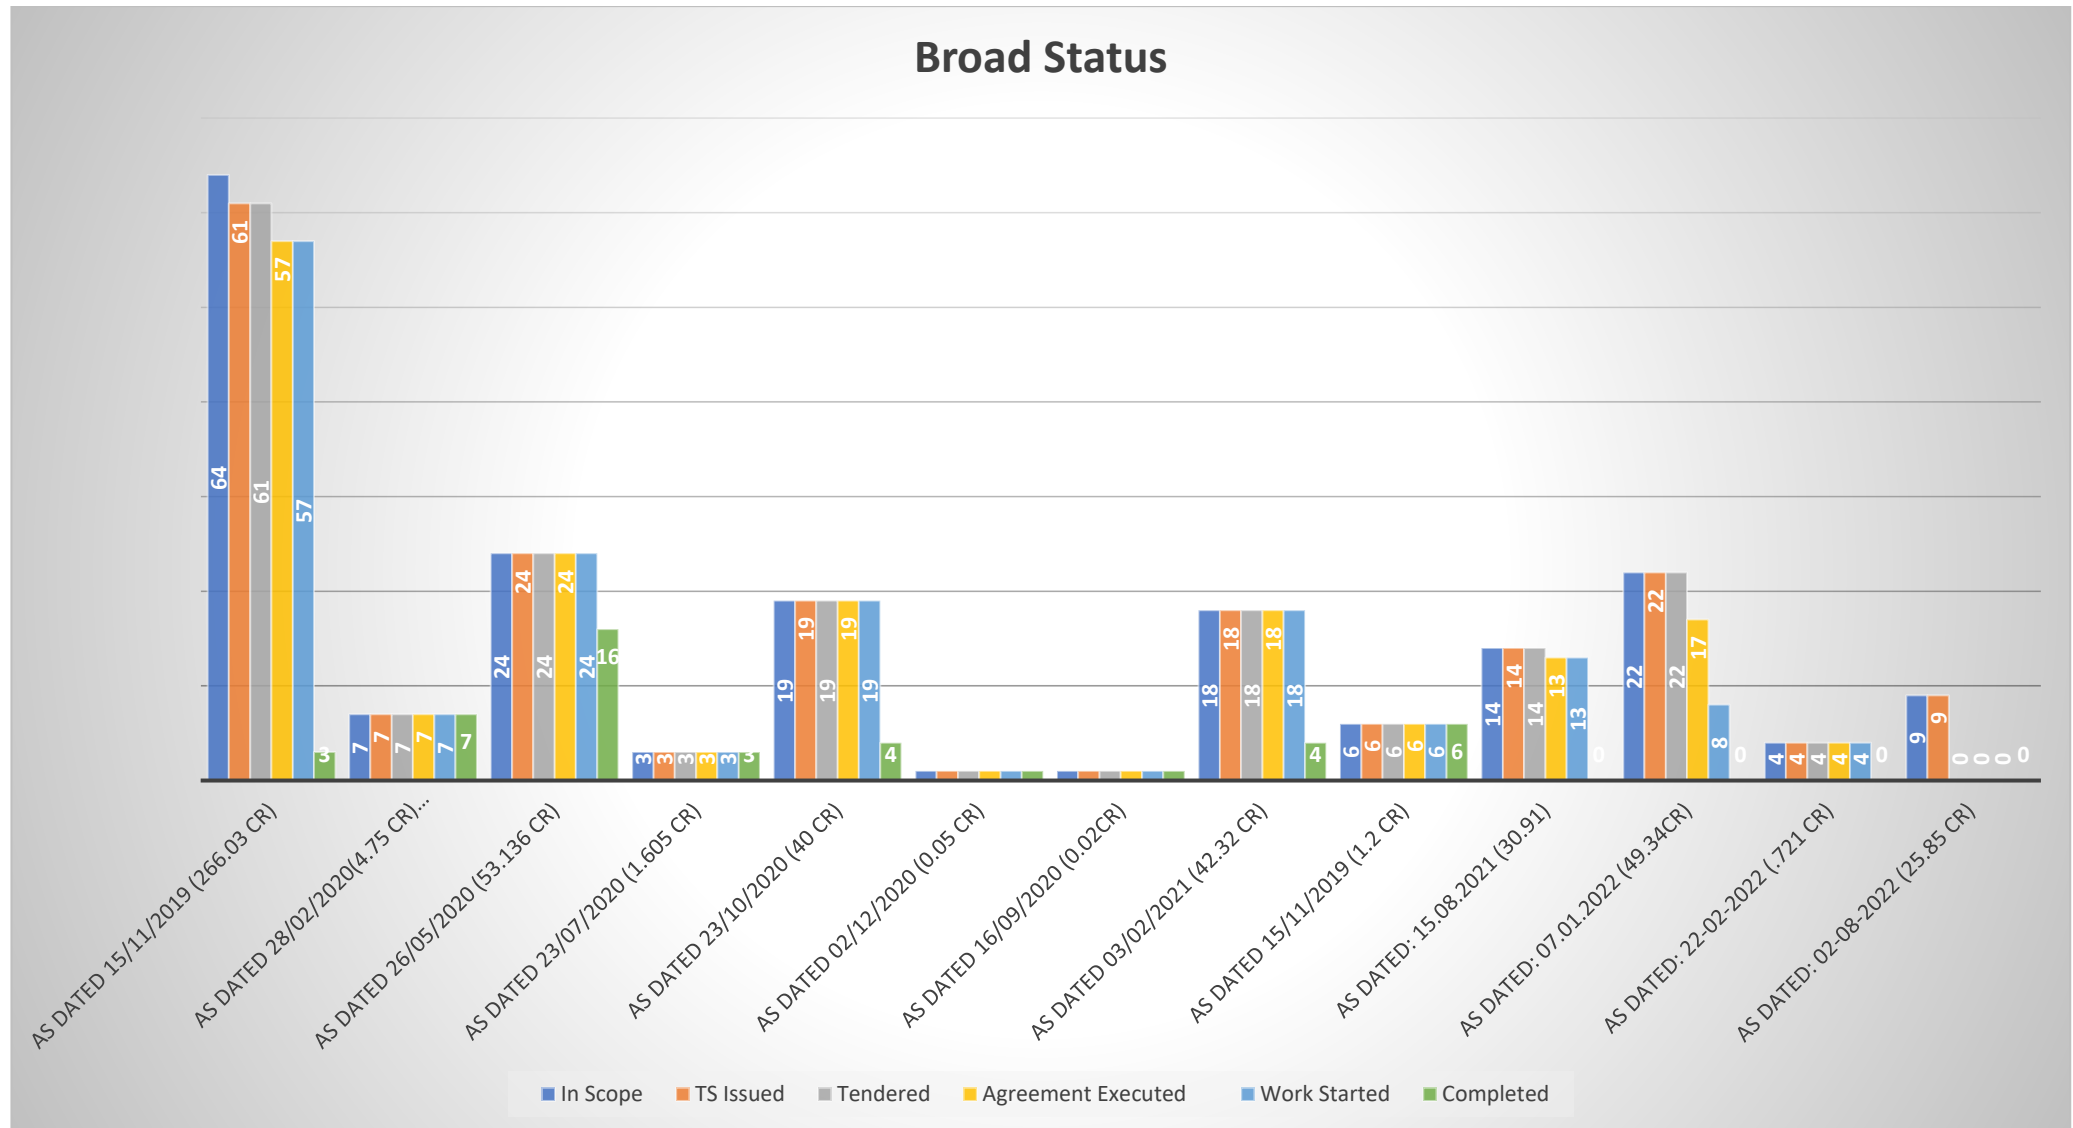

### 3. CONSOLIDATED AS WISE STATUS

| Project Status (AS Wise Consolidated Numbers) |   |  |                    |            |               |            |              |              |                                     |                        |                  |               |                    |                      |                           |
|---|---|--|--------------------|------------|---------------|------------|--------------|--------------|-------------------------------------|------------------------|------------------|---------------|--------------------|----------------------|---------------------------|
| SI No   | AS No   | Description  | AS Amount (Crores) | Total Nos  | To be Dropped | In Scope   | No TS Issued | Nos Tendered | Nos Tender Excess Approval Required | Nos Agreement Executed | Nos Work Started | Nos Completed | Tender Amount (cr) | Agreement Amount(cr) | Total Expenditure (Crore) |
| 1   | GO(Rt) No 485/2019/P&EA dated 15/11/2019,                         | Reconstruction of various LSG roads in DBMT mode in Pathanamthitta, Idukki and Wayanad districts-77 nos.   | 266.3055           | 77         | 13            | 64         | 61           | 61           | 0                                   | 61                     | 61               | 3             | 127.156            | 122.67               | 15.348                    |
| 2   | G.O. (Rt.)No. 115/2020/P&EA, Thiruvananthapuram, Dated 28/02/2020 | Conducting investigation/ data collection of roads identified in 7 districts, AS Issued for 4.75 Crore, details as follows.  | 4.75               | 7          | 0             | 7          | 7            | 7            | 0                                   | 7                      | 7                | 7             | 4.57               | 3.2                  | 1.151                     |
| 3   | G.O. (Rt.) No.224/2020/P&EA, Thiruvananthapuram, Dated 26/05/2020 | Rebuilding LSG Roads in 4 districts viz., Alappuzha, Kottayam, Ernakulam and Thrissur, Total AS Issued for Rs. 53.136 Crore, for 25 roads details as follows                 | 53.136             | 25         | 1             | 24         | 24           | 24           | 0                                   | 24                     | 24               | 16            | 39.89              | 38.84                | 26.123                    |
| 4   | G.O.(Rt)No.1389/2020/ LSGD Dated, Thiruvananthapuram, 23/07/2020  | Consultancy services for design and DPR preparation of flood affected roads in Pathanamthitta, Idukki and Wayanad districts, AS issued for 1.605 Crores, details as follows. | 1.605              | 3          | 0             | 3          | 3            | 3            | 0                                   | 3                      | 3                | 3             | 1.35               | 1.35                 | 0.8667                    |
| 5   | G.O. (Rt.) No.404/2020/P&EA, Thiruvananthapuram, Dated 23/10/2020 | Rebuilding LSG Roads in 5 districts viz., Alappuzha, Kottayam, Ernakulam, Thrissur and Wayanad, AS issued for Rs. 40 Core. Details as follows                                | 40                 | 21         | 2             | 19         | 19           | 19           | 0                                   | 19                     | 19               | 4             | 30.98              | 31.26                | 8.651                     |
| 6   | GO (Rt) No. 62/2021/P&EA , Dated 03/02/2021                       | rebuilding 19 number of LSGD Roads in 6 districts viz., Pathanamthitta, Kottayam, Ernakulam, Alappuzha, Thrissur & Wayana  | 42.32              | 19         | 1             | 18         | 18           | 18           | 0                                   | 18                     | 18               | 4             | 32.27              | 33.17                | 5.662                     |
| 7   | G.O.(Rt)No.2257/2020/LSGD dated 02.12.2020                        | CBR Investigation of Roads in Wayanad  | 0.0546             | 1          | 0             | 1          | 1            | 1            | 0                                   | 1                      | 1                | 1             |                    |                      | 0.05                      |
| 8   | GO(Rt) No 234/2021/LSGD dated 15/11/2019                          | Soil Investigation for Bridges   | 1.2                | 6          | 0             | 6          | 6            | 6            | 0                                   | 6                      | 6                | 6             |                    |                      | 0.33                      |
| 9   | GO(Rt) No 1669/2020/LSGD dated 16.09.2020                         | Topographic Survey for roads in Wayanad  | 0.0246             | 1          | 0             | 1          | 1            | 1            | 0                                   | 1                      | 1                | 1             |                    |                      | 0.02                      |
| 10  | G.O.(Rt)No.348/2021 /P&EA, 15.08.2021                             | rebuilding 14 LSG Roads in 4 districts viz., Alappuzha, Pathanamthitta, Idukki and Wayanad   | 30.91              | 14         | 0             | 14         | 14           | 14           | 0                                   | 14                     | 14               | 0             | 23.36              | 23.51                | 0.5388                    |
| 11  | G.O.(Rt)No.18/2022/ P&EA, 07.01.2022                              | rebuilding 22 number of LSGD Roads in 5 districts viz, Alappuzha, Pathanamthitta, Ernakulam, Idukki and Wayanad  | 49.34              | 22         | 0             | 22         | 22           | 22           | 0                                   | 22                     | 22               | 0             | 37.73              | 35.18                | 0.152                     |
| 12  | GO (Rt) No. 405/2022/LSGD, dt: TVM 22-02-2022                     | Engaging consultants for Designing bridges - 31 Nos  | 0.721              | 4          | 0             | 4          | 4            | 4            | 0                                   | 4                      | 4                | 0             | 0.29               | 0.284                | 0                         |
| 13  | GO(Rt) No. 300/2022/P&EA , dt: 02/08/2022                         | 10 roads   | 25.85(-)           | 10         | 0             | 10         | 10           | 0            | 0                                   | 0                      | 0                | 0             | 0                  | 0                    | 0                         |
|   |   | <b>Totals</b>  | <b>490.3667</b>    | <b>210</b> | <b>17</b>     | <b>193</b> | <b>190</b>   | <b>180</b>   | <b>0</b>                            | <b>180</b>             | <b>180</b>       | <b>45</b>     | <b>297.596</b>     | <b>289.464</b>       | <b>59.1659</b>            |

#### 4. OVERVIEW OF STATUS OF WORKS – DISTRICT WISE

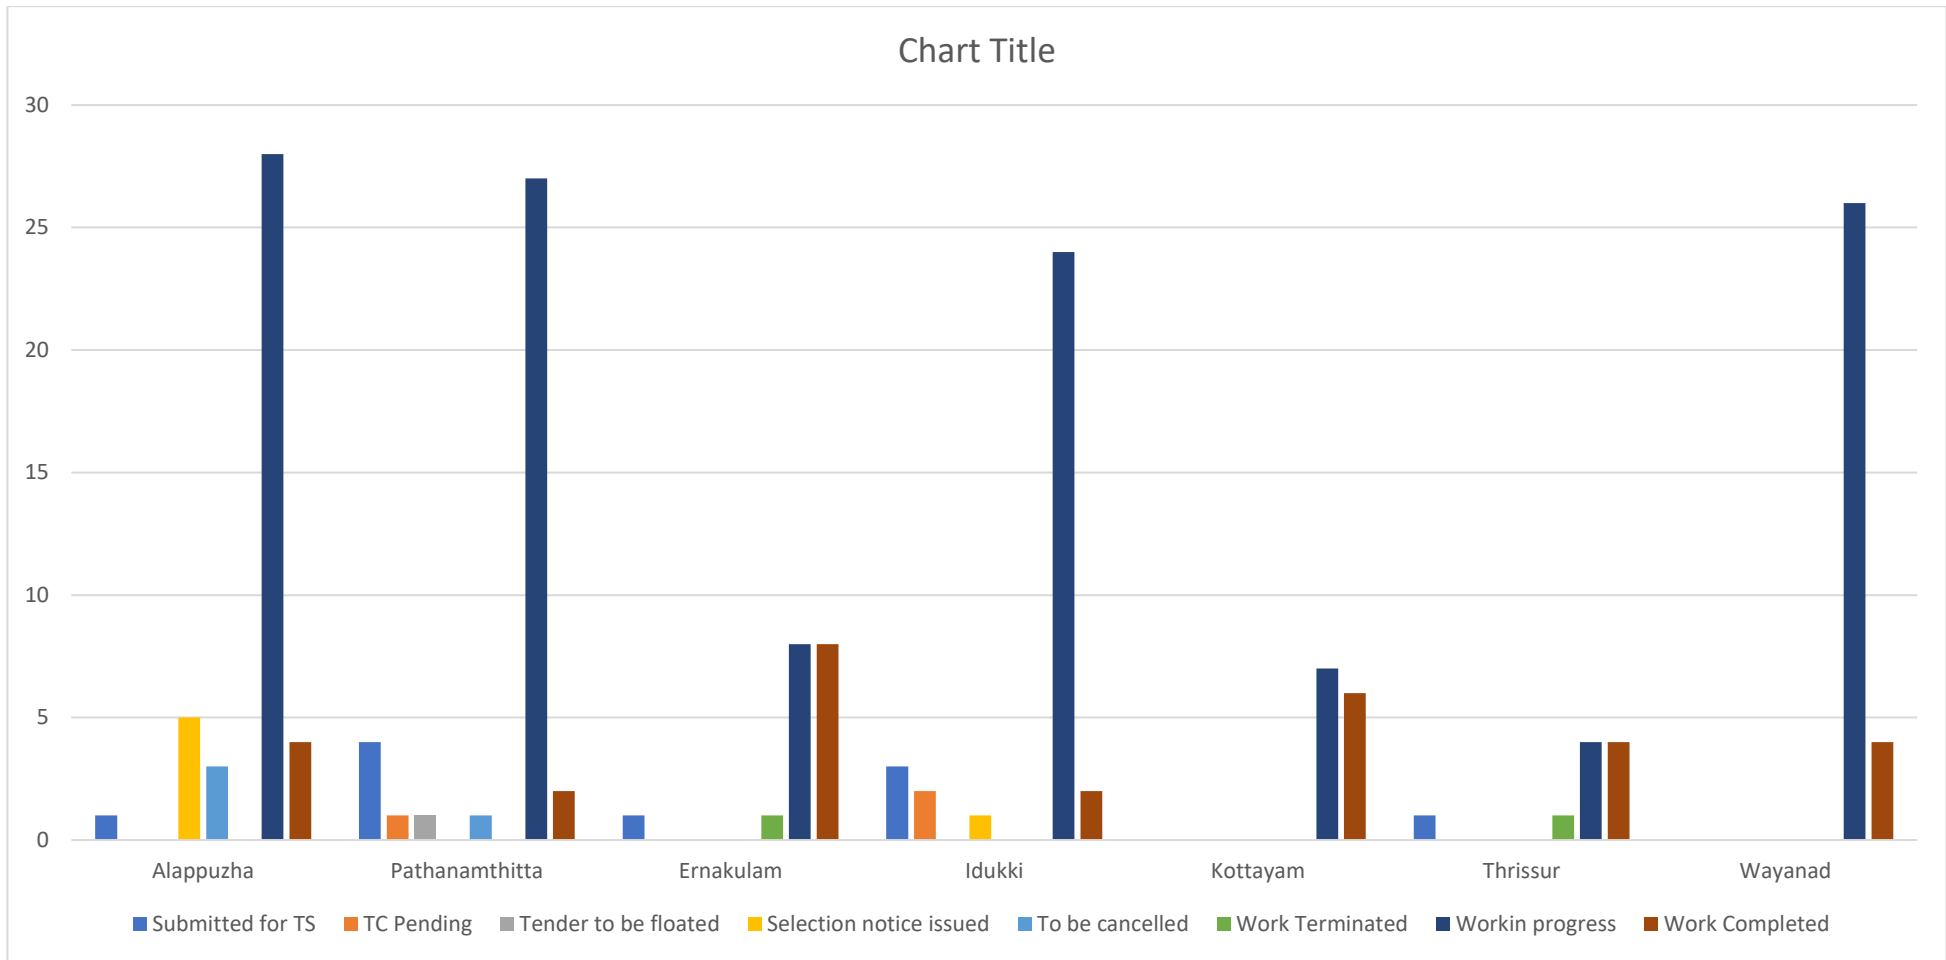

## 5. DISTRICT WISE STATUS OF PROJECTS

| SI No | Description                 | Alappuzha | Pathanamthitta | Ernakulam | Idukki    | Kottayam  | Thrissur  | Wayanad   | Total       |
|-------|-----------------------------|-----------|----------------|-----------|-----------|-----------|-----------|-----------|-------------|
| 1     | Submitted for TS            | 0         | 0              | 0         | 0         | 0         | 0         | 0         | 0           |
| 2     | Technical Committee Pending | 0         | 1              | 0         | 2         | 0         | 0         | 0         | 3           |
| 3     | Tender to be floated        | 1         | 6              | 2         | 3         | 0         | 1         | 0         | 13          |
| 4     | To be cancelled             | 2         | 0              | 0         | 0         | 0         | 0         | 0         | 2           |
| 5     | Work in Progress            | 33        | 27             | 9         | 24        | 5         | 5         | 23        | 127         |
| 6     | Work Completed              | 6         | 3              | 10        | 3         | 9         | 4         | 9         | 44          |
|       | <b>Total</b>                | <b>42</b> | <b>37</b>      | <b>21</b> | <b>32</b> | <b>14</b> | <b>10</b> | <b>32</b> | <b>188*</b> |

{\*5 more design works that cannot be included one single district (Total: 193)}

6. SOME PROJECT PHOTOS



Thadikadavu Vayalodam Road - EKM



Panjam Kavala Road- EKM





Thandilam Manali Kecheri Road - Thrissur



Chakram Colony Road – Wayanad



AC Canal Mankuzhi Road - ALP



Pennukkara Canal Road - ALP



## DETAILED REPORTS OF WORKS

AS WISE

**G.O.(Rt.)No.485/2019/P&EA dated 15-11-2019(266.03cr) Pathanamthitta**

| SI No | Name of Work   | District       | Status             | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|--|----------------|--------------------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Rehabilitation of Adoor Gopalakrishnan Road in Erathu GP in in Pathanamthitta district               | Pathanamthitta | Under Construction | 2.46        | 1.8977            | 1.9534            | 2021-10-27     | 2023-04-30      | 48%              | 0%               |                 |
| 2     | Renovation of CK Road in Kottangal GP in Pathanamthitta district                                     | Pathanamthitta | Under Construction | 2.77        | 1.7836            | 1.8925            | 2021-10-27     | 2023-06-30      | 30%              | 0%               | 0.0025          |
| 3     | Paivazhy Nediakala Road in Pandalam MC in Pathanamthitta district                                    | Pathanamthitta | Under Construction | 3.76        | 2.7723            | 3.0208            | 2021-10-27     | 2023-05-30      | 60%              | 12%              | 0.4331          |
| 4     | Renovation of Chakrasalakadavu Panachimoottil Road in Kuttoor GP in Pathanamthitta district          | Pathanamthitta | Under Construction | 2.77        | 2.094             | 2.2824            | 2021-10-27     | 2023-05-30      | 50%              | 0%               |                 |
| 5     | Improvement of Thannithode Plantation road in Pathanamthitta district                                | Pathanamthitta | Under Construction | 5.27        | 4.0737            | 4.2613            | 2021-10-21     | 2023-03-31      | 70%              | 8%               | 0.4446          |
| 6     | Reconstruction of Banglamkadavu Stadium Valiyakulam Road in Vadasserikkara GP in Pathanamthitta dist | Pathanamthitta | Under Construction | 2.31        | 1.873             | 1.8728            | 2022-03-21     | 2023-06-30      | 15%              | 0%               |                 |
| 7     | Reconstruction of Banglamkadavu Valiyakulam Road in Vadasserikkara GP in Pathanamthitta district     | Pathanamthitta | Under Construction | 2.05        | 1.6814            | 1.6433            | 2022-03-21     | 2023-04-30      | 40%              | 0%               |                 |
| 8     | Chana Kurumpanmoozhy Road in Naranamoozhy GP, Ranni LAC, Pathanamthitta district                     | Pathanamthitta | Under Construction | 2.18        | 1.7904            | 1.7007            | 2022-03-21     | 2023-05-30      | 20%              | 0%               |                 |
| 9     | Madukkamoodu Ayyappa Medical College Road in Vadasserikkara GP, Ranni LAC, Pathanamthitta district   | Pathanamthitta | Under Construction | 1.47        | 1.1821            | 1.0639            | 2021-10-27     | 2023-04-30      | 65%              | 17%              | 0.2455          |

|    |  |                |                    |       |        |        |            |            |     |    |        |
|----|--|----------------|--------------------|-------|--------|--------|------------|------------|-----|----|--------|
| 10 | Rationkadapadi Mulanthanam Road in Perunadu GP, Ranni LAC in Pathanamthitta district                 | Pathanamthitta | Under Construction | 1.4   | 1.0919 | 1.1288 | 2021-12-27 | 2023-07-30 | 20% | 0% |        |
| 11 | Arummoode- Chala Puthenchantha 14th mile Adoor LAC Pallikkal LSGI Pathanamthitta district            | Pathanamthitta | Under Construction | 1.88  | 1.3583 | 1.4787 | 2022-12-27 | 2023-07-30 | 20% | 0% |        |
| 12 | Anthyalankavu Marthomapallipadi Karamvelipadi Road in Naranganam GP, Aranmula LAC, Pathanamthitta di | Pathanamthitta | Under Construction | 1.39  | 1.0759 | 1.1079 | 2022-06-22 | 2023-05-30 | 35% | 0% |        |
| 13 | Kiliyanikkal Thoolikulam Road Ranni LAC Cherukole LSGI in Pathanamthitta district                    | Pathanamthitta | Under Construction | 1.56  | 1.1108 | 1.2585 | 2022-03-21 | 2023-06-30 | 40% | 0% |        |
| 14 | Reconstruction of Parakkavu Valakuzhi Road in Ezhumattur GP in Pathanamthitta District               | Pathanamthitta | Under Construction | 1.97  | 1.4124 | 1.5535 | 2022-03-21 | 2023-04-30 | 50% | 0% |        |
| 15 | Reconstruction of Melepadai Chellakadu Road in Pazhavangadi GP in Pathanamthitta District            | Pathanamthitta | Under Construction | 2.09  | 1.649  | 1.7181 | 2022-03-24 | 2023-07-30 | 25% | 0% |        |
| 16 | Erathodu Ashankuzhy road in Tiruvalla LAC Niranam LSGI Pathanamthitta District                       | Pathanamthitta | Under Construction | 1.96  | 1.5591 | 1.6152 | 2022-04-21 | 2023-07-31 | 35% | 0% |        |
| 17 | Kalarikode Pallana Puthenvelipadi Road in Pathanamthitta district Aranmula LAC Aranmula LSGI         | Pathanamthitta | To be Dropped      | 1.98  | 1.3039 | -      | 0000-00-00 | 0000-00-00 | 0%  | 0% |        |
| 18 | Vattathenpady Nallathupady Road in Pathanamthitta district Aranmula LAC Aranmula LSGI                | Pathanamthitta | Under Construction | 1.13  | 0.7040 | 0.8133 | 2022-10-07 | 2023-04-30 | 35% | 0% | 0.0018 |
| 19 | Poovanmala Panamplackal Road in Pathanamthitta district Ranni LAC Angadi LSGI                        | Pathanamthitta | Tender Process     | 1.21  | 0.7659 | -      | 0000-00-00 | 0000-00-00 | 0%  | 0% |        |
| 20 | Thiruvabharanapatha Road   | Pathanamthitta | AS Received        | 8     |        |        | 0000-00-00 | 0000-00-00 | 0%  | 0% |        |
|    | Total  |                |                    | 49.61 | 31.18  | 30.37  |            |            |     |    | 1.13   |

**G.O.(Rt.)No.485/2019/P&EA dated 15-11-2019(266.03cr) Idukki**

| SI No | Name of Work   | District | Status             | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|--|----------|--------------------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Improvement of Aashramam Pottanpady Road in Arakkulam GP, Idukki LAC, Idukki No.-18                  | Idukki   | Under Construction | 1.63        | 1.3               | 1.1995            | 2021-11-06     | 2022-10-06      | 0%               | 0%               |                 |
| 2     | Improvement of Adivaram-Ottalalpady city road in Rajakkad GP, Udumbanchola LAC, Idukki No:6          | Idukki   | Under Construction | 2.37        | 2.2782            | 2.2511            | 2021-11-06     | 2023-03-31      | 70%              | 15%              | 0.3564          |
| 3     | Improvement of Ambalappara-Kadaplackal Road in Upputhara GP, Peermade LAC, Idukki district-08        | Idukki   | Under Construction | 1           | 0.8091            | 0.6709            | 2021-10-27     | 2023-03-31      | 55%              | 0%               | 0.0045          |
| 4     | Improvement of Ellapalli tottam bhagom road Arakkulam GP, Idukki LAC, Idukki No. 20                  | Idukki   | Under Construction | 1.93        | 1.556             | 1.308             | 2021-10-27     | 2022-12-27      | 50%              | 27%              | 0.5207          |
| 5     | Improvement of Ellapally Chellikal Road in Arakkulam GP, Idukki LAC, Idukki No:19                    | Idukki   | Under Construction | 4.33        | 3.4625            | 3.1298            | 2021-10-27     | 2022-12-27      | 15%              | 0%               |                 |
| 6     | Improvement of Pazhaya Kochira road in Vandenmedu GP, Udumbanchola LAC, Idukki-No:26                 | Idukki   | Under Construction | 1.61        | 1.3136            | 1.2553            | 2021-10-27     | 2023-03-31      | 80%              | 35%              | 0.5598          |
| 7     | Improvement of Vimalagiri-Enikuthu Road in Mariyapuram GP, Idukki LAC, Idukki No:29                  | Idukki   | Under Construction | 2.5         | 2.027             | 1.8182            | 2021-10-27     | 2023-03-31      | 75%              | 22%              | 0.5543          |
| 8     | Improvement of Anachal Thokkupara- Acherikunnu Asramam road in Vellathooval GP, Devikulam LAC, Idukk | Idukki   | Under Construction | 2.11        | 1.7144            | 1.5873            | 2021-11-26     | 2023-03-26      | 45%              | 0%               | 0.0048          |
| 9     | Improvement of Murikkumthotti-Mathekkal padi Shallyil Road in Rajakumari GP, Udumbanchola LAC, Idukk | Idukki   | Under Construction | 1.22        | 0.9643            | 0.8645            | 2021-11-26     | 2023-03-31      | 35%              | 0%               | 0.0026          |

|    |  |        |                    |        |        |        |            |            |     |     |        |
|----|--|--------|--------------------|--------|--------|--------|------------|------------|-----|-----|--------|
| 10 | Improvement of Kattekkanam-Chelamoodu Road in Idukki-25, Karunapuram GP, Udumbanchola LAC            | Idukki | Under Construction | 0.925  | 0.685  | 0.737  | 2021-12-27 | 2023-05-30 | 6%  | 0%  |        |
| 11 | Improvement of Idinjamaal companypadi road Udumbanchola LAC Erattayar LSGI Idukki district           | Idukki | Under Construction | 7.245  | 5.1368 | 5.5859 | 2021-12-27 | 2023-03-31 | 80% | 36% | 2.6426 |
| 12 | Improvement of Perumbankuthu 6th mile road in Mankulam GP, Devikulam LAC, Idukki No:9                | Idukki | Under Construction | 4.12   | 2.9094 | 3.1899 | 2021-12-29 | 2023-12-31 | 25% | 1%  | 0.0344 |
| 13 | Improvement of Kurushupallipadi thannikandam Painavu road in Vazhathope GP, Idukki LAC, Idukki distr | Idukki | Under Construction | 3.3175 | 2.3698 | 2.6029 | 2021-12-29 | 2023-12-31 | 20% | 0%  |        |
| 14 | Improvement of Surianelly-Gundumala Road in Chinnakkanal GP, Devikulam LAC, Idukki District-12       | Idukki | Under Construction | 2.0475 | 1.4479 | 1.5891 | 2021-12-27 | 2023-12-31 | 6%  | 0%  |        |
| 15 | Improvement of Panachikuzhi Road in Rajakkad GP, Udumbanchola LAC, Idukki District                   | Idukki | Under Construction | 4.42   | 3.3761 | 3.2497 | 2021-12-29 | 2023-03-31 | 75% | 7%  | 0.2892 |
| 16 | Improvement of Padicup Plakkayam Kuttamudi Tribal colony road in Adimaly GP Devikulam LAC Idukki 05  | Idukki | Under Construction | 5.06   | 4.0507 | 3.4994 | 2022-02-11 | 2023-05-30 | 15% | 0%  |        |
| 17 | Improvement of Perikkankaval Kollamkulambadi Kaikavala Road in Vathikudy GP Idukki LAC idukki 27     | Idukki | Under Construction | 2.06   | 1.709  | 1.5678 | 2022-02-09 | 2023-03-31 | 70% | 28% | 0.5724 |
| 18 | Improvement of Puthed Anoorthode Footbridge Road in Arakkulam GP, Idukki LAC in Idukki               | Idukki | Under Construction | 3.83   | 2.9954 | 2.9012 | 2022-03-24 | 2023-02-24 | 6%  | 0%  |        |

|    |  |        |                                   |               |        |        |            |            |     |    |      |
|----|--|--------|-----------------------------------|---------------|--------|--------|------------|------------|-----|----|------|
| 19 | Balagram Anyarthulu Road<br>Udumbanchola LAC<br>Pampadumpara LSGI Idukki<br>district                   | Idukki | Under<br>Construction             | 7.63557<br>22 | 5.8442 | 5.9702 | 0000-00-00 | 2023-12-31 | 10% | 0% |      |
| 20 | Naalumukku -Tunnel site road in<br>Udumbanchola LAC Erattayar<br>LSGI Idukki District                  | Idukki | Under<br>Construction             | 2.2615        | 1.6137 | 1.7247 | 2022-04-21 | 2023-05-30 | 40% | 0% |      |
| 21 | Improvement of Pallikudi city<br>Mangathupalam Road in<br>Vathikudy GP, Idukki LAC, Idukki<br>District | Idukki | Under<br>Construction             | 2.7           | 2.1475 | 1.9673 | 2022-04-26 | 2023-12-31 | 10% | 0% |      |
| 22 | 50th Mile Kallakuttykudi<br>Mankulam Road  | Idukki | Technical<br>Committee<br>Pending | 8             |        |        | 0000-00-00 | 0000-00-00 | 0%  | 0% |      |
| 23 | Mangathotti Kanakapuzha NR<br>City Road  | Idukki | Technical<br>Committee<br>Pending | 8             |        |        | 0000-00-00 | 0000-00-00 | 0%  | 0% |      |
|    | Total  |        |                                   | 80.32         | 49.71  | 48.67  |            |            |     |    | 5.54 |



**G.O.(Rt.)No.485/2019/P&EA dated 15-11-2019(266.03cr) Wayanad**

| Sl No | Name of Work   | District | Status             | AS Amt.(cr)   | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|--|----------|--------------------|---------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Improvement of Cheriyaankolli - Kalluvettumthazhe in Padinjarethara GP in Kalpetta LAC Wayanad-09    | Wayanad  | Under Construction | 1.44          | 1.09              | 1.0591            | 2021-11-06     | 2022-12-06      | 16%              | 0%               |                 |
| 2     | Improvement of Ediyamvayal - Pinangodu road in Pozhuthana GP in Kalpetta LAC Wayanad 04              | Wayanad  | Under Construction | 2.22          | 1.6774            | 1.5423            | 2021-06-22     | 2023-01-31      | 90%              | 0%               |                 |
| 3     | Improvement of Erumatherivu - Choottakadavu road in Mananthavdy GP in Mananthavady LAC Wayanad-13    | Wayanad  | Under Construction | 2.61277<br>68 | 1.7896            | 1.9682            | 2022-03-21     | 2023-01-21      | 10%              | 0%               |                 |
| 4     | Improvement of Karlad - Manjoora road in Thariyode GP in Kalpetta LAC Waynad-05                      | Wayanad  | Under Construction | 1.89          | 1.4417            | 1.3084            | 2021-10-27     | 2023-03-27      | 38%              | 0%               | 0.0069          |
| 5     | Improvement of Kuppadithara -Millu mukku kurumani road in Padinjarethara GP in Kalpetta LAC Waynad-0 | Wayanad  | Completed          | 1.45          | 1.10              | 1.10              | 2021-10-27     | 2022-06-27      | 100%             | 54%              | 0.7868          |
| 6     | Improvement of Kottathara - Kakkanchal Thekkumthara Road in Kottathara GP in Kalpetta LAC - Waynad-0 | Wayanad  | Under Construction | 2.74          | 2.2526            | 2.2526            | 2021-10-27     | 2022-12-27      | 33%              | 0%               |                 |
| 7     | Improvement of Varayad - Thekkumpadi Road Muttill GP in Kalpetta LAC Waynad-02                       | Wayanad  | Under Construction | 1.87          | 1.53              | 1.50              | 2021-02-26     | 2022-08-26      | 48%              | 3%               | 0.0624          |
| 8     | Improvement of Chundel - Chundel estate - Pappala Anoth Road in Chundel GP in Kalpetta LAC- Wayanad- | Wayanad  | Under Construction | 5.661         | 4.3236            | 3.8668            | 2021-06-22     | 2023-02-25      | 78%              | 48%              | 2.7112          |
| 9     | Improvement of MH Nagar - Cholapuram road in Vengappally GP in Kalpetta LAC Waynad-06                | Wayanad  | Under Construction | 2.4           | 1.8558            | 1.6335            | 2021-10-27     | 2023-01-31      | 90%              | 0%               |                 |

|    |   |         |                    |      |        |        |            |            |      |     |        |
|----|---|---------|--------------------|------|--------|--------|------------|------------|------|-----|--------|
| 10 | Improvement of Varayal - Melevarayal Road in Thanival GP in Mananthavady LAC Waynad-18            | Wayanad | Under Construction | 1.34 | 1.0106 | 0.979  | 2021-08-02 | 2022-12-02 | 33%  | 5%  | 0.0723 |
| 11 | Improvement of Kattimoola Aroola Kolathada Road in Thavinjal GP in Mananthavady LAC Wayanad 19    | Wayanad | Completed          | 2.79 | 2.1266 | 2.0662 | 2021-11-06 | 2022-11-06 | 100% | 74% | 2.0604 |
| 12 | Improvement of Korome Karimbil Road in Thondernad GP of Mananthavdy LAC Wayanad 21                | Wayanad | Under Construction | 5.6  | 4.4587 | 4.2993 | 2021-11-06 | 2022-10-06 | 6%   | 0%  |        |
| 13 | Improvement of Orappu Evanarikulam Kattimoola Road in Mananthavadi LAC Thanival Wayanad 20        | Wayanad | Completed          | 3.45 | 2.6093 | 2.5173 | 2021-11-06 | 2022-10-06 | 100% | 65% | 2.2442 |
| 14 | Improvement of Puthiyedam Makkimala Road in Thavinjal GP in Mananthavady LAC of Wayanad 16        | Wayanad | Under Construction | 3.89 | 2.902  | 2.813  | 2021-11-06 | 2022-12-06 | 33%  | 0%  |        |
| 15 | Improvement of 44th mile Makkimala Road in Mananthavady LAC, Thanival LSGI, Wayanad 17            | Wayanad | Under Construction | 3.09 | 2.39   | 2.3545 | 2021-11-17 | 2022-12-17 | 33%  | 0%  |        |
| 16 | Improvement of Panamaram Keenjukadavu Palakunnu Road Mananthavady LAC, Panamaram LSGI, Wayanad 01 | Wayanad | Under Construction | 6.22 | 4.8684 | 4.7356 | 2021-11-17 | 2022-12-17 | 16%  | 6%  | 0.38   |
| 17 | Improvement of Pilakavu Pancharakolli Road in Mananthavady LAC, Mananthavady LSGI, Wayanad 15     | Wayanad | Under Construction | 3.09 | 2.3803 | 2.3223 | 2021-11-17 | 2023-01-31 | 90%  | 0%  |        |

|       |   |         |                    |               |         |        |            |            |     |     |        |
|-------|---|---------|--------------------|---------------|---------|--------|------------|------------|-----|-----|--------|
| 18    | Improvement of Kollikandam Kunneri Nelom Road in Thondernadu GP in Mananthavady LAC in Wayanad 22 | Wayanad | Under Construction | 1.1275        | 0.7727  | 0.8213 | 2021-12-27 | 2022-10-06 | 6%  | 0%  |        |
| 19    | Improvement of Valliurkavu Varadimoola Road in Mananthavady GP Mananthavady LAC in Wayanad 10     | Wayanad | Under Construction | 1.45          | 1.1336  | 0.9963 | 2022-02-17 | 2022-12-17 | 13% | 25% | 0.3555 |
| 20    | Improvement of Vilanilam Pilakavu road in Mananthavdy GP Mananthavady LAC Wayanad 14              | Wayanad | Under Construction | 3.89          | 3.0935  | 2.787  | 2022-02-17 | 2022-12-17 | 58% | 0%  |        |
| 21    | Improvement of Thannikkal Payyampally Road in Mananthavady LAC in Wayanad 12                      | Wayanad | Under Construction | 1.98615<br>54 | 1.46058 | 1.5557 | 2022-03-26 | 2023-02-26 | 0%  | 0%  |        |
| Total |   |         |                    | 60.21         | 46.27   | 44.48  |            |            |     |     | 8.68   |

**G.O.(Rt.)No.115/2020/P&EA dated 28-02-2020(4.75cr)**

| Sl No | Name of Work   | District       | Status    | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|--|----------------|-----------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Investigation/ data collection - Pathanamthitta District | Pathanamthitta | Completed | 0.4152      | 0.4152            | 0.2768            | 2020-09-04     | 2022-08-30      | 100%             | 13%              | 0.0550          |
| 2     | Investigation/ data collection - Alappuzha District      | Alappuzha      | Completed | 0.8174      | 0.8174            | 0.5449            | 2020-09-04     | 2022-08-30      | 100%             | 22%              | 0.1780          |
| 3     | Investigation/ data collection - Kottayam District       | Kottayam       | Completed | 0.1208      | 0.1208            | 0.0951            | 2020-08-27     | 2022-08-30      | 100%             | 13%              | 0.0156          |
| 4     | Investigation/ data collection -Idukki District          | Idukki         | Completed | 1.9027      | 1.9027            | 1.3148            | 2020-08-27     | 2022-08-30      | 100%             | 33%              | 0.6196          |
| 5     | Investigation/ data collection - Ernakulam District      | Ernakulam      | Completed | 0.2057      | 0.2057            | 0.1526            | 2020-08-27     | 2022-08-30      | 100%             | 19%              | 0.0396          |
| 6     | Investigation/ data collection - Thrissur District       | Thrissur       | Completed | 0.3854      | 0.3854            | 0.2802            | 2020-08-27     | 2022-08-30      | 100%             | 13%              | 0.0493          |
| 7     | Investigation/ data collection - Wayanad District        | Wayanad        | Completed | 0.7243      | 0.7243            | 0.5436            | 2020-08-27     | 2022-08-30      | 100%             | 27%              | 0.1943          |
|       | Total  |                |           | 4.57        | 4.57              | 3.21              |                |                 |                  |                  | 1.15            |

**G.O.(Rt.)No.224/2020/P&EA dated 26-05-2020(53.136cr)**

| SI No | Name of Work  | District  | Status             | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|---|-----------|--------------------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Up gradation of Ennakkad Alumoodu Elanjimel Road in Budhanoor GP in Alappuzha                     | Alappuzha | Under Construction | 6.39        | 4.9438            | 4.8004            | 2020-10-09     | 2023-01-31      | 50%              | 1%               | 0.0569          |
| 2     | Rehabilitation of Thandilam Manali Kecheri Road in Thrissur                                       | Thrissur  | Completed          | 5           | 3.6692            | 3.6479            | 2020-09-23     | 2022-11-18      | 100%             | 60%              | 3.0039          |
| 3     | Up gradation of Budhanoor Ponnathara Road in Alappuzha  | Alappuzha | Under Construction | 2.91        | 2.37              | 2.30              | 2020-10-09     | 2023-01-31      | 40%              | 0%               |                 |
| 4     | Renovation of Kulikkanpalam Shappupadi Road in Alappuzha  | Alappuzha | Completed          | 2.78        | 2.06              | 1.8871            | 2020-09-22     | 2022-09-30      | 100%             | 46%              | 1.2732          |
| 5     | Reconstruction of AV Mukku Sharangakkavu Road in Alappuzha  | Alappuzha | Completed          | 2.82        | 2.0495            | 1.873             | 2020-11-06     | 2022-09-30      | 100%             | 54%              | 1.5152          |
| 6     | Reconstruction of Pennukara canal Jn Nettuvaramcode road in Alappuzha                             | Alappuzha | Completed          | 2.99        | 1.8603            | 1.6985            | 2020-09-04     | 2022-04-20      | 100%             | 66%              | 1.9591          |
| 7     | Up gradation of Pannikuzhy Kavumthazham Road in Ernakulam   | Ernakulam | Completed          | 1.81        | 1.42              | 1.25              | 2020-09-18     | 2022-02-10      | 100%             | 77%              | 1.4002          |
| 8     | Improvement of Girideepam Kadathukadavu Road in Kottayam District                                 | Kottayam  | Completed          | 1.75        | 1.2935            | 1.2392            | 2020-10-05     | 2022-07-15      | 100%             | 68%              | 1.1936          |
| 9     | Rehabilitation of Pavamkulangara Kannankulangara Road in Thrippunithura Municipality in Ernakulam | Ernakulam | Under Construction | 1.32        | 0.97              | 0.95              | 2020-10-05     | 2022-12-31      | 93%              | 41%              | 0.5383          |
| 10    | Upgradation of Vayalodam Thadikkadavu Road in Ernakulam District                                  | Ernakulam | Completed          | 1.38        | 0.914             | 0.9138            | 2020-10-28     | 2022-08-30      | 100%             | 72%              | 0.9881          |
| 11    | Renovation of Valavazhi Road in Angamaly Municipality in Ernakulam District                       | Ernakulam | Under Construction | 0.87        | 0.658             | 0.648             | 2020-10-05     | 2022-08-30      | 0%               | 0%               |                 |
| 12    | Rehabilitation of Paduavathil Police Station Road in Kadungalloor GP in Ernakulam                 | Ernakulam | Under Construction | 0.66        | 0.5006            | 0.4947            | 2020-10-05     | 2022-11-30      | 0%               | 0%               |                 |

|    |   |           |                    |         |        |        |            |            |      |     |        |
|----|---|-----------|--------------------|---------|--------|--------|------------|------------|------|-----|--------|
| 13 | Up gradation of Kadungalloor Masjid road in Ernakulam   | Ernakulam | Completed          | 0.72    | 0.481  | 0.4809 | 2020-09-28 | 2022-03-30 | 100% | 65% | 0.4686 |
| 14 | Improvement of Chittanda Padinjattumuri Road in Thrissur                                      | Thrissur  | Completed          | 6.72    | 5.4    | 5.09   | 2020-09-23 | 2022-11-28 | 100% | 55% | 3.6973 |
| 15 | Improvement of Pathinanchilkadavu Illikkal road in Kottayam Municipality in Kottayam District | Kottayam  | Under Construction | 4       | 2.9446 | 2.9301 | 2020-10-28 | 2022-10-30 | 60%  | 58% | 2.3141 |
| 16 | Improvement of Kunnumpuram Mahilasamajam Road in Thiruvappu GP in Kottayam District           | Kottayam  | Completed          | 1.84    | 1.3434 | 1.3247 | 2020-10-13 | 2022-03-30 | 100% | 74% | 1.3544 |
| 17 | Up gradation of Anicadu Pravidakunnu Road in Ernakulam  | Ernakulam | Under Construction | 1.3     | 1.0883 | 1.075  | 2020-10-05 | 2022-06-30 | 93%  | 81% | 1.0517 |
| 18 | Construction of Udumpuzha Chempassery Road in Ernakulam                                       | Ernakulam | Under Construction | 1.03    | 0.7666 | 0.739  | 2020-10-24 | 2023-03-30 | 13%  | 0%  |        |
| 19 | Renovation of Okkal Juma masjid Road in Okkal GP in Ernakulam                                 | Ernakulam | Completed          | 0.166   | 0.1409 | 0.1318 | 2020-11-04 | 2022-03-31 | 100% | 89% | 0.1474 |
| 20 | Reconstruction of BJP Kadavu Road in Ernakulam District                                       | Ernakulam | Completed          | 0.12    | 0.10   | 0.0928 | 2020-09-29 | 2022-03-31 | 100% | 82% | 0.0982 |
| 21 | Rehabilitation of St.Mary's Swaraj road in Kumbalangi G P in Ernakulam                        | Ernakulam | Completed          | 0.53136 | 0.501  | 0.501  | 2020-10-05 | 2022-05-15 | 100% | 51% | 0.2696 |
| 22 | Renovation of Kavanathinkara Manchira Road in Aymanam GP in Kottayam District                 | Kottayam  | Completed          | 0.93    | 0.6712 | 0.6501 | 2020-10-28 | 2022-08-08 | 100% | 53% | 0.4917 |
| 23 | Renovation of TV Puram Theeradesa Road in TV Puram GP in Kottayam District                    | Kottayam  | Completed          | 3.5     | 2.9401 | 3.2337 | 2021-01-20 | 2022-10-30 | 100% | 93% | 3.2682 |
| 24 | Malakunnam Kannanthrappadi road in Kurichy GP in Kottayam District                            | Kottayam  | Completed          | 1.19    | 0.8096 | 0.8898 | 2021-01-20 | 2022-02-15 | 100% | 87% | 1.034  |
|    | Total   |           |                    | 52.73   | 39.9   | 38.84  |            |            |      |     | 26.12  |

**G.O.(Rt.)No.1389/2020/LSGD dated 23-07-2020(1.605cr)**

| Sl No | Name of Work  | District       | Status    | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|---|----------------|-----------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Design and DPR Preparation of 218km roads in Idukki         | Idukki         | Completed | 0.6480      | 0.6480            | 0.6480            | 2020-10-21     | 2022-08-30      | 100%             | 50%              | 0.3239          |
| 2     | Design and DPR Preparation of 218km roads in Pathanamthitta | Pathanamthitta | Completed | 0.3074      | 0.3074            | 0.3074            | 2020-10-21     | 2022-08-30      | 100%             | 58%              | 0.1781          |
| 3     | Design and DPR Preparation of 218km roads in Wayanad        | Wayanad        | Completed | 0.3979      | 0.3979            | 0.3979            | 2020-10-21     | 2022-08-30      | 100%             | 92%              | 0.3647          |
|       | Total   |                |           | 1.35        | 1.35              | 1.35              |                |                 |                  |                  | 0.87            |

**G.O.(Rt.)No.404/2020/P&EA dated 23-10-2020(40cr)**

| SI No | Name of Work   | District  | Status             | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|--|-----------|--------------------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Olassa - Cherthalli Road in Kottayam   | Kottayam  | Under Construction | 1.21        | 1.0104            | 0.9829            | 2021-02-18     | 2023-02-18      | 35%              | 16%              | 0.1986          |
| 2     | Kambanikadavu Pattarmadom Road in Kottayam   | Kottayam  | Completed          | 1.14        | 0.9258            | 0.8885            | 2021-05-04     | 0000-00-00      | 100%             | 78%              | 0.8857          |
| 3     | Chakram colony road in Wayanad   | Wayanad   | Completed          | 0.93        | 0.758             | 0.6821            | 2021-02-16     | 2022-01-24      | 100%             | 65%              | 0.6089          |
| 4     | Maravayal Chathothu road in Wayanad  | Wayanad   | Under Construction | 1.6         | 1.335             | 1.2127            | 2021-02-16     | 2023-03-31      | 35%              | 0%               |                 |
| 5     | Kanjikkal Mukku Ganam theatre road in in Bharanikavu GP, Kayamkulam LAC, Alappuzha District          | Alappuzha | Under Construction | 2.14        | 1.6332            | 1.6294            | 2021-05-04     | 2023-03-31      | 50%              | 24%              | 0.5048          |
| 6     | Reconstruction of AC Canal to Mankuzhy Road in Ramankary GP, Kuttanad LAC, Alappuzha District        | Alappuzha | Under Construction | 1.15        | 0.9364            | 1.0205            | 2021-08-26     | 2023-03-31      | 70%              | 18%              | 0.2118          |
| 7     | Chirakkarapadi - Chetalapuncha, Pmattipuncha, Pazhamchira Road in Venmani and Cheriyanad GP, Chengan | Alappuzha | Under Construction | 3.48        | 2.8405            | 2.6804            | 2021-05-04     | 2023-03-31      | 50%              | 0%               | 0.0043          |
| 8     | Reconstruction of Manathukadu Puthuveedu Road and Protection in Chambakulam, Kuttanad LAC, Alappuzha | Alappuzha | Under Construction | 2           | 1.6692            | 1.7855            | 2021-08-26     | 2023-04-30      | 50%              | 20%              | 0.4001          |
| 9     | Reconstruction of Madathilkadavu Mahilasamajam Kandathilpalli Road in Thiruvapp GP, Ettumanoor LAC   | Kottayam  | Under Construction | 1.45        | 1.2218            | 1.3046            | 2021-08-26     | 2023-01-26      | 6%               | 0%               |                 |
| 10    | Cheepunkal - Malikayal Chira Road in Aymanam GP, Ettumanoor LAC, Kottayam District                   | Kottayam  | Under Construction | 1.48        | 1.2318            | 1.2195            | 2021-02-22     | 2022-12-22      | 40%              | 0%               |                 |



|    |  |           |                    |       |        |        |            |            |      |     |        |
|----|--|-----------|--------------------|-------|--------|--------|------------|------------|------|-----|--------|
| 11 | Panjamkavala road ward-18 in Chendamangalam GP, North Paravoor District, Ernakulam District. | Ernakulam | Completed          | 1.34  | 1.0426 | 0.997  | 2021-05-04 | 2022-03-01 | 100% | 74% | 0.9923 |
| 12 | Chillukarankunnu road in Punnayurkulam GP, Guruvayoor LAC, Thrissur District.                | Thrissur  | Under Construction | 0.96  | 0.7093 | 0.6754 | 2021-07-28 | 2023-02-15 | 10%  | 17% | 0.163  |
| 13 | Kuranchery Nayarangadi road Kallampara colony in Thrissur                                    | Thrissur  | Under Construction | 12.5  | 9.8568 | 9.8285 | 2021-05-04 | 2023-03-31 | 60%  | 31% | 3.8779 |
| 14 | Reconstruction of LPS Mukkam Kollori Road in Chempu GP, Vaikom LAC, Kottayam district        | Kottayam  | Under Construction | 0.52  | 0.4275 | 0.4683 | 2021-11-06 | 2022-11-06 | 5%   | 0%  |        |
| 15 | Harbour Road to Manaladi Jetty Road in Ramankary GP, Kuttanad LAC, Alappuzha district        | Alappuzha | Under Construction | 1.24  | 1.0376 | 1.141  | 2021-11-06 | 2023-02-06 | 30%  | 0%  |        |
| 16 | Improvement of Karoorchira Anjalangadi Road in Thrissur district                             | Thrissur  | Under Construction | 1.95  | 1.5563 | 1.6963 | 2021-11-06 | 2023-03-31 | 35%  | 3%  | 0.05   |
| 17 | Rehabilitation of Paris Road in Kandanassery GP in Thrissur district                         | Thrissur  | Under Construction | 1.7   | 1.3425 | 1.4642 | 2021-11-06 | 2023-03-31 | 30%  | 3%  | 0.053  |
| 18 | Construction of Musiris Puzhayoram Road ward 4 in Chendamangalam GP in Ernakulam             | Ernakulam | Under Construction | 1     | 0.8399 | 0.9156 | 2021-10-27 | 2022-11-30 | 6%   | 0%  |        |
| 19 | Improvement of Puthiyakavu Pozhankavu Road in Thrissur                                       | Thrissur  | Completed          | 0.75  | 0.6129 | 0.6734 | 2021-10-27 | 2022-09-05 | 100% | 93% | 0.7011 |
|    | Total  |           |                    | 38.54 | 30.99  | 31.27  |            |            |      |     | 8.65   |

**G.O.(Rt.)No.62/2021/P&EA dated 03-02-2021(42.32cr)**

| Sl No | Name of Work   | District       | Status             | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|--|----------------|--------------------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Renovation of Kottomonpara Melekottomonpara Pandyanpara Road in Seethathode GP in Pathanamthitta dis | Pathanamthitta | Under Construction | 2.48        | 2.0038            | 1.9291            | 2021-08-02     | 2023-03-31      | 60%              | 14%              | 0.3468          |
| 2     | Improvement of Edatod Palli Basilica Road in Angamaly Municipality in Ernakulam district             | Ernakulam      | Completed          | 0.52        | 0.4116            | 0.4039            | 2021-07-23     | 2022-05-30      | 100%             | 88%              | 0.4554          |
| 3     | Improvement of Thazhe Arappetta Mankunnu Road in Moopainadu GP in Kalpetta LAC in Wayanad district   | Wayanad        | Under Construction | 4.2         | 3.274             | 3.0978            | 2021-08-02     | 2023-03-31      | 33%              | 2%               | 0.0999          |
| 4     | Rehabilitation of Thazhathangadi -Thanitheruvu Road in Pulpally GP in Wayanad                        | Wayanad        | Completed          | 1.2         | 0.9441            | 0.9191            | 2021-08-02     | 2022-07-15      | 100%             | 82%              | 0.9858          |
| 5     | Reconstruction of PWD Road to Arackalchira and Protection Wall in Chambakulam GP in Alappuzha distri | Alappuzha      | Under Construction | 1.22        | 1.0262            | 1.025             | 2021-08-26     | 2023-04-30      | 60%              | 41%              | 0.5055          |
| 6     | Reconstruction of Govt. HS Kochalivettam Road in Kumarakom GP in Kottayam                            | Kottayam       | Completed          | 0.28        | 0.2259            | 0.2482            | 2021-10-18     | 2022-12-31      | 100%             | 0%               |                 |
| 7     | Upgradation of Madathekkathil Chalukara Road in Alappuzha  | Alappuzha      | Completed          | 0.27        | 0.2138            | 0.2316            | 2021-10-27     | 2022-09-30      | 100%             | 0%               |                 |
| 8     | Rehabilitation of Mithrapuzha Vayanasalapadi Vendoorpadi in Chenganoor municipality in Alappuzha     | Alappuzha      | Under Construction | 3.32        | 2.6043            | 2.8365            | 2021-10-27     | 2022-09-30      | 55%              | 55%              | 1.8111          |
| 9     | Upgradation of Kattanam Nambukulangara Road in Bharanikkavu GP in Alappuzha                          | Alappuzha      | Under Construction | 3.17        | 2.5671            | 2.8214            | 2021-10-27     | 2023-03-31      | 25%              | 0%               |                 |
| 10    | Reconstruction of Palangattupadi Manarathara Road in Alappuzha                                       | Alappuzha      | Under Construction | 2.49        | 2.0215            | 2.2216            | 2021-10-27     | 2023-01-31      | 30%              | 2%               | 0.054           |

|    |  |                |                    |       |        |        |            |            |     |     |        |
|----|--|----------------|--------------------|-------|--------|--------|------------|------------|-----|-----|--------|
| 11 | Reconstruction of Panachamoodu Kochuveetilmukku Road in Alappuzha                                    | Alappuzha      | Under Construction | 3.24  | 2.631  | 2.8892 | 2021-10-27 | 2023-02-15 | 20% | 0%  |        |
| 12 | Upgradation of Highschool Nannad Eradichira in Alappuzha   | Alappuzha      | Under Construction | 5.37  | 4.4847 | 4.7721 | 2021-10-27 | 2022-11-15 | 40% | 1%  | 0.0425 |
| 13 | Rehabilitation and reconstruction of Ex-Servicemen Colony Centre Road in Athirappally GP in Thrissur | Thrissur       | Under Construction | 2.6   | 1.9077 | 2.044  | 2021-10-27 | 2023-02-28 | 60% | 47% | 1.2271 |
| 14 | Nadakavu Ethiyerakavu Road in Vazhakulam GP, Kunnathunadu LAC in Ernakulam district                  | Ernakulam      | Under Construction | 0.41  | 0.2877 | 0.3161 | 2021-10-27 | 2023-02-27 | 30% | 0%  |        |
| 15 | Renovation of Panchayatpadi Pulluchani Radhapadi Road in Pathanamthitta district                     | Pathanamthitta | Under Construction | 4.04  | 3.2808 | 3.597  | 2021-10-27 | 2023-06-30 | 35% | 3%  | 0.1339 |
| 16 | Renovation of Policestationpadi TVM Hospital Elangavattom kshetram Road in Konni GP in Pathanamthit  | Pathanamthitta | Under Construction | 2.57  | 1.9547 | 2.1454 | 2021-10-27 | 2023-09-30 | 25% | 0%  |        |
| 17 | Upgradation of Narakathara Upperil Road in Kumarapuram GP Haripad LAC in Alappuzha                   | Alappuzha      | To be Dropped      | 1.95  | 1.5338 | 1.6731 | 0000-00-00 | 0000-00-00 | 0%  | 0%  |        |
| 18 | market Jetty Vathikkadu jetty Road   | Alappuzha      | AS Pending         | 1.14  | 0.9027 |        | 0000-00-00 | 0000-00-00 | 0%  | 0%  |        |
|    | Total  |                |                    | 40.47 | 32.28  | 33.17  |            |            |     |     | 5.66   |

**G.O.(Rt)No.2257/2020/LSGD dated 02.12.2020(0.0546cr)**

| Sl No | Name of Work                          | District | Status    | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|---------------------------------------|----------|-----------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | CBR Investigation of Roads in Wayanad | Wayanad  | Completed | 0.0546      |                   |                   | 2020-02-10     | 0000-00-00      | 100%             | 87%              | 0.0475          |
|       | Total                                 |          |           | 0.05        | 0                 | 0                 |                |                 |                  |                  | 0.05            |

**G.O.(Rt.)No.234/2021/LSGD dated 28.01.2021(1.2 cr)**

| Sl No | Name of Work  | District       | Status    | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|---|----------------|-----------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Soil Investigation for Bridges in TSR/PKD/MLP/WYD/KNR |                | Completed | 0.2001      |                   | 0.2001            | 2020-08-25     | 0000-00-00      | 100%             | 14%              | 0.0289          |
| 2     | Soil Investigation in Pathanamthitta 3 Bridges        | Pathanamthitta | Completed | 0.06        |                   |                   | 0000-00-00     | 0000-00-00      | 100%             | 0%               |                 |
| 3     | Soil Investigation in Alappuzha 10 Bridges            | Alappuzha      | Completed | 0.25        |                   |                   | 0000-00-00     | 0000-00-00      | 100%             | 34%              | 0.0859          |
| 4     | Soil Investigation in Kottayam 2 Bridges              | Kottayam       | Completed | 0.04        |                   |                   | 2020-08-02     | 2021-11-01      | 100%             | 80%              | 0.0319          |
| 5     | Soil Investigation in Idukki 12 Bridges               | Idukki         | Completed | 0.34        |                   | 0.21              | 2021-08-02     | 0000-00-00      | 100%             | 53%              | 0.1807          |
| 6     | Soil Investigation in Ernakulam 9 Bridges             | Ernakulam      | Completed | 0.275       |                   |                   | 0000-00-00     | 0000-00-00      | 100%             | 0%               |                 |
|       | Total   |                |           | 1.17        | 0                 | 0.41              |                |                 |                  |                  | 0.33            |

**G.O.(Rt) 1669/2020/LSGD dated 16.09.2020(0.0246 cr)**

| Sl No | Name of Work                            | District | Status    | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|---|----------|-----------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Topographic Survey for roads in Wayanad | Wayanad  | Completed | 0.0246      |                   |                   | 2020-01-15     | 0000-00-00      | 100%             | 62%              | 0.0153          |
|       | Total                                   |          |           | 0.02        | 0                 | 0                 |                |                 |                  |                  | 0.02            |

**G.O.(Rt.)No.348/2021/P&EA dated 15-08-2021(30.91cr)**

| SI No | Name of Work   | District       | Status             | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|--|----------------|--------------------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Rehabilitation of Athikkayam Kadumeenchira Road in Naranamoozhy GP ,Ranni LAC, Pathanamthitta Distri | Pathanamthitta | Under Construction | 3.05        | 1.8423            | 1.8506            | 2022-03-30     | 2023-07-30      | 30%              | 0%               |                 |
| 2     | Reconstruction of Factorypadi Karintharuvi Road in Upputhara GP, Peerumedu LAC , Idukki District     | Idukki         | Under Construction | 3.22        | 2.6584            | 2.4446            | 2022-01-04     | 2023-05-30      | 25%              | 0%               |                 |
| 3     | Reconstruction of Sooryakanthikavala Old Post Office Road in Upputhara GP, Peerumedu LAC , Idukki Di | Idukki         | Under Construction | 1.3         | 1.0761            | 0.9889            | 2022-01-04     | 2023-05-30      | 10%              | 0%               |                 |
| 4     | Rehabilitation of Valiyaparambil-Eetichuvadu Road in Pazhavangadi GP ,Ranni LAC, Pathanamthitta Dis  | Pathanamthitta | Under Construction | 1.7         | 1.1769            | 1.1664            | 2022-01-06     | 2023-03-31      | 40%              | 0%               |                 |
| 5     | Rehabilitation of Janaseva Road in Thiruvalla LAC Peringara LSGI Pathanamthitta district             | Pathanamthitta | Under Construction | 3.1         | 2.3319            | 2.3218            | 2022-02-28     | 2023-07-31      | 30%              | 0%               |                 |
| 6     | Improvement of Kalpetta Town Jilla Stadium Road in Kalpetta LAC in Wayanad district                  | Wayanad        | Under Construction | 2.97        | 2.1802            | 2.3231            | 2022-03-21     | 2023-03-21      | 25%              | 0%               |                 |
| 7     | Rehabilitation of Ushuspadi-Vallaparamuruppu Kizhakkekkarapally Road in Adoor LAC Ezhankulam LSGI P  | Pathanamthitta | Under Construction | 2.25        | 1.5712            | 1.6261            | 2022-03-21     | 2023-06-30      | 40%              | 0%               |                 |
| 8     | Upgradation of 45-il Puthuvel Jetty road in Kuttanad LAC Thakazhy LSGI Alappuzha District            | Alappuzha      | Under Construction | 2.01        | 1.6508            | 1.7983            | 2022-04-21     | 2023-02-09      | 15%              | 0%               |                 |

|    |  |                |                    |       |        |        |            |            |     |     |        |
|----|--|----------------|--------------------|-------|--------|--------|------------|------------|-----|-----|--------|
| 9  | Reconstruction of Govt Hospital road in Kuttanad LAC Thakazhy LSGI Alappuzha District                | Alappuzha      | Under Construction | 2.19  | 1.8226 | 1.9648 | 2022-04-21 | 2023-02-09 | 25% | 25% | 0.5388 |
| 10 | Construction of Nalenkalpadi to Kunnathuparambu road in Kuttanad LAC Thalavady LSGI Alappuzha Distr  | Alappuzha      | Under Construction | 1.98  | 1.6008 | 1.7636 | 2022-04-26 | 2023-01-21 | 10% | 0%  |        |
| 11 | Construction of Manenkarypadi to Kodumkuthuparambu road in Kuttanad LAC Chambakulam LSGI Alappuzha D | Alappuzha      | Under Construction | 1.35  | 1.0432 | 1.1407 | 2022-04-21 | 2023-03-26 | 25% | 0%  |        |
| 12 | Ambiyathupadi Ikkara Boat jetty road in Kuttanad LAC Edathua LSGI Alappuzha District                 | Alappuzha      | Under Construction | 3.6   | 2.8969 | 3.186  | 2022-04-26 | 2023-03-27 | 10% | 0%  |        |
| 13 | Reconstruction of Kannankara Edamuri Road in Pathanamthitta District                                 | Pathanamthitta | Under Construction | 1.13  | 0.8596 | 0.9451 | 2022-07-05 | 2023-05-31 | 6%  | 0%  |        |
| 14 | Malayuman Vazhayilpadi Road in Pathanamthitta  | Pathanamthitta | Technical Sanction | 1.06  | 0.6512 | -      | 0000-00-00 | 0000-00-00 | 0%  | 0%  |        |
|    | Total  |                |                    | 30.91 | 23.36  | 23.52  |            |            |     |     | 0.54   |



**G.O.(Rt.)No.18/2022/P&EA dated 07-01-2022(49.34cr)**

| Sl No | Name of Work   | District       | Status             | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|--|----------------|--------------------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Rehabilitation of Koipallymelethilpadi Road in Ayroor GP Ranni LAC in Pathanamthitta District      | Pathanamthitta | Under Construction | 1.44        | 1.1745            | 1.1146            | 2022-04-26     | 2023-07-31      | 10%              | 0%               |                 |
| 2     | Rehabilitation of Ozhukuneetilpadi Paruthimootilpadi Road in Peringara GP Thiruvalla LAC in Pathan | Pathanamthitta | Under Construction | 3.47        | 2.3329            | 2.25              | 2022-04-21     | 2021-08-31      | 6%               | 0%               |                 |
| 3     | Rehabilitation of Kannamplackalpadi Puthenpalam Road in Nedumkandom GP Udumbanchola LAC in Idukki  | Idukki         | Under Construction | 1.13        | 0.8631            | 0.8221            | 2022-04-30     | 2023-05-30      | 10%              | 0%               |                 |
| 4     | Upgradation of KE Carmel Pulickal Road in Kanjikuzhy GP, Cherthala LAC, Alappuzha District         | Alappuzha      | Under Construction | 0.99        | 0.7717            | 0.7461            | 2022-04-21     | 2023-01-31      | 95%              | 0%               |                 |
| 5     | Upgradation of Kavumpadi to Perumal Jetty Road in Kavalam GP, Kuttanad LAC, Alappuzha District     | Alappuzha      | Under Construction | 2.01        | 1.7106            | 1.5968            | 2022-04-30     | 2023-04-30      | 35%              | 0%               |                 |
| 6     | Karichira to Puthusseri Road in Ambalappuzha South GP, Ambalappuzha LAC, Alappuzha District        | Alappuzha      | Under Construction | 2.61        | 2.2172            | 2.1828            | 2022-04-21     | 2023-04-30      | 10%              | 0%               |                 |
| 7     | St. Therasas LPS to Nalpathil Kalinku Road in Kavalam GP Kuttanad LAC in Alappuzha district        | Alappuzha      | Under Construction | 1.74        | 1.4799            | 1.4097            | 2022-05-20     | 2023-02-06      | 30%              | 0%               |                 |

|    |   |           |                    |      |        |        |            |            |     |    |        |
|----|---|-----------|--------------------|------|--------|--------|------------|------------|-----|----|--------|
| 8  | Eranjoli Pulikkal Road in Kaniyambatta GP Kalpetta LAC in Wayanad district                            | Wayanad   | Under Construction | 3.38 | 2.7585 | 2.6115 | 2022-05-18 | 2023-05-18 | 0%  | 0% |        |
| 9  | Improvement of Changadakadavu Chamadipoyi Road in Edavaka GP Mananthavady LAC in Wayanad district     | Wayanad   | Under Construction | 3.04 | 2.3899 | 2.1842 | 2022-06-14 | 2023-06-14 | 6%  | 0% |        |
| 10 | Upgradation of Kallanchery Tharasserri Road in Kumbalangi GP Kochi LAC in Ernakulam District          | Ernakulam | Under Construction | 3.1  | 2.5728 | 2.83   | 2022-07-23 | 2023-04-30 | 6%  | 5% | 0.1513 |
| 11 | Upgradation of Thiruvaniyoor Meppadam Road in Thiruvaniyoor GP Kunnathunadu LAC in Ernakulam District | Ernakulam | Under Construction | 3.42 | 2.5597 | 2.6811 | 2022-07-14 | 2023-04-30 | 6%  | 0% |        |
| 12 | Anchalangadi Bridge to Mancompu Govt. LPS Road in Alappuzha District                                  | Alappuzha | Under Construction | 3.22 | 2.7025 | 2.9652 | 2022-07-05 | 2023-07-05 | 6%  | 0% |        |
| 13 | Construction of Amarathode Pathilchira Road in Alappuzha District                                     | Alappuzha | Under Construction | 2.5  | 2.1142 | 2.3232 | 2022-07-05 | 2023-04-30 | 10% | 0% |        |
| 14 | Construction of Pekkali Bridge to Kadakam Road in Alappuzha District                                  | Alappuzha | Under Construction | 0.95 | 0.7924 | 0.8225 | 2022-07-01 | 2022-04-30 | 15% | 0% |        |
| 15 | Upgradation of PS Kavala Chudukattumpuram Chooramana Road in Thycattussery GP Aroor LAC in Alappuzha  | Alappuzha | Under Construction | 3.17 | 2.6942 | 2.9633 | 2022-07-05 | 2023-07-05 | 0%  | 0% |        |
| 16 | Construction of Kumaramkari Society Road in Alappuzha District  | Alappuzha | Under Construction | 3.79 | 3.2144 | 3.492  | 2022-07-04 | 2023-05-04 | 10% | 0% |        |
| 17 | Therambilpadi Road in Thalavady GP Kuttanad LAC in Alappuzha District                                 | Alappuzha | Under Construction | 2.42 | 1.988  | 2.1868 | 2022-07-05 | 2023-07-05 | 0%  | 0% |        |

|    |  |           |                    |       |        |       |            |            |     |    |      |
|----|--|-----------|--------------------|-------|--------|-------|------------|------------|-----|----|------|
| 18 | Footpath Thottuvala First Bridge to Aattutheeram Road in Kainakary GP Kuttanad LAC in Alappuzha Dist | Alappuzha | Under Construction | 1.49  | -      | -     | 0000-00-00 | 0000-00-00 | 6%  | 0% |      |
| 19 | SN JN. Chengadakkari Chengada Road in Chennam Pallipuram GP  | Alappuzha | To be Dropped      | 0.74  | 0.6233 | -     | 0000-00-00 | 0000-00-00 | 0%  | 0% |      |
| 20 | Kanichukulangara kavala Kalathilveedu Road in kanjikuzhy GP  | Alappuzha | Under Construction | 1.57  | 1.263  | -     | 0000-00-00 | 0000-00-00 | 6%  | 0% |      |
| 21 | Kainad Pally- Karumathra Kshetram Road in Neelampaeroor GP   | Alappuzha | Under Construction | 1.81  | 1.5102 | -     | 0000-00-00 | 0000-00-00 | 10% | 0% |      |
| 22 | Holy family School to Pazhoor temple road in Kainakary GP  | Alappuzha | Under Construction | 1.35  | -      | -     | 0000-00-00 | 2023-07-22 | 10% | 0% |      |
|    | Total  |           |                    | 49.34 | 37.73  | 35.18 |            |            |     |    | 0.15 |

**G.O.(Rt)No.300/2022/P&EA dated 02-08-2022(25.85cr)**

| Sl No | Name of Work                                | District       | Status             | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|---|----------------|--------------------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Valiyapalli Kayalpuram School Road          | Alappuzha      | Tender Process     | 4.3         | -                 | -                 | 0000-00-00     | 0000-00-00      | 0%               | 0%               |                 |
| 2     | Ramapuram Illathupadi Valiyathupadi Road    | Pathanamthitta | Technical Sanction | 0.85        | -                 | -                 | 0000-00-00     | 0000-00-00      | 0%               | 0%               |                 |
| 3     | Pulikeezhu Road                             | Pathanamthitta | Technical Sanction | 2.6         | -                 | -                 | 0000-00-00     | 0000-00-00      | 0%               | 0%               |                 |
| 4     | Papanattupadi Panchayathupadi Road          | Pathanamthitta | Technical Sanction | 2.22        | -                 | -                 | 0000-00-00     | 0000-00-00      | 0%               | 0%               |                 |
| 5     | Thattekkallu Ponnezhuthan                   | Idukki         | AS Received        | 3.25        | -                 | -                 | 0000-00-00     | 0000-00-00      | 0%               | 0%               |                 |
| 6     | Bhoomiyankulam Keshamini Road               | Idukki         | AS Received        | 1.9         | -                 | -                 | 0000-00-00     | 0000-00-00      | 0%               | 0%               |                 |
| 7     | Araikkalpadai Ambikavilasam Estatepadi Road | Idukki         | AS Received        | 5.65        | -                 | -                 | 0000-00-00     | 0000-00-00      | 0%               | 0%               |                 |
| 8     | Sahi Rubber Ambalamukku Kattuman Road       | Ernakulam      | Tender Process     | 1.7         | -                 | -                 | 0000-00-00     | 0000-00-00      | 0%               | 0%               |                 |
| 9     | Kuzhur Iranikulam Indira Gandhi Road        | Thrissur       | Tender Process     | 3.38        | -                 | -                 | 0000-00-00     | 0000-00-00      | 0%               | 0%               |                 |
|       | Total                                       |                |                    | 25.85       | 0                 | 0                 |                |                 |                  |                  | 0               |

**G.O.(Rt)No.405/2022/LSGD dated 22.02.2022(0.721cr)**

| Sl No | Name of Work  | District | Status          | AS Amt.(cr) | Tendered Amt.(cr) | Contract Amt.(cr) | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Expenditure(cr) |
|-------|---|----------|-----------------|-------------|-------------------|-------------------|----------------|-----------------|------------------|------------------|-----------------|
| 1     | Consultancy Services for design and preparation of DPR of Bridges (Alappuzha Dist)                    |          | DPR Preparation |             | 0.0923            | 0.0905            | 2022-09-30     | 2022-12-30      | 0%               | 0%               |                 |
| 2     | Consultancy Services for design and preparation of DPR of Bridges (ERNAKULAM AND THRISSUR Dist)       |          | DPR Preparation |             | 0.0401            | 0.0397            | 2022-09-19     | 2022-12-19      | 0%               | 0%               |                 |
| 3     | Consultancy Services for design and preparation of DPR of Bridges (Idukki Dist)                       |          | DPR Preparation |             | 0.0998            | 0.0978            | 2022-09-30     | 2022-12-30      | 0%               | 0%               |                 |
| 4     | Consultancy Services for design and preparation of DPR of Bridges (Kannur, Palakkat and Wayanad Dist) |          | DPR Preparation |             | 0.0579            | 0.0567            | 2022-09-30     | 2022-12-30      | 0%               | 0%               |                 |
|       | Total   |          |                 | 0           | 0.29              | 0.28              |                |                 |                  |                  | 0               |



**DETAILED REPORTS OF WORKS  
DISTRICT WISE**

## ALAPPUZHA

| SI No | Name of Work   | AS No.                        | Status             | AS Amt. | Tendered Amt. | Contract Amt. | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Remarks |
|-------|--|-------------------------------|--------------------|---------|---------------|---------------|----------------|-----------------|------------------|------------------|---------|
| 1     | Up gradation of Ennakkad Alumoodu Elanjimel Road in Budhanoor GP in Alappuzha                        | G.O.(Rt.)No.224/2<br>020/P&EA | Under Construction | 6.39    | 4.9438        | 4.8004        | 2020-10-09     | 2023-01-31      | 50%              | 1%               |         |
| 2     | Up gradation of Budhanoor Ponnathara Road in Alappuzha   | G.O.(Rt.)No.224/2<br>020/P&EA | Under Construction | 2.91    | 2.37          | 2.30          | 2020-10-09     | 2023-01-31      | 40%              | 0%               |         |
| 3     | Renovation of Kulikkanpalam Shappupadi Road in Alappuzha   | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 2.78    | 2.06          | 1.8871        | 2020-09-22     | 2022-09-30      | 100%             | 46%              |         |
| 4     | Reconstruction of AV Mukku Sharangakkavu Road in Alappuzha   | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 2.82    | 2.0495        | 1.873         | 2020-11-06     | 2022-09-30      | 100%             | 54%              |         |
| 5     | Reconstruction of Pennukara canal Jn Nettuvaramcode road in Alappuzha                                | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 2.99    | 1.8603        | 1.6985        | 2020-09-04     | 2022-04-20      | 100%             | 66%              |         |
| 6     | Kanjikkal Mukku Ganam theatre road in in Bharanikavu GP, Kayamkulam LAC, Alappuzha District          | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 2.14    | 1.6332        | 1.6294        | 2021-05-04     | 2023-03-31      | 50%              | 24%              |         |
| 7     | Reconstruction of AC Canal to Mankuzhy Road in Ramankary GP, Kuttanad LAC, Alappuzha District        | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 1.15    | 0.9364        | 1.0205        | 2021-08-26     | 2023-03-31      | 70%              | 18%              |         |
| 8     | Chirakkarapadi - Chetalapuncha, Pmattipuncha, Pazhamchira Road in Venmani and Cheriyanad GP, Chengan | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 3.48    | 2.8405        | 2.6804        | 2021-05-04     | 2023-03-31      | 50%              | 0%               |         |
| 9     | Reconstruction of Manathukadu Puthuveedu Road and Protection in Chambakulam, Kuttanad LAC, Alappuzha | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 2       | 1.6692        | 1.7855        | 2021-08-26     | 2023-04-30      | 50%              | 20%              |         |
| 10    | Reconstruction of PWD Road to Arackalchira and Protection Wall in Chambakulam GP in Alappuzha distri | G.O.(Rt.)No.62/20<br>21/P&EA  | Under Construction | 1.22    | 1.0262        | 1.025         | 2021-08-26     | 2023-04-30      | 60%              | 41%              |         |
| 11    | Harbour Road to Manaladi Jetty Road in Ramankary GP, Kuttanad LAC, Alappuzha district                | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 1.24    | 1.0376        | 1.141         | 2021-11-06     | 2023-02-06      | 30%              | 0%               |         |

|    |  |                               |                    |      |        |        |            |            |      |     |  |
|----|--|-------------------------------|--------------------|------|--------|--------|------------|------------|------|-----|--|
| 12 | Upgradation of Madathekkathil Chalukara Road in Alappuzha  | G.O.(Rt.)No.62/20<br>21/P&EA  | Completed          | 0.27 | 0.2138 | 0.2316 | 2021-10-27 | 2022-09-30 | 100% | 0%  |  |
| 13 | Rehabilitation of Mithrapuzha Vayanasalapadi Vendoorpadi in Chenganoor municipality in Alappuzha     | G.O.(Rt.)No.62/20<br>21/P&EA  | Under Construction | 3.32 | 2.6043 | 2.8365 | 2021-10-27 | 2022-09-30 | 55%  | 55% |  |
| 14 | Upgradation of Kattanam Nambukulangara Road in Bharanikkavu GP in Alappuzha                          | G.O.(Rt.)No.62/20<br>21/P&EA  | Under Construction | 3.17 | 2.5671 | 2.8214 | 2021-10-27 | 2023-03-31 | 25%  | 0%  |  |
| 15 | Reconstruction of Palangattupadi Manarathara Road in Alappuzha                                       | G.O.(Rt.)No.62/20<br>21/P&EA  | Under Construction | 2.49 | 2.0215 | 2.2216 | 2021-10-27 | 2023-01-31 | 30%  | 2%  |  |
| 16 | Reconstruction of Panachamoodu Kochuveetilmukku Road in Alappuzha                                    | G.O.(Rt.)No.62/20<br>21/P&EA  | Under Construction | 3.24 | 2.631  | 2.8892 | 2021-10-27 | 2023-02-15 | 20%  | 0%  |  |
| 17 | Upgradation of Highschool Nannad Eradichira in Alappuzha   | G.O.(Rt.)No.62/20<br>21/P&EA  | Under Construction | 5.37 | 4.4847 | 4.7721 | 2021-10-27 | 2022-11-15 | 40%  | 1%  |  |
| 18 | Upgradation of Narakathara Upperil Road in Kumarapuram GP Haripad LAC in Alappuzha                   | G.O.(Rt.)No.62/20<br>21/P&EA  | To be Dropped      | 1.95 | 1.5338 | 1.6731 | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 19 | Upgradation of 45-il Puthuvel Jetty road in Kuttanad LAC Thakazhy LSGI Alappuzha District            | G.O.(Rt.)No.348/2<br>021/P&EA | Under Construction | 2.01 | 1.6508 | 1.7983 | 2022-04-21 | 2023-02-09 | 15%  | 0%  |  |
| 20 | Reconstruction of Govt Hospital road in Kuttanad LAC Thakazhy LSGI Alappuzha District                | G.O.(Rt.)No.348/2<br>021/P&EA | Under Construction | 2.19 | 1.8226 | 1.9648 | 2022-04-21 | 2023-02-09 | 25%  | 25% |  |
| 21 | Construction of Nalenkalpadi to Kunnathuparambu road in Kuttanad LAC Thalavady LSGI Alappuzha Distr  | G.O.(Rt.)No.348/2<br>021/P&EA | Under Construction | 1.98 | 1.6008 | 1.7636 | 2022-04-26 | 2023-01-21 | 10%  | 0%  |  |
| 22 | Construction of Manenkarypadi to Kodumkuthuparambu road in Kuttanad LAC Chambakulam LSGI Alappuzha D | G.O.(Rt.)No.348/2<br>021/P&EA | Under Construction | 1.35 | 1.0432 | 1.1407 | 2022-04-21 | 2023-03-26 | 25%  | 0%  |  |
| 23 | Ambiyathupadi Ikkara Boat jetty road in Kuttanad LAC Edathua LSGI Alappuzha District                 | G.O.(Rt.)No.348/2<br>021/P&EA | Under Construction | 3.6  | 2.8969 | 3.186  | 2022-04-26 | 2023-03-27 | 10%  | 0%  |  |



|    |  |                              |                    |      |        |        |            |            |     |    |  |
|----|--|------------------------------|--------------------|------|--------|--------|------------|------------|-----|----|--|
| 24 | Upgradation of KE Carmel Pulickal Road in Kanjikuzhy GP, Cherthala LAC, Alappuzha District           | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 0.99 | 0.7717 | 0.7461 | 2022-04-21 | 2023-01-31 | 95% | 0% |  |
| 25 | Upgradation of Kavumpadi to Perumal Jetty Road in Kavalam GP, Kuttanad LAC, Alappuzha District       | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 2.01 | 1.7106 | 1.5968 | 2022-04-30 | 2023-04-30 | 35% | 0% |  |
| 26 | Karichira to Puthusseri Road in Ambalappuzha South GP, Ambalappuzha LAC, Alappuzha District          | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 2.61 | 2.2172 | 2.1828 | 2022-04-21 | 2023-04-30 | 10% | 0% |  |
| 27 | St. Therasas LPS to Nalpathil Kalinku Road in Kavalam GP Kuttanad LAC in Alappuzha district          | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 1.74 | 1.4799 | 1.4097 | 2022-05-20 | 2023-02-06 | 30% | 0% |  |
| 28 | Anchalangadi Bridge to Mancompu Govt. LPS Road in Alappuzha District                                 | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 3.22 | 2.7025 | 2.9652 | 2022-07-05 | 2023-07-05 | 6%  | 0% |  |
| 29 | Construction of Amarathode Pathilchira Road in Alappuzha District                                    | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 2.5  | 2.1142 | 2.3232 | 2022-07-05 | 2023-04-30 | 10% | 0% |  |
| 30 | Construction of Pekkali Bridge to Kadakam Road in Alappuzha District                                 | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 0.95 | 0.7924 | 0.8225 | 2022-07-01 | 2022-04-30 | 15% | 0% |  |
| 31 | Upgradation of PS Kavala Chudukattumpuram Chooramana Road in Thycattusery GP Aroor LAC in Alappuzha  | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 3.17 | 2.6942 | 2.9633 | 2022-07-05 | 2023-07-05 | 0%  | 0% |  |
| 32 | Construction of Kumaramkari Society Road in Alappuzha District                                       | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 3.79 | 3.2144 | 3.492  | 2022-07-04 | 2023-05-04 | 10% | 0% |  |
| 33 | Therambilpadi Road in Thalavady GP Kuttanad LAC in Alappuzha District                                | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 2.42 | 1.988  | 2.1868 | 2022-07-05 | 2023-07-05 | 0%  | 0% |  |
| 34 | Footpath Thottuvala First Bridge to Aattutheeram Road in Kainakary GP Kuttanad LAC in Alappuzha Dist | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 1.49 | -      | -      | 0000-00-00 | 0000-00-00 | 6%  | 0% |  |
| 35 | SN JN. Chengadakkari Chengada Road in Chennam Pallipuram GP  | G.O.(Rt.)No.18/20<br>22/P&EA | To be Dropped      | 0.74 | 0.6233 | -      | 0000-00-00 | 0000-00-00 | 0%  | 0% |  |
| 36 | Kanichukulangara kavala Kalathilveedu Road in kanjikuzhy GP  | G.O.(Rt.)No.18/20<br>22/P&EA | Under Construction | 1.57 | 1.263  | -      | 0000-00-00 | 0000-00-00 | 6%  | 0% |  |

|    |  |                               |                    |        |        |        |            |            |      |     |  |
|----|--|-------------------------------|--------------------|--------|--------|--------|------------|------------|------|-----|--|
| 37 | Kainad Pally- Karumathra Kshetram Road in Neelampaeroor GP | G.O.(Rt.)No.18/20<br>22/P&EA  | Under Construction | 1.81   | 1.5102 | -      | 0000-00-00 | 0000-00-00 | 10%  | 0%  |  |
| 38 | Holy family School to Pazhoor temple road in Kainakary GP  | G.O.(Rt.)No.18/20<br>22/P&EA  | Under Construction | 1.35   | -      | -      | 0000-00-00 | 2023-07-22 | 10%  | 0%  |  |
| 39 | Valiyapalli Kayalpuram School Road                         | G.O.(Rt)No.300/2<br>022/P&EA  | Tender Process     | 4.3    | -      | -      | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 40 | market Jetty Vathikkadu jetty Road                         | G.O.(Rt.)No.62/20<br>21/P&EA  | AS Pending         | 1.14   | 0.9027 |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 41 | Investigation/ data collection - Alappuzha District        | G.O.(Rt)No.115/2<br>020/P&EA  | Completed          | 0.8174 | 0.8174 | 0.5449 | 2020-09-04 | 2022-08-30 | 100% | 22% |  |
| 42 | Soil Investigation in Alappuzha 10 Bridges                 | G.O.(Rt.)No.234/2<br>021/LSGD | Completed          | 0.25   |        |        | 0000-00-00 | 0000-00-00 | 100% | 34% |  |
| 43 | Moorthitta Mukkatheri Vazhayi(Chackittapady Bridge)        | G.O.(Rt)No.221/2<br>020/P&EA  | DPR Preparation    |        |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 44 | Naduvath moon bridge                                       | G.O.(Rt)No.221/2<br>020/P&EA  | DPR Preparation    |        |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 45 | Nellanickal Ambalam Road                                   | G.O.(Rt)No.221/2<br>020/P&EA  | DPR Preparation    |        |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 46 | SNDP to Nadukkodu  | G.O.(Rt)No.221/2<br>020/P&EA  | DPR Preparation    |        |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 47 | SNDP to Vadaparambu Culvert Road                           | G.O.(Rt)No.221/2<br>020/P&EA  | DPR Preparation    |        |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 48 | Vallamkadavu Chillithuruth Swamithara Road                 | G.O.(Rt)No.221/2<br>020/P&EA  | DPR Preparation    |        |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 49 | Sn Junction Tsunami Smaraka Road                           | G.O.(Rt)No.221/2<br>020/P&EA  | DPR Preparation    |        |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |

**PATHANAMTHITTA**

| SI No | Name of Work   | AS No                         | Status             | AS Amt.       | Tendered Amt. | Contract Amt. | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Remarks |
|-------|--|-------------------------------|--------------------|---------------|---------------|---------------|----------------|-----------------|------------------|------------------|---------|
| 1     | Renovation of Kottomonpara Melekottomonpara Pandyanpara Road in Seethathode GP in Pathanamthitta dis | G.O.(Rt.)No.62/20<br>21/P&EA  | Under Construction | 2.48          | 2.0038        | 1.9291        | 2021-08-02     | 2023-03-31      | 60%              | 14%              |         |
| 2     | Rehabilitation of Adoor Gopalakrishnan Road in Erathu GP in in Pathanamthitta district               | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 2.457477<br>1 | 1.8977        | 1.9534        | 2021-10-27     | 2023-04-30      | 48%              | 0%               |         |
| 3     | Renovation of CK Road in Kottangal GP in Pathanamthitta district                                     | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 2.769         | 1.7836        | 1.8925        | 2021-10-27     | 2023-06-30      | 30%              | 0%               |         |
| 4     | Paivazhy Nediakala Road in Pandalam MC in Pathanamthitta district                                    | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 3.758860<br>3 | 2.7723        | 3.0208        | 2021-10-27     | 2023-05-30      | 60%              | 12%              |         |
| 5     | Renovation of Panchayatpadi Pulluchani Radhapadi Road in Pathanamthitta district                     | G.O.(Rt.)No.62/20<br>21/P&EA  | Under Construction | 4.04          | 3.2808        | 3.597         | 2021-10-27     | 2023-06-30      | 35%              | 3%               |         |
| 6     | Renovation of Policestationpadi TVM Hospital Elangavattom kshetram Road in Konni GP in Pathanamthit  | G.O.(Rt.)No.62/20<br>21/P&EA  | Under Construction | 2.57          | 1.9547        | 2.1454        | 2021-10-27     | 2023-09-30      | 25%              | 0%               |         |
| 7     | Renovation of Chakrasalakadavu Panachimoottil Road in Kuttoor GP in Pathanamthitta district          | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 2.769         | 2.094         | 2.2824        | 2021-10-27     | 2023-05-30      | 50%              | 0%               |         |
| 8     | Improvement of Thannithode Plantation road in Pathanamthitta district                                | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 5.2695        | 4.0737        | 4.2613        | 2021-10-21     | 2023-03-31      | 70%              | 8%               |         |
| 9     | Reconstruction of Banglamkadavu Stadium Valiyakulam Road in Vadasserikkara GP in Pathanamthitta dist | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 2.31          | 1.873         | 1.8728        | 2022-03-21     | 2023-06-30      | 15%              | 0%               |         |
| 10    | Reconstruction of Banglamkadavu Valiyakulam Road in Vadasserikkara GP in Pathanamthitta district     | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 2.05          | 1.6814        | 1.6433        | 2022-03-21     | 2023-04-30      | 40%              | 0%               |         |

|    |   |                           |                    |           |        |        |            |            |     |     |  |
|----|---|---------------------------|--------------------|-----------|--------|--------|------------|------------|-----|-----|--|
| 11 | Chana Kurumpanmoozhy Road in Naranamoozhy GP, Ranni LAC, Pathanamthitta district                      | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 2.18      | 1.7904 | 1.7007 | 2022-03-21 | 2023-05-30 | 20% | 0%  |  |
| 12 | Madukkamoodu Ayyappa Medical College Road in Vadasserikkara GP, Ranni LAC, Pathanamthitta district    | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.47      | 1.1821 | 1.0639 | 2021-10-27 | 2023-04-30 | 65% | 17% |  |
| 13 | Rationkadapadi Mulanthanam Road in Perunadu GP, Ranni LAC in Pathanamthitta district                  | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.401     | 1.0919 | 1.1288 | 2021-12-27 | 2023-07-30 | 20% | 0%  |  |
| 14 | Arummoode- Chala Puthenchantha 14th mile Adoor LAC Pallikkal LSGI Pathanamthitta district             | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.875     | 1.3583 | 1.4787 | 2022-12-27 | 2023-07-30 | 20% | 0%  |  |
| 15 | Rehabilitation of Athikkayam Kadumeenchira Road in Naranamoozhy GP ,Ranni LAC, Pathanamthitta Distri  | G.O.(Rt.)No.348/2021/P&EA | Under Construction | 3.05      | 1.8423 | 1.8506 | 2022-03-30 | 2023-07-30 | 30% | 0%  |  |
| 16 | Rehabilitation of Valiyaparambil-Eetichuvadu Road in Pazhavangadi GP ,Ranni LAC, Pathanamthitta Dis   | G.O.(Rt.)No.348/2021/P&EA | Under Construction | 1.7       | 1.1769 | 1.1664 | 2022-01-06 | 2023-03-31 | 40% | 0%  |  |
| 17 | Rehabilitation of Janaseva Road in Thiruvalla LAC Peringara LSGI Pathanamthitta district              | G.O.(Rt.)No.348/2021/P&EA | Under Construction | 3.1       | 2.3319 | 2.3218 | 2022-02-28 | 2023-07-31 | 30% | 0%  |  |
| 18 | Anthyalankavu Marthomappallipadi Karamvelipadi Road in Naranganam GP, Aranmula LAC, Pathanamthitta di | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.3868464 | 1.0759 | 1.1079 | 2022-06-22 | 2023-05-30 | 35% | 0%  |  |
| 19 | Kiliyanikkal Thoolikulam Road Ranni LAC Cherukole LSGI in Pathanamthitta district                     | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.5625875 | 1.1108 | 1.2585 | 2022-03-21 | 2023-06-30 | 40% | 0%  |  |
| 20 | Reconstruction of Parakkavu Valakuzhi Road in Ezhumattur GP in Pathanamthitta District                | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.9716022 | 1.4124 | 1.5535 | 2022-03-21 | 2023-04-30 | 50% | 0%  |  |
| 21 | Reconstruction of Melepadu Chellakadu Road in Pazhavangadi GP in Pathanamthitta District              | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 2.092     | 1.649  | 1.7181 | 2022-03-24 | 2023-07-30 | 25% | 0%  |  |

|    |   |                           |                    |        |        |        |            |            |     |    |  |
|----|---|---------------------------|--------------------|--------|--------|--------|------------|------------|-----|----|--|
| 22 | Rehabilitation of Ushuspadi-Vallaparamuruppu Kizhakkekkarapally Road in Adoor LAC Ezhamkulam LSGI P | G.O.(Rt.)No.348/2021/P&EA | Under Construction | 2.25   | 1.5712 | 1.6261 | 2022-03-21 | 2023-06-30 | 40% | 0% |  |
| 23 | Erathodu Ashankuzhy road in Tiruvalla LAC Niranam LSGI Pathanamthitta District                      | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.9645 | 1.5591 | 1.6152 | 2022-04-21 | 2023-07-31 | 35% | 0% |  |
| 24 | Rehabilitation of Koipallymelethilpadi Road in Ayroor GP Ranni LAC in Pathanamthitta District       | G.O.(Rt.)No.18/2022/P&EA  | Under Construction | 1.44   | 1.1745 | 1.1146 | 2022-04-26 | 2023-07-31 | 10% | 0% |  |
| 25 | Rehabilitation of Ozhukuneetilpadi Paruthimootilpadi Road in Peringara GP Thiruvalla LAC in Pathan  | G.O.(Rt.)No.18/2022/P&EA  | Under Construction | 3.47   | 2.3329 | 2.25   | 2022-04-21 | 2021-08-31 | 6%  | 0% |  |
| 26 | Reconstruction of Kannankara Edamuri Road in Pathanamthitta District                                | G.O.(Rt.)No.348/2021/P&EA | Under Construction | 1.13   | 0.8596 | 0.9451 | 2022-07-05 | 2023-05-31 | 6%  | 0% |  |
| 27 | Kalarikode Pallana Puthenvelipadi Road in Pathanamthitta district Aranmula LAC Aranmula LSGI        | G.O.(Rt.)No.485/2019/P&EA | To be Dropped      | 1.98   | 1.3039 | -      | 0000-00-00 | 0000-00-00 | 0%  | 0% |  |
| 28 | Vattathenpady Nallathupady Road in Pathanamthitta district Aranmula LAC Aranmula LSGI               | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.128  | 0.7040 | 0.8133 | 2022-10-07 | 2023-04-30 | 35% | 0% |  |
| 29 | Poovanmala Panamplackal Road in Pathanamthitta district Ranni LAC Angadi LSGI                       | G.O.(Rt.)No.485/2019/P&EA | Tender Process     | 1.2125 | 0.7659 | -      | 0000-00-00 | 0000-00-00 | 0%  | 0% |  |
| 30 | Malayuman Vazhayilpadi Road in Pathanamthitta   | G.O.(Rt.)No.348/2021/P&EA | Technical Sanction | 1.06   | 0.6512 | -      | 0000-00-00 | 0000-00-00 | 0%  | 0% |  |
| 31 | Ramapuram Illathupadi Valiyathupadi Road  | G.O.(Rt.)No.300/2022/P&EA | Technical Sanction | 0.85   | -      | -      | 0000-00-00 | 0000-00-00 | 0%  | 0% |  |
| 32 | Pulikeezhu Road   | G.O.(Rt.)No.300/2022/P&EA | Technical Sanction | 2.6    | -      | -      | 0000-00-00 | 0000-00-00 | 0%  | 0% |  |
| 33 | Papanattupadi Panchayathupadi Road  | G.O.(Rt.)No.300/2022/P&EA | Technical Sanction | 2.22   | -      | -      | 0000-00-00 | 0000-00-00 | 0%  | 0% |  |

|    |  |                               |             |        |        |        |            |            |      |     |  |
|----|--|-------------------------------|-------------|--------|--------|--------|------------|------------|------|-----|--|
| 34 | Thiruvabharanapatha Road                                       | G.O.(Rt.)No.485/2<br>019/P&EA | AS Received | 8      |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 35 | Investigation/ data collection -<br>Pathanamthitta District    | G.O.(Rt)No.115/2<br>020/P&EA  | Completed   | 0.4152 | 0.4152 | 0.2768 | 2020-09-04 | 2022-08-30 | 100% | 13% |  |
| 36 | Design and DPR Preparation of<br>218km roads in Pathanamthitta | G.O.(Rt)No.1389/<br>2020/LSGD | Completed   | 0.3074 | 0.3074 | 0.3074 | 2020-10-21 | 2022-08-30 | 100% | 58% |  |
| 37 | Soil Investigation in Pathanamthitta 3<br>Bridges              | G.O.(Rt.)No.234/2<br>021/LSGD | Completed   | 0.06   |        |        | 0000-00-00 | 0000-00-00 | 100% | 0%  |  |

## KOTTAYAM

| SI No | Name of Work   | AS No                         | Status             | AS Amt. | Tendered Amt. | Contract Amt. | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Remarks |
|-------|--|-------------------------------|--------------------|---------|---------------|---------------|----------------|-----------------|------------------|------------------|---------|
| 1     | Improvement of Girideepam Kadathukadavu Road in Kottayam District                                  | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 1.75    | 1.2935        | 1.2392        | 2020-10-05     | 2022-07-15      | 100%             | 68%              |         |
| 2     | Improvement of Pathinanchilkadavu Illikkal road in Kottayam Municipality in Kottayam District      | G.O.(Rt.)No.224/2<br>020/P&EA | Under Construction | 4       | 2.9446        | 2.9301        | 2020-10-28     | 2022-10-30      | 60%              | 58%              |         |
| 3     | Improvement of Kunnumpuram Mahilasamajam Road in Thiruvrppu GP in Kottayam District                | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 1.84    | 1.3434        | 1.3247        | 2020-10-13     | 2022-03-30      | 100%             | 74%              |         |
| 4     | Renovation of Kavanathinkara Manchira Road in Aymanam GP in Kottayam District                      | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 0.93    | 0.6712        | 0.6501        | 2020-10-28     | 2022-08-08      | 100%             | 53%              |         |
| 5     | Renovation of TV Puram Theeradesa Road in TV Puram GP in Kottayam District                         | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 3.5     | 2.9401        | 3.2337        | 2021-01-20     | 2022-10-30      | 100%             | 93%              |         |
| 6     | Malakunnam Kannanthrappadi road in Kurichy GP in Kottayam District                                 | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 1.19    | 0.8096        | 0.8898        | 2021-01-20     | 2022-02-15      | 100%             | 87%              |         |
| 7     | Olassa - Cherthalli Road in Kottayam   | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 1.21    | 1.0104        | 0.9829        | 2021-02-18     | 2023-02-18      | 35%              | 16%              |         |
| 8     | Kambanikadavu Pattarmadom Road in Kottayam   | G.O.(Rt.)No.404/2<br>020/P&EA | Completed          | 1.14    | 0.9258        | 0.8885        | 2021-05-04     | 0000-00-00      | 100%             | 78%              |         |
| 9     | Reconstruction of Madathilkadavu Mahilasamajam Kandathilpalli Road in Thiruvrpp GP, Ettumanoor LAC | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 1.45    | 1.2218        | 1.3046        | 2021-08-26     | 2023-01-26      | 6%               | 0%               |         |
| 10    | Cheepunkal - Malikayal Chira Road in Aymanam GP, Ettumanoor LAC, Kottayam District                 | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 1.48    | 1.2318        | 1.2195        | 2021-02-22     | 2022-12-22      | 40%              | 0%               |         |
| 11    | Reconstruction of LPS Mukkam Kollori Road in Chempu GP, Vaikom LAC, Kottayam district              | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 0.52    | 0.4275        | 0.4683        | 2021-11-06     | 2022-11-06      | 5%               | 0%               |         |

|    |   |                               |           |        |        |        |            |            |      |     |  |
|----|---|-------------------------------|-----------|--------|--------|--------|------------|------------|------|-----|--|
| 12 | Reconstruction of Govt. HS<br>Kochalivettam Road in Kumarakom<br>GP in Kottayam | G.O.(Rt.)No.62/20<br>21/P&EA  | Completed | 0.28   | 0.2259 | 0.2482 | 2021-10-18 | 2022-12-31 | 100% | 0%  |  |
| 13 | Investigation/ data collection -<br>Kottayam District                           | G.O.(Rt)No.115/2<br>020/P&EA  | Completed | 0.1208 | 0.1208 | 0.0951 | 2020-08-27 | 2022-08-30 | 100% | 13% |  |
| 14 | Soil Investigation in Kottayam 2<br>Bridges                                     | G.O.(Rt.)No.234/2<br>021/LSGD | Completed | 0.04   |        |        | 2020-08-02 | 2021-11-01 | 100% | 80% |  |



## IDUKKI

| SI No | Name of Work  | AS No                         | Status             | AS Amt. | Tendered Amt. | Contract Amt. | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Remarks |
|-------|---|-------------------------------|--------------------|---------|---------------|---------------|----------------|-----------------|------------------|------------------|---------|
| 1     | Improvement of Aashramam Pottanpady Road in Arakkulam GP, Idukki LAC, Idukki No.-18                 | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 1.63    | 1.3           | 1.1995        | 2021-11-06     | 2022-10-06      | 0%               | 0%               |         |
| 2     | Improvement of Adivaram-Ottalalpady city road in Rajakkad GP, Udumbanchola LAC, Idukki No:6         | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 2.37    | 2.2782        | 2.2511        | 2021-11-06     | 2023-03-31      | 70%              | 15%              |         |
| 3     | Improvement of Ambalappara-Kadapplackal Road in Upputhara GP, Peermade LAC, Idukki district-08      | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 1       | 0.8091        | 0.6709        | 2021-10-27     | 2023-03-31      | 55%              | 0%               |         |
| 4     | Improvement of Ellapalli tottam bhagom road Arakkulam GP, Idukki LAC, Idukki No. 20                 | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 1.93    | 1.556         | 1.308         | 2021-10-27     | 2022-12-27      | 50%              | 27%              |         |
| 5     | Improvement of Ellapally Chellikal Road in Arakkulam GP, Idukki LAC, Idukki No:19                   | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 4.33    | 3.4625        | 3.1298        | 2021-10-27     | 2022-12-27      | 15%              | 0%               |         |
| 6     | Improvement of Pazhaya Kochira road in Vandenmedu GP, Udumbanchola LAC, Idukki- No:26               | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 1.61    | 1.3136        | 1.2553        | 2021-10-27     | 2023-03-31      | 80%              | 35%              |         |
| 7     | Improvement of Vimalagiri- Enikuthu Road in Mariyapuram GP, Idukki LAC, Idukki No:29                | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 2.5     | 2.027         | 1.8182        | 2021-10-27     | 2023-03-31      | 75%              | 22%              |         |
| 8     | Improvement of Anachal Thokkupara-Acherikunnu Asramam road in Vellathooval GP, Devikulam LAC, Idukk | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 2.11    | 1.7144        | 1.5873        | 2021-11-26     | 2023-03-26      | 45%              | 0%               |         |
| 9     | Improvement of Murikkumthotti-Mathekkalpadi Shallyil Road in Rajakumari GP, Udumbanchola LAC, Idukk | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 1.22    | 0.9643        | 0.8645        | 2021-11-26     | 2023-03-31      | 35%              | 0%               |         |

|    |  |                           |                    |        |        |        |            |            |     |     |  |
|----|--|---------------------------|--------------------|--------|--------|--------|------------|------------|-----|-----|--|
| 10 | Improvement of Kattekkanam-Chelamoodu Road in Idukki-25, Karunapuram GP, Udumbanchola LAC            | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 0.925  | 0.685  | 0.737  | 2021-12-27 | 2023-05-30 | 6%  | 0%  |  |
| 11 | Improvement of Idinjamaal companypadi road Udumbanchola LAC Erattayar LSGI Idukki district           | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 7.245  | 5.1368 | 5.5859 | 2021-12-27 | 2023-03-31 | 80% | 36% |  |
| 12 | Improvement of Perumbankuthu 6th mile road in Mankulam GP, Devikulam LAC, Idukki No:9                | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 4.12   | 2.9094 | 3.1899 | 2021-12-29 | 2023-12-31 | 25% | 1%  |  |
| 13 | Improvement of Kurushupallipadi thannikandam Painavu road in Vazhathope GP, Idukki LAC, Idukki distr | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 3.3175 | 2.3698 | 2.6029 | 2021-12-29 | 2023-12-31 | 20% | 0%  |  |
| 14 | Improvement of Surianelly-Gundumala Road in Chinnakkanal GP, Devikulam LAC, Idukki District-12       | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 2.0475 | 1.4479 | 1.5891 | 2021-12-27 | 2023-12-31 | 6%  | 0%  |  |
| 15 | Reconstruction of Factorypadi Karintharuvi Road in Upputhara GP, Peerumedu LAC , Idukki District     | G.O.(Rt.)No.348/2021/P&EA | Under Construction | 3.22   | 2.6584 | 2.4446 | 2022-01-04 | 2023-05-30 | 25% | 0%  |  |
| 16 | Reconstruction of Sooryakanthikavala Old Post Office Road in Upputhara GP, Peerumedu LAC , Idukki Di | G.O.(Rt.)No.348/2021/P&EA | Under Construction | 1.3    | 1.0761 | 0.9889 | 2022-01-04 | 2023-05-30 | 10% | 0%  |  |
| 17 | Improvement of Panachikuzhi Road in Rajakkad GP, Udumbanchola LAC, Idukki District                   | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 4.42   | 3.3761 | 3.2497 | 2021-12-29 | 2023-03-31 | 75% | 7%  |  |
| 18 | Improvement of Padicip Plakkayam Kuttamudi Tribal colony road in Adimaly GP Devikulam LAC Idukki 05  | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 5.06   | 4.0507 | 3.4994 | 2022-02-11 | 2023-05-30 | 15% | 0%  |  |
| 19 | Improvement of Perikkankaval Kollamkulambadi Kaikavala Road in Vathikudy GP Idukki LAC idukki 27     | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 2.06   | 1.709  | 1.5678 | 2022-02-09 | 2023-03-31 | 70% | 28% |  |
| 20 | Improvement of Puthed Anoorthode Footbridge Road in Arakkulam GP, Idukki LAC in Idukki               | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 3.83   | 2.9954 | 2.9012 | 2022-03-24 | 2023-02-24 | 6%  | 0%  |  |

|    |  |                               |                                   |               |        |        |            |            |      |     |  |
|----|--|-------------------------------|-----------------------------------|---------------|--------|--------|------------|------------|------|-----|--|
| 21 | Balagram Anyarthulu Road<br>Udumbanchola LAC Pampadumpara<br>LSGI Idukki district                        | G.O.(Rt.)No.485/2<br>019/P&EA | Under<br>Construction             | 7.635572<br>2 | 5.8442 | 5.9702 | 0000-00-00 | 2023-12-31 | 10%  | 0%  |  |
| 22 | Naalumukku -Tunnel site road in<br>Udumbanchola LAC Erattayar LSGI<br>Idukki District                    | G.O.(Rt.)No.485/2<br>019/P&EA | Under<br>Construction             | 2.2615        | 1.6137 | 1.7247 | 2022-04-21 | 2023-05-30 | 40%  | 0%  |  |
| 23 | Improvement of Pallikudi city<br>Mangathupalam Road in Vathikudy<br>GP, Idukki LAC, Idukki District      | G.O.(Rt.)No.485/2<br>019/P&EA | Under<br>Construction             | 2.7           | 2.1475 | 1.9673 | 2022-04-26 | 2023-12-31 | 10%  | 0%  |  |
| 24 | Rehabilitation of Kannamplackalpathi<br>Puthenpalam Road in Nedumkandom<br>GP Udumbanchola LAC in Idukki | G.O.(Rt.)No.18/20<br>22/P&EA  | Under<br>Construction             | 1.13          | 0.8631 | 0.8221 | 2022-04-30 | 2023-05-30 | 10%  | 0%  |  |
| 25 | Thattekkallu Ponnezhuthan  | G.O.(Rt)No.300/2<br>022/P&EA  | AS Received                       | 3.25          | -      | -      | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 26 | Bhoomiyankulam Keshamini Road  | G.O.(Rt)No.300/2<br>022/P&EA  | AS Received                       | 1.9           | -      | -      | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 27 | Araikkalpathi Ambikavilasam<br>Estatepathi Road  | G.O.(Rt)No.300/2<br>022/P&EA  | AS Received                       | 5.65          | -      | -      | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 28 | 50th Mile Kallakuttykudi Mankulam<br>Road  | G.O.(Rt.)No.485/2<br>019/P&EA | Technical<br>Committee<br>Pending | 8             |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 29 | Mangathotti Kanakapuzha NR City<br>Road  | G.O.(Rt.)No.485/2<br>019/P&EA | Technical<br>Committee<br>Pending | 8             |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 30 | Investigation/ data collection -Idukki<br>District   | G.O.(Rt)No.115/2<br>020/P&EA  | Completed                         | 1.9027        | 1.9027 | 1.3148 | 2020-08-27 | 2022-08-30 | 100% | 33% |  |
| 31 | Design and DPR Preparation of<br>218km roads in Idukki   | G.O.(Rt)No.1389/<br>2020/LSGD | Completed                         | 0.6480        | 0.6480 | 0.6480 | 2020-10-21 | 2022-08-30 | 100% | 50% |  |
| 32 | Soil Investigation in Idukki 12 Bridges  | G.O.(Rt.)No.234/2<br>021/LSGD | Completed                         | 0.34          |        | 0.21   | 2021-08-02 | 0000-00-00 | 100% | 53% |  |
| 33 | Kallarmukku Bridge   | G.O.(Rt)No.221/2<br>020/P&EA  | DPR<br>Preparation                |               |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 34 | Panthrandam mile mezhukunel palam<br>and approach road   | G.O.(Rt)No.221/2<br>020/P&EA  | DPR<br>Preparation                |               |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |

|    |   |                              |                    |  |  |  |            |            |    |    |  |
|----|---|------------------------------|--------------------|--|--|--|------------|------------|----|----|--|
| 35 | Thooval Bridge                              | G.O.(Rt)No.221/2<br>020/P&EA | DPR<br>Preparation |  |  |  | 0000-00-00 | 0000-00-00 | 0% | 0% |  |
| 36 | Upputhodu-Ponnachipadi Bridge               | G.O.(Rt)No.221/2<br>020/P&EA | DPR<br>Preparation |  |  |  | 0000-00-00 | 0000-00-00 | 0% | 0% |  |
| 37 | Mulakuvalli-PulavanalluKokkarakkulam Bridge | G.O.(Rt)No.221/2<br>020/P&EA | DPR<br>Preparation |  |  |  | 0000-00-00 | 0000-00-00 | 0% | 0% |  |
| 38 | Moozhikkal-Thoppilkadavu Bridge             | G.O.(Rt)No.221/2<br>020/P&EA | DPR<br>Preparation |  |  |  | 0000-00-00 | 0000-00-00 | 0% | 0% |  |
| 39 | Maniyampara-Kanjiraveli Bridge              | G.O.(Rt)No.221/2<br>020/P&EA | DPR<br>Preparation |  |  |  | 0000-00-00 | 0000-00-00 | 0% | 0% |  |
| 40 | Hanging Bridge in 11th Ward                 | G.O.(Rt)No.221/2<br>020/P&EA | DPR<br>Preparation |  |  |  | 0000-00-00 | 0000-00-00 | 0% | 0% |  |
| 41 | Chittoor-Madathinkadavu                     | G.O.(Rt)No.221/2<br>020/P&EA | DPR<br>Preparation |  |  |  | 0000-00-00 | 0000-00-00 | 0% | 0% |  |
| 42 | OlamattomThekkumbhagomkadavu bridge         | G.O.(Rt)No.221/2<br>020/P&EA | DPR<br>Preparation |  |  |  | 0000-00-00 | 0000-00-00 | 0% | 0% |  |

## ERNAKULAM

| SI No | Name of Work  | AS No                         | Status             | AS Amt. | Tendered Amt. | Contract Amt. | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Remarks |
|-------|---|-------------------------------|--------------------|---------|---------------|---------------|----------------|-----------------|------------------|------------------|---------|
| 1     | Up gradation of Pannikuzhy Kavumthazham Road in Ernakulam   | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 1.81    | 1.42          | 1.25          | 2020-09-18     | 2022-02-10      | 100%             | 77%              |         |
| 2     | Rehabilitation of Pavamkulangara Kannankulangara Road in Thrippunithura Municipality in Ernakulam | G.O.(Rt.)No.224/2<br>020/P&EA | Under Construction | 1.32    | 0.97          | 0.95          | 2020-10-05     | 2022-12-31      | 93%              | 41%              |         |
| 3     | Upgradation of Vayalodam Thadikkadavu Road in Ernakulam District                                  | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 1.38    | 0.914         | 0.9138        | 2020-10-28     | 2022-08-30      | 100%             | 72%              |         |
| 4     | Renovation of Valavazhi Road in Angamaly Municipality in Ernakulam District                       | G.O.(Rt.)No.224/2<br>020/P&EA | Under Construction | 0.87    | 0.658         | 0.648         | 2020-10-05     | 2022-08-30      | 0%               | 0%               |         |
| 5     | Rehabilitation of Paduavathil Police Station Road in Kadungalloor GP in Ernakulam                 | G.O.(Rt.)No.224/2<br>020/P&EA | Under Construction | 0.66    | 0.5006        | 0.4947        | 2020-10-05     | 2022-11-30      | 0%               | 0%               |         |
| 6     | Up gradation of Kadungalloor Masjid road in Ernakulam   | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 0.72    | 0.481         | 0.4809        | 2020-09-28     | 2022-03-30      | 100%             | 65%              |         |
| 7     | Up gradation of Anicadu Pravidakunnu Road in Ernakulam  | G.O.(Rt.)No.224/2<br>020/P&EA | Under Construction | 1.3     | 1.0883        | 1.075         | 2020-10-05     | 2022-06-30      | 93%              | 81%              |         |
| 8     | Construction of Udumpuzha Chempassery Road in Ernakulam   | G.O.(Rt.)No.224/2<br>020/P&EA | Under Construction | 1.03    | 0.7666        | 0.739         | 2020-10-24     | 2023-03-30      | 13%              | 0%               |         |
| 9     | Renovation of Okkal Juma masjid Road in Okkal GP in Ernakulam                                     | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 0.166   | 0.1409        | 0.1318        | 2020-11-04     | 2022-03-31      | 100%             | 89%              |         |
| 10    | Reconstruction of BJP Kadavu Road in Ernakulam District   | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 0.12    | 0.10          | 0.0928        | 2020-09-29     | 2022-03-31      | 100%             | 82%              |         |
| 11    | Rehabilitation of St.Mary's Swaraj road in Kumbalangi G P in Ernakulam                            | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 0.53136 | 0.501         | 0.501         | 2020-10-05     | 2022-05-15      | 100%             | 51%              |         |
| 12    | Panjamkavala road ward-18 in Chendamangalam GP, North Paravoor District, Ernakulam District.      | G.O.(Rt.)No.404/2<br>020/P&EA | Completed          | 1.34    | 1.0426        | 0.997         | 2021-05-04     | 2022-03-01      | 100%             | 74%              |         |

|    |   |                               |                       |        |        |        |            |            |      |     |  |
|----|---|-------------------------------|-----------------------|--------|--------|--------|------------|------------|------|-----|--|
| 13 | Improvement of Edatod Palli Basilica Road in Angamaly Municipality in Ernakulam district              | G.O.(Rt.)No.62/20<br>21/P&EA  | Completed             | 0.52   | 0.4116 | 0.4039 | 2021-07-23 | 2022-05-30 | 100% | 88% |  |
| 14 | Construction of Musiris Puzhayoram Road ward 4 in Chendamangalam GP in Ernakulam                      | G.O.(Rt.)No.404/2<br>020/P&EA | Under<br>Construction | 1      | 0.8399 | 0.9156 | 2021-10-27 | 2022-11-30 | 6%   | 0%  |  |
| 15 | Nadakavu Ethiyerakavu Road in Vazhakulam GP, Kunnathunadu LAC in Ernakulam district                   | G.O.(Rt.)No.62/20<br>21/P&EA  | Under<br>Construction | 0.41   | 0.2877 | 0.3161 | 2021-10-27 | 2023-02-27 | 30%  | 0%  |  |
| 16 | Upgradation of Kallanchery Tharasseri Road in Kumbalangy GP Kochi LAC in Ernakulam District           | G.O.(Rt.)No.18/20<br>22/P&EA  | Under<br>Construction | 3.1    | 2.5728 | 2.83   | 2022-07-23 | 2023-04-30 | 6%   | 5%  |  |
| 17 | Upgradation of Thiruvaniyoor Meppadam Road in Thiruvaniyoor GP Kunnathunadu LAC in Ernakulam District | G.O.(Rt.)No.18/20<br>22/P&EA  | Under<br>Construction | 3.42   | 2.5597 | 2.6811 | 2022-07-14 | 2023-04-30 | 6%   | 0%  |  |
| 18 | Sahi Rubber Ambalamukku Kattuman Road   | G.O.(Rt)No.300/2<br>022/P&EA  | Tender<br>Process     | 1.7    | -      | -      | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 19 | Investigation/ data collection - Ernakulam District   | G.O.(Rt)No.115/2<br>020/P&EA  | Completed             | 0.2057 | 0.2057 | 0.1526 | 2020-08-27 | 2022-08-30 | 100% | 19% |  |
| 20 | Soil Investigation in Ernakulam 9 Bridges   | G.O.(Rt.)No.234/2<br>021/LSGD | Completed             | 0.275  |        |        | 0000-00-00 | 0000-00-00 | 100% | 0%  |  |
| 21 | Construction of kaipettipalam   | G.O.(Rt)No.221/2<br>020/P&EA  | DPR<br>Preparation    |        |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |
| 22 | Construction of Varatupadi Colony padi palam  | G.O.(Rt)No.221/2<br>020/P&EA  | DPR<br>Preparation    |        |        |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |

## THRISSUR

| SI No | Name of Work   | AS No                         | Status             | AS Amt. | Tendered Amt. | Contract Amt. | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Remarks |
|-------|--|-------------------------------|--------------------|---------|---------------|---------------|----------------|-----------------|------------------|------------------|---------|
| 1     | Rehabilitation of Thandilam Manali Kecheri Road in Thrissur  | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 5       | 3.6692        | 3.6479        | 2020-09-23     | 2022-11-18      | 100%             | 60%              |         |
| 2     | Improvement of Chittanda Padinjattumuri Road in Thrissur   | G.O.(Rt.)No.224/2<br>020/P&EA | Completed          | 6.72    | 5.4           | 5.09          | 2020-09-23     | 2022-11-28      | 100%             | 55%              |         |
| 3     | Chillukarankunnu road in Punnayurkulam GP, Guruvayoor LAC, Thrissur District.                        | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 0.96    | 0.7093        | 0.6754        | 2021-07-28     | 2023-02-15      | 10%              | 17%              |         |
| 4     | Kuranchery Nayarangadi road Kallampara colony in Thrissur  | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 12.5    | 9.8568        | 9.8285        | 2021-05-04     | 2023-03-31      | 60%              | 31%              |         |
| 5     | Improvement of Karoorchira Anjlangadi Road in Thrissur district                                      | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 1.95    | 1.5563        | 1.6963        | 2021-11-06     | 2023-03-31      | 35%              | 3%               |         |
| 6     | Rehabilitation of Paris Road in Kandanaserry GP in Thrissur district                                 | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 1.7     | 1.3425        | 1.4642        | 2021-11-06     | 2023-03-31      | 30%              | 3%               |         |
| 7     | Improvement of Puthiyakavu Pozhankavu Road in Thrissur   | G.O.(Rt.)No.404/2<br>020/P&EA | Completed          | 0.75    | 0.6129        | 0.6734        | 2021-10-27     | 2022-09-05      | 100%             | 93%              |         |
| 8     | Rehabilitation and reconstruction of Ex-Servicemen Colony Centre Road in Athirappally GP in Thrissur | G.O.(Rt.)No.62/20<br>21/P&EA  | Under Construction | 2.6     | 1.9077        | 2.044         | 2021-10-27     | 2023-02-28      | 60%              | 47%              |         |
| 9     | Kuzhur Iranikulam Indira Gandhi Road   | G.O.(Rt.)No.300/2<br>022/P&EA | Tender Process     | 3.38    | -             | -             | 0000-00-00     | 0000-00-00      | 0%               | 0%               |         |
| 10    | Chottilappara Bridge   | G.O.(Rt.)No.221/2<br>020/P&EA | Submitted for AS   | 2.75    | -             | -             | 0000-00-00     | 0000-00-00      | 0%               | 0%               |         |
| 11    | Investigation/ data collection - Thrissur District   | G.O.(Rt.)No.115/2<br>020/P&EA | Completed          | 0.3854  | 0.3854        | 0.2802        | 2020-08-27     | 2022-08-30      | 100%             | 13%              |         |
| 12    | Thali Viruttanam Road  | G.O.(Rt.)No.221/2<br>020/P&EA | DPR Preparation    |         |               |               | 0000-00-00     | 0000-00-00      | 0%               | 0%               |         |

## WAYANAD

| SI No | Name of Work   | AS No                         | Status             | AS Amt.       | Tendered Amt. | Contract Amt. | Agreement Date | Completion Date | Phy. Progress(%) | Fin. Progress(%) | Remarks |
|-------|--|-------------------------------|--------------------|---------------|---------------|---------------|----------------|-----------------|------------------|------------------|---------|
| 1     | Chakram colony road in Wayanad   | G.O.(Rt.)No.404/2<br>020/P&EA | Completed          | 0.93          | 0.758         | 0.6821        | 2021-02-16     | 2022-01-24      | 100%             | 65%              |         |
| 2     | Maravayal Chathothu road in Wayanad  | G.O.(Rt.)No.404/2<br>020/P&EA | Under Construction | 1.6           | 1.335         | 1.2127        | 2021-02-16     | 2023-03-31      | 35%              | 0%               |         |
| 3     | Improvement of Cheriyaankolli - Kalluvettumthazhe in Padinjarethara GP in Kalpetta LAC Wayanad-09    | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 1.44          | 1.09          | 1.0591        | 2021-11-06     | 2022-12-06      | 16%              | 0%               |         |
| 4     | Improvement of Ediyamvayal - Pinangodu road in Pozhuthana GP in Kalpetta LAC Wayanad 04              | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 2.22          | 1.6774        | 1.5423        | 2021-06-22     | 2023-01-31      | 90%              | 0%               |         |
| 5     | Improvement of Erumatherivu - Choottakadavu road in Mananthavdy GP in Mananthavady LAC Wayanad-13    | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 2.612776<br>8 | 1.7896        | 1.9682        | 2022-03-21     | 2023-01-21      | 10%              | 0%               |         |
| 6     | Improvement of Karlad - Manjoora road in Thariyode GP in Kalpetta LAC Waynad-05                      | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 1.89          | 1.4417        | 1.3084        | 2021-10-27     | 2023-03-27      | 38%              | 0%               |         |
| 7     | Improvement of Kuppadithara -Millu mukku kurumani road in Padinjarethara GP in Kalpetta LAC Waynad-0 | G.O.(Rt.)No.485/2<br>019/P&EA | Completed          | 1.45          | 1.10          | 1.10          | 2021-10-27     | 2022-06-27      | 100%             | 54%              |         |
| 8     | Improvement of Kottathara - Kakkanchal Thekkumthara Road in Kottathara GP in Kalpetta LAC - Waynad-0 | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 2.74          | 2.2526        | 2.2526        | 2021-10-27     | 2022-12-27      | 33%              | 0%               |         |
| 9     | Improvement of Varayad - Thekkumpadi Road Muttil GP in Kalpetta LAC Waynad-02                        | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 1.87          | 1.53          | 1.50          | 2021-02-26     | 2022-08-26      | 48%              | 3%               |         |
| 10    | Improvement of Chundel - Chundel estate - Pappala Anoth Road in Chundel GP in Kalpetta LAC- Wayanad- | G.O.(Rt.)No.485/2<br>019/P&EA | Under Construction | 5.661         | 4.3236        | 3.8668        | 2021-06-22     | 2023-02-25      | 78%              | 48%              |         |



|    |  |                           |                    |      |        |        |            |            |      |     |  |
|----|--|---------------------------|--------------------|------|--------|--------|------------|------------|------|-----|--|
| 11 | Improvement of MH Nagar - Cholapuram road in Vengappally GP in Kalpetta LAC Waynad-06              | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 2.4  | 1.8558 | 1.6335 | 2021-10-27 | 2023-01-31 | 90%  | 0%  |  |
| 12 | Improvement of Thazhe Arappetta Mankunnu Road in Moopainadu GP in Kalpetta LAC in Wayanad district | G.O.(Rt.)No.62/2021/P&EA  | Under Construction | 4.2  | 3.274  | 3.0978 | 2021-08-02 | 2023-03-31 | 33%  | 2%  |  |
| 13 | Rehabilitation of Thazhathangadi -Thanitheruvu Road in Pulpally GP in Wayanad                      | G.O.(Rt.)No.62/2021/P&EA  | Completed          | 1.2  | 0.9441 | 0.9191 | 2021-08-02 | 2022-07-15 | 100% | 82% |  |
| 14 | Improvement of Varayal - Melevarayal Road in Thanival GP in Mananthavady LAC Waynad-18             | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.34 | 1.0106 | 0.979  | 2021-08-02 | 2022-12-02 | 33%  | 5%  |  |
| 15 | Improvement of Kattimoola Aroola Kolathada Road in Thavinjal GP in Mananthavady LAC Wayanad 19     | G.O.(Rt.)No.485/2019/P&EA | Completed          | 2.79 | 2.1266 | 2.0662 | 2021-11-06 | 2022-11-06 | 100% | 74% |  |
| 16 | Improvement of Korome Karimbil Road in Thondernad GP of Mananthavdy LAC Wayanad 21                 | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 5.6  | 4.4587 | 4.2993 | 2021-11-06 | 2022-10-06 | 6%   | 0%  |  |
| 17 | Improvement of Orappu Evanarikulam Kattimoola Road in Mananthavadi LAC Thanival Wayanad 20         | G.O.(Rt.)No.485/2019/P&EA | Completed          | 3.45 | 2.6093 | 2.5173 | 2021-11-06 | 2022-10-06 | 100% | 65% |  |
| 18 | Improvement of Puthiyedam Makkimala Road in Thavinjal GP in Mananthavady LAC of Wayanad 16         | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 3.89 | 2.902  | 2.813  | 2021-11-06 | 2022-12-06 | 33%  | 0%  |  |
| 19 | Improvement of 44th mile Makkimala Road in Mananthavady LAC, Thanival LSGI, Wayanad 17             | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 3.09 | 2.39   | 2.3545 | 2021-11-17 | 2022-12-17 | 33%  | 0%  |  |
| 20 | Improvement of Panamaram Keenjukadavu Palakunnu Road Mananthavady LAC, Panamaram LSGI, Wayanad 01  | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 6.22 | 4.8684 | 4.7356 | 2021-11-17 | 2022-12-17 | 16%  | 6%  |  |
| 21 | Improvement of Pilakavu Pancharakolli Road in Mananthavady LAC, Mananthavady LSGI, Wayanad 15      | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 3.09 | 2.3803 | 2.3223 | 2021-11-17 | 2023-01-31 | 90%  | 0%  |  |

|    |   |                           |                    |           |         |        |            |            |      |     |  |
|----|---|---------------------------|--------------------|-----------|---------|--------|------------|------------|------|-----|--|
| 22 | Improvement of Kollikandam Kunneri Nelom Road in Thondernadu GP in Mananthavady LAC in Wayanad 22 | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.1275    | 0.7727  | 0.8213 | 2021-12-27 | 2022-10-06 | 6%   | 0%  |  |
| 23 | Improvement of Valliurkavu Varadimoola Road in Mananthavady GP Mananthavady LAC in Wayanad 10     | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.45      | 1.1336  | 0.9963 | 2022-02-17 | 2022-12-17 | 13%  | 25% |  |
| 24 | Improvement of Vilanilam Pilakavu road in Mananthavdy GP Mananthavady LAC Wayanad 14              | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 3.89      | 3.0935  | 2.787  | 2022-02-17 | 2022-12-17 | 58%  | 0%  |  |
| 25 | Improvement of Thannikkal Payyampally Road in Mananthavady LAC in Wayanad 12                      | G.O.(Rt.)No.485/2019/P&EA | Under Construction | 1.9861554 | 1.46058 | 1.5557 | 2022-03-26 | 2023-02-26 | 0%   | 0%  |  |
| 26 | Improvement of Kalpetta Town Jilla Stadium Road in Kalpetta LAC in Wayanad district               | G.O.(Rt.)No.348/2021/P&EA | Under Construction | 2.97      | 2.1802  | 2.3231 | 2022-03-21 | 2023-03-21 | 25%  | 0%  |  |
| 27 | Eranjoli Pulikkal Road in Kaniyambatta GP Kalpetta LAC in Wayanad district                        | G.O.(Rt.)No.18/2022/P&EA  | Under Construction | 3.38      | 2.7585  | 2.6115 | 2022-05-18 | 2023-05-18 | 0%   | 0%  |  |
| 28 | Improvement of Changadakadavu Chamadipoyi Road in Edavaka GP Mananthavady LAC in Wayanad district | G.O.(Rt.)No.18/2022/P&EA  | Under Construction | 3.04      | 2.3899  | 2.1842 | 2022-06-14 | 2023-06-14 | 6%   | 0%  |  |
| 29 | Investigation/ data collection - Wayanad District   | G.O.(Rt)No.115/2020/P&EA  | Completed          | 0.7243    | 0.7243  | 0.5436 | 2020-08-27 | 2022-08-30 | 100% | 27% |  |
| 30 | Design and DPR Preparation of 218km roads in Wayanad  | G.O.(Rt)No.1389/2020/LSGD | Completed          | 0.3979    | 0.3979  | 0.3979 | 2020-10-21 | 2022-08-30 | 100% | 92% |  |
| 31 | CBR Investigation of Roads in Wayanad   | G.O.(Rt)No.2257/2020/LSGD | Completed          | 0.0546    |         |        | 2020-02-10 | 0000-00-00 | 100% | 87% |  |
| 32 | Topographic Survey for roads in Wayanad   | G.O.(Rt)1669/2020/LSGD    | Completed          | 0.0246    |         |        | 2020-01-15 | 0000-00-00 | 100% | 62% |  |
| 33 | 41 mile varayal bridge  | G.O.(Rt)No.221/2020/P&EA  | DPR Preparation    |           |         |        | 0000-00-00 | 0000-00-00 | 0%   | 0%  |  |

## 25. LIST OF BRIDGES FOR WHICH DPR TO BE PREPARED

| Sl. No. | District  | LAC          | Local Body       | Name of bridge                                      | Type of Bridge   | Approximate span | Remarks   |
|---------|-----------|--------------|------------------|---|------------------|------------------|---|
| 1       | Alappuzha | Chengannur   | Mannar Gp        | Moorthitta Mukkatheri Vazhayi(Chackittapady Bridge) | RCC              | 12               | Design work in progress   |
| 2       | Alappuzha | Kuttanad     | Neelamperoor GP  | Naduvath moon bridge                                | RCC              | 20               | Design work in progress   |
| 3       | Alappuzha | Kuttanad     | Nellar GP        | Nellanickal Ambalam Road                            | RCC              | 35               | Design work in progress   |
| 4       | Alappuzha | Kuttanad Gp  | Muttar GP        | SNDP to Nadukkodu                                   | RCC              | 15               | Design work in progress   |
| 5       | Alappuzha | Kuttanad Gp  | Muttar GP        | SNDP to Vadaparambu Culvert Road                    | RCC              | 10.5             | Design work in progress   |
| 6       | Alappuzha | Chenganoor   | Chennithala GP   | Vallamkadavu Chillithuruth Swamithara Road          | RCC              | 21               | Design work in progress   |
| 7       | Idukki    | Udumbumchola | Nedumkandam      | Kallarmukku Bridge                                  | RCC              | 12.5             | Design work in progress   |
| 8       | Idukki    | Devikulam    | Adimaly          | Pantrandam mile mezhukunel palam and approach road  | RCC              | 40.3             | Design work in progress   |
| 9       | Idukki    | Udumbumchola | Nedumkandam      | Thooval Bridge                                      | RCC              | 22               | Design work in progress   |
| 10      | Idukki    | Idukki       | Vathikudy GP     | Upputhodu-Ponnachipadi Bridge                       | RCC              | 13.3             | Design work in progress   |
| 11      | Idukki    | Idukki       | Vazhathoppu GP   | Mulakuvalli-PulavanalluKokkarakkulam Bridge         | RCC              | 10               | Design work in progress   |
| 12      | Idukki    | Peermedu     | Peruvanthanam GP | Moozhikkal-Thoppilkadavu Bridge                     | RCC              | 38               | Design work in progress   |
| 13      | Idukki    | Devikulam    | Adimaly GP       | Maniyampara-Kanjiraveli Bridge                      | Steel footbridge | 78               | Tendered 3 times. No response. Decided to prepare DPR in-house. |
| 14      | Idukki    | Devikulam    | Munnar GP        | Hanging Bridge in 11th Ward                         | Steel footbridge | 60               | Tendered 3 times. No response. Decided to prepare DPR in-house. |

|    |                |               |                 |  |                  |      |   |
|----|----------------|---------------|-----------------|--|------------------|------|---|
| 15 | Idukki         | Thodupuzha    | Manakkad GP     | Chittoor-Madathinkadavu  | Steel footbridge | 55   | Tendered 3 times. No response. Decided to prepare DPR in-house.               |
| 16 | Idukki         | Thodupuzha    | Idavetty GP     | OlamattomThekkumbhagomkadavu bridge                                      | Steel footbridge | 60   | Tendered 3 times. No response. Decided to prepare DPR in-house.               |
| 17 | Ernakulam      | Kalamaserry   | Karimalur       | Construction of kaipettipalam  | RCC              | 28   | Design work in progress   |
| 18 | Ernakulam      | Kalamaserry   | Alangad GP      | Construction of Varatupadi Coloni padi palam                             | RCC              | 17   | Design work in progress   |
| 19 | Palakkad       | Nenmara       | Vadavannur GP   | Allambalampalam road   | RCC              | 55   | Design work in progress   |
| 20 | Thrissur       | wadakkanchery | Varavoor GP     | Thali Viruttanam Road  | RCC              | 13   | Design work in progress   |
| 21 | Wayanad        | Mananthavady  | Thovihal GP     | 41 mile varayal bridge   | RCC              | 15   | Design work in progress   |
| 22 | Kannur         | Peravoor      | Aralam GP       | Manchuvadu bridge  | RCC              | 12   | Design work in progress   |
| 23 | Alappuzha      | Alappuzha     | Mannancherry GP | Mannancherry Jn Puthanparambu Thaikkavu Road                             | RCC              | 9.6  | Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km |
| 24 | Alappuzha      | Haripad       | Pallipad GP     | Anjilimoodu Sudheesh Bhavanam road                                       | RCC              | 10.2 | Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km |
| 25 | Pathanamthitta | Aranmula      | Mallapuzhaserry | Chakkittapadi korakodepadi road( kolakuzhy bridge)- walk way bridge      | RCC              | 8.6  | Bridge work taken up by other agency. Reported by EE PIU Kottayam             |
| 26 | Pathanamthitta | Thiruvalla    | Kalooopara      | Shastangal vakkayil kadavu thottipara( managed by irrigation department) | RCC              | 9.3  | Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km |
| 27 | Ernakulam      | Muvattupuzha  | Ayavana GP      | Suspension bridge at Keecherikadavu                                      | Steel footbridge | 66   | Bridge work taken up by other agency (PMGSY). Reported by EE PIU Thrissur     |

|    |           |               |                    |   |     |      |   |
|----|-----------|---------------|--------------------|---|-----|------|---|
| 28 | Ernakulam | Kalamaserry   | Eloor Municipality | Construction of pachamukku unthithodu palam and approach road | RCC | 13.5 | Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km |
| 29 | Ernakulam | Kothamangalam | Kuttampuzha        | Manikandanchal Vellaramkuthu St Colony road                   | RCC | 8.5  | Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km |
| 30 | Ernakulam | Kunnathuadu   | Thiruvaniyoor GP   | Thiruvaniyoor Mepadam Road                                    | RCC | 8.3  | No new Bridge required. Reported by EE PIU Thrissur.                          |
| 31 | Thrissur  | Manalur       | Choondal GP        | Chottilappara Bridge  | RCC | 12   | DPR prepared inhouse and submitted to RKI for AS                              |
