



## PROJECT MANAGEMENT UNIT-REBUILD KERALA INITIATIVE

### PROGRESS REPORT OF PROJECTS

As on 09/11/2023

## Contents


1. INTRODUCTION .....	3
2. OVERVIEW OF STATUS OF WORKS – AS WISE .....	4
3. CONSOLIDATED AS WISE STATUS .....	5
4. OVERVIEW OF STATUS OF WORKS – DISTRICT WISE .....	6
5. DISTRICT WISE STATUS OF PROJECTS .....	7
6. SOME PROJECT PHOTOS (BEFORE & AFTER) .....	8
7. LIST OF WORKS BASED ON PHYSICAL PROGRESS.....	21
8. DETAILED REPORT OF WORKS- AS WISE.....	28
9. DETAILED REPORT OF WORKS- DISTRICT WISE.....	54
10. LIST OF BRIDGES .....	78



## 1. INTRODUCTION

Between June 1 and 19 August 2018, our State of Kerala went through the worst ever floods in history since 1924. One sixth of the State's population — about 5.4 million of us, Keralites — were affected. The floods and the accompanying landslides were catastrophic in terms of loss of lives, livelihoods, property and infrastructure. Govt: of Kerala addressed the phenomena in a comprehensive and systematic way by formulating REBUILD KERALA DEVELOPMENT PROGRAMME, a Resilient Recovery Policy Framework and Action Plan for Shaping Kerala's Resilient, Risk-Informed Development and Recovery from 2018 Floods . The key sectors identified in the RKDP are:, Integrated Water Resource Management, Water Supply, Sanitation, Urban, Roads and Bridges, Transportation, Forestry, Agriculture, Animal Husbandry and Dairy Development, Fisheries, Livelihoods and Land. RURAL ROADS which are back bone to the rural economy were drastically affected by the flood and are given due consideration by Kerala Government. As a part of Rebuild Kerala Initiative, the Government constituted a Project Management Unit (PMU) under Local Self Government Department for the effective management of projects assigned to the department.

## 2. OVERVIEW OF STATUS OF WORKS – AS WISE

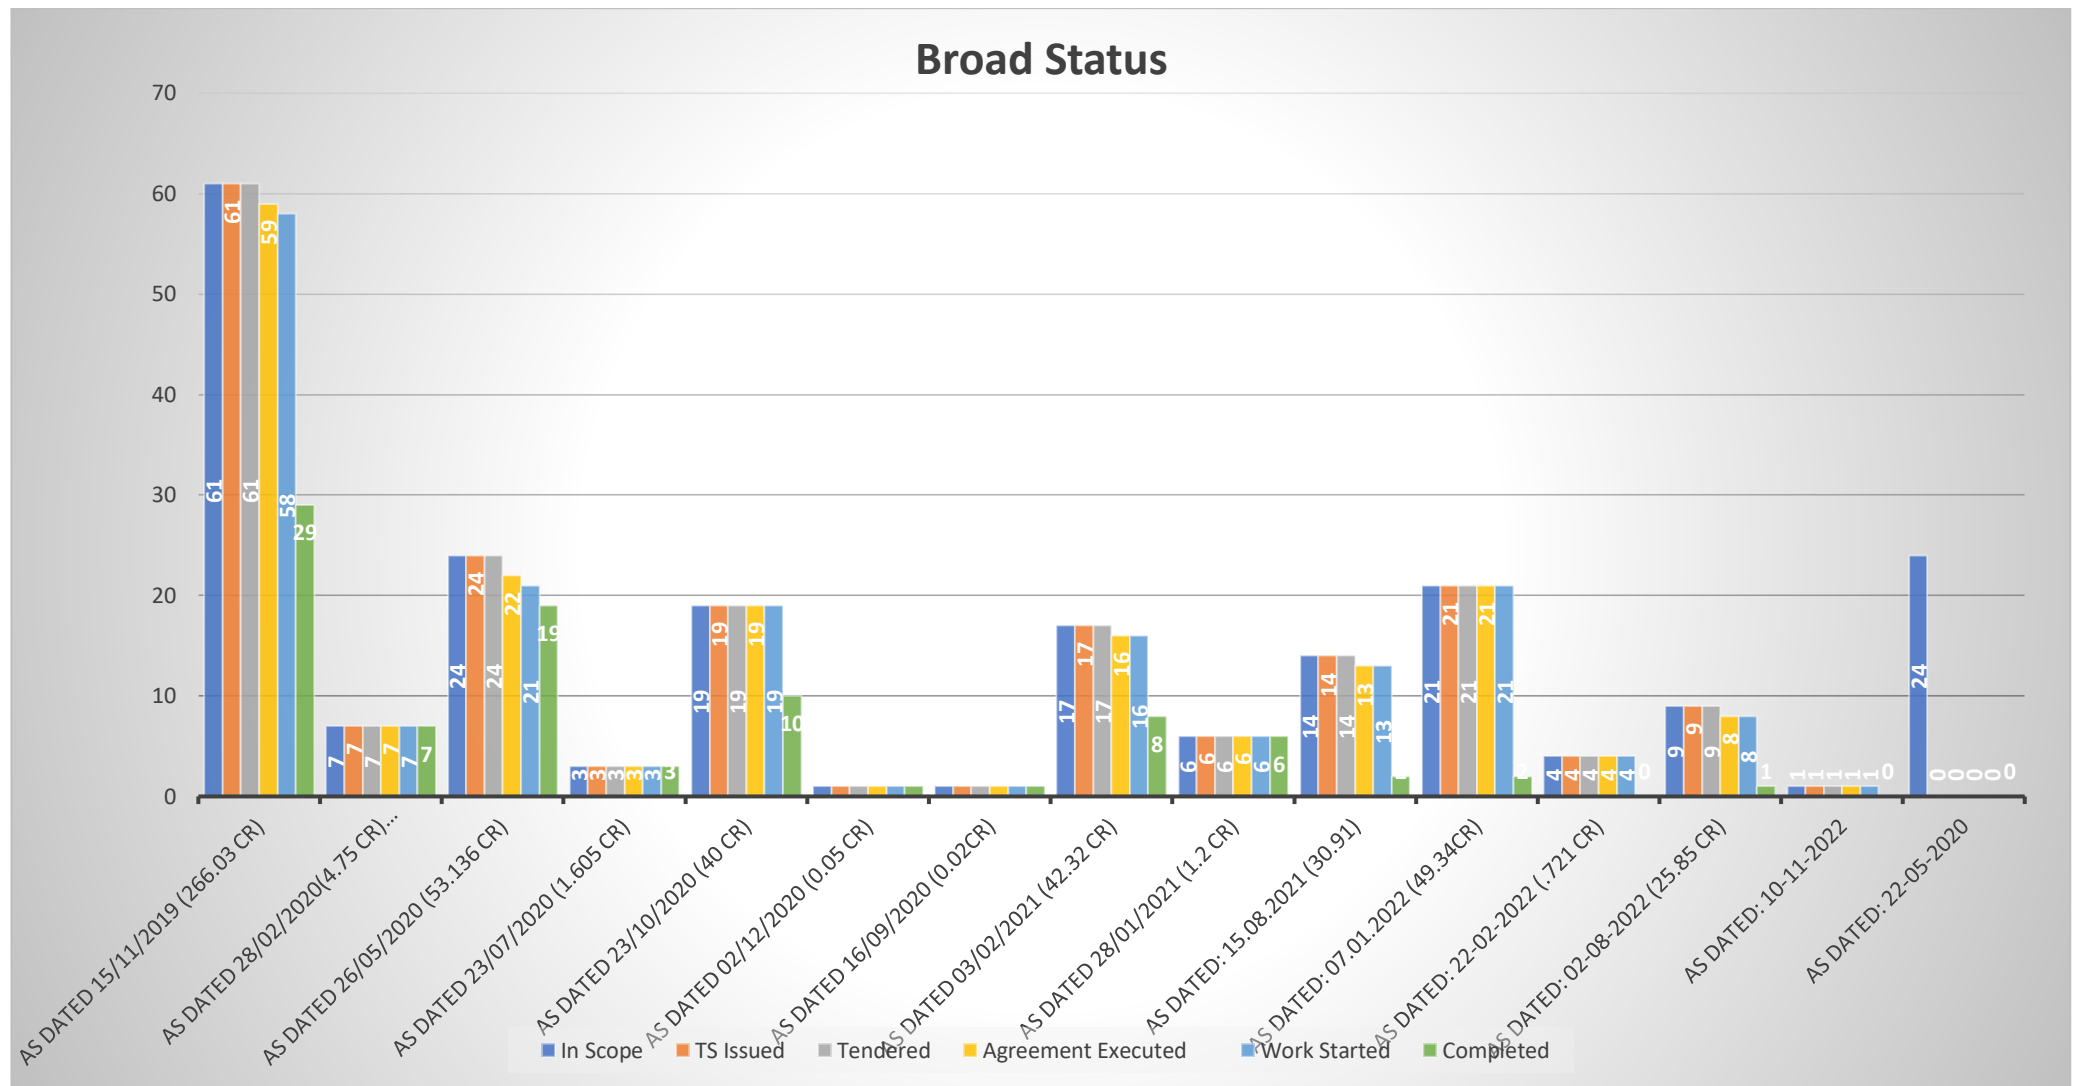


### 3. CONSOLIDATED AS WISE STATUS

Project Status (AS Wise Consolidated Numbers)																
Sl No	AS No	Description	AS Amount (Crores)	Actual Amount after savings	Total Nos	Dropped	In Scope	No TS Issued	Nos Tendered	Nos Tender Excess Approval Required	Nos Agreement Executed	Nos Work Started	Nos Completed	Tender Amount (cr)	Agreement Amount (cr)	Total Expenditure (Crore)
1	GO(R) No 485/2019/P&EA dated 15/11/2019,	Reconstruction of various LSG roads in DBMT mode in Pathanamthitta, Idukki and Wayanad districts-77 nos,	266.3055	201.33	77	16	61	61	61	2	59	58(1No. to be terminated)	29	133.54	123.5	64.82
2	G.O. (R) No. 115/2020/P&EA, Thiruvananthapuram, Dated 28/02/2020	Conducting investigation/ data collection of roads identified in 7 districts, AS Issued for 4.75 Crore, details as follows.	4.75	4.75	7	0	7	7	7	0	7	7	7	4.57	3.2	1.2422
3	G.O. (Rt.) No. 224/2020/P&EA, Thiruvananthapuram, Dated 26/05/2020	Rebuilding LSG Roads in 4 districts viz., Alappuzha, Kottayam, Ernakulam and Thrissur, Total AS Issued for Rs. 53.136 Crore, for 25 roads details as follows	53.136	53.136	25	1	24	24	24	1	22(1No. selection notice issued)	21(1 No. To be dropped)	19	39.89	38.84	35.22
4	G.O.(R)No. 1389/ 2020/ LSGD Dated, Thiruvananthapuram, 23/07/2020	Consultancy services for design and DPR preparation of flood affected roads in Pathanamthitta, Idukki and Wayanad districts, AS issued for 1.605 Crores, details as follows.	1.605	1.605	3	0	3	3	3	0	3	3	3	1.35	1.35	1.05
5	G.O. (Rt.) No. 404/2020/P&EA, Thiruvananthapuram, Dated 23/10/2020	Rebuilding LSG Roads in 5 districts viz., Alappuzha, Kottayam, Ernakulam, Thrissur and Wayanad, AS issued for Rs. 40 Core. Details as follows	40	40	21	2	19	19	19	0	19	19	10	30.98	31.26	16.11
6	GO (R) No. 62/2021/P&EA , Dated 03/02/2021	rebuilding 19 number of LSGD Roads in 6 districts viz., Pathanamthitta, Kottayam, Ernakulam, Alappuzha, Thrissur & Wayanad	42.32	42.32	19	2	17	17	17	0	16(1No. re-tendered)	16	8	30.74	31.5	17.38
7	G.O.(R)No. 2257/2020/LSGD dated 02.12.2020	CBR Investigation of Roads in Wayanad	0.0546	0.546	1	0	1	1	1	0	1	1	1			0.048
8	GO(R) No 234/2021/LSGD dated 28/01/2021	Soil Investigation for Bridges	1.2	1.2	6	0	6	6	6	0	6	6	6			0.33
9	GO(R) No 1669/2020/LSGD dated 16.09.2020	Topographic Survey for roads in Wayanad	0.0246	0.0246	1	0	1	1	1	0	1	1	1			0.015
10	G.O.(R)No. 348/2021/P&EA, 15.08.2021	rebuilding 14 LSG Roads in 4 districts viz., Alappuzha, Pathanamthitta, Idukki and Wayanad	30.91	30.91	14	0	14	14	14	1	13	13	2	23.36	23.51	8.62
11	G.O.(R)No. 18/2022/P&EA, 07.01.2022	rebuilding 22 number of LSGD Roads in 5 districts viz., Alappuzha, Pathanamthitta, Ernakulam, Idukki and	49.34	49.34	22	1	21	21	21	0	21	21	2	39.51	40.85	11.25
12	GO (R) No. 405/2022/LSGD, dt: TVM 22-02-2022	Engaging consultants for Designing bridges - 31 Nos	0.721	0.721	4	0	4	4	4	0	4	4	0	0.29	0.284	0
13	GO(R) No. 300/2022/P&EA , dt: 02/08/2022	9 roads			9	0	9	9	9	1	8	8	1	17.125	15.582	0.014
14	G.O.(R).No.422/2022/P&EA	Extension of Vayalodam Thadikkadavu Road			1	0	1	1	1	0	1	1	0	1.266	1.325	0.003
15	G.O.(R).No.221/2020/P&EA, dt: 22/05/2020	Reconstruction of flood damaged bridges and culverts			42	18	24	*Detailed list of bridges separately attached								0
<b>Totals</b>			<b>490.367</b>	<b>425.8826</b>	<b>252</b>	<b>40</b>	<b>212</b>	<b>188</b>	<b>188</b>	<b>5</b>	<b>181</b>	<b>179</b>	<b>89</b>	<b>322.621</b>	<b>311.201</b>	<b>156.1022</b>

Page 1

#### 4. OVERVIEW OF STATUS OF WORKS – DISTRICT WISE

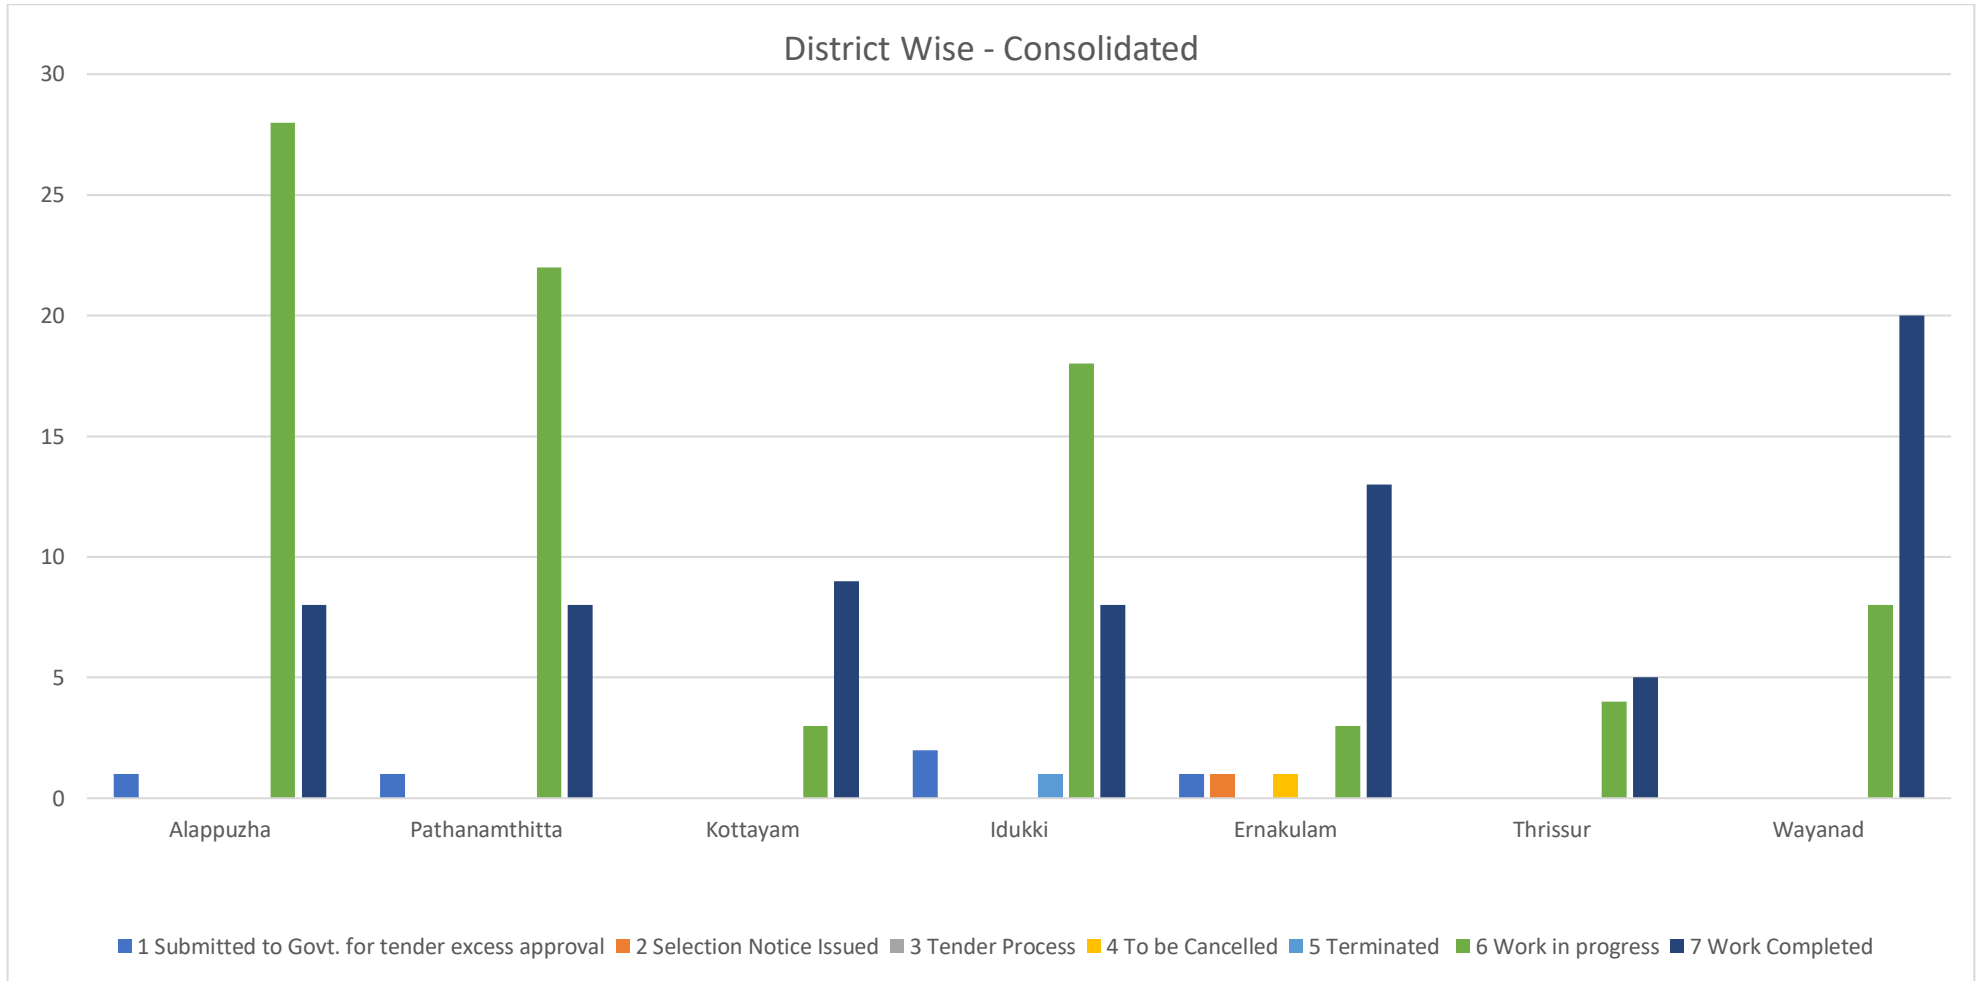

## 5. STATUS OF WORKS

### DISTRICT WISE CONSOLIDATED

SI No.	Description	Alappuzha	Pathanamthitta	Kottayam	Idukki	Ernakulam	Thrissur	Wayanad	Total
1	Submitted to Govt. for tender excess approval	1	1	0	2	1	0	0	5
2	Selection Notice Issued	0	0	0	0	1	0	0	1
3	Tender Process	1 (Re-tendered)	0	0	0	0	0	0	1
4	To be Cancelled	0	0	0	0	1	0	0	1
5	Terminated	0	0	0	1	0	0	0	1
6	Work in progress	28	22	3	18	3	4	8	86
7	Work Completed	8	8	9	8	13	5	20	71
	<b>Total</b>	<b>38</b>	<b>31</b>	<b>12</b>	<b>29</b>	<b>19</b>	<b>9</b>	<b>28</b>	<b>166</b>

## STATUS OF BRIDGES

District	Design Work in Progress	DPR Submitted to Govt.	AS Received and TS Required	Submitted to Govt.for tender excess	Total
Alappuzha	6	0	1	0	7
Idukki	8	2	0	0	10
Ernakulam	0	2	0	0	2
Thrissur	1	0	0	1	2
Palakkad	0	1	0	0	1
Wayanad	0	0	1	0	1
Kannur	0	1	0	0	1
<b>Total</b>	<b>15</b>	<b>6</b>	<b>2</b>	<b>1</b>	<b>24</b>




## STATUS OF OTHER WORKS

Sl No.	Description	G.O No.	Nos.	Status
1	Investigation/ data collection of roads in 7 districts	115/2020	7	Completed
2	Consultancy services for design and DPR preparation of roads	1389/2020	3	Completed
3	CBR Investigation of Roads in Wayanad	2257/2020	1	Completed
4	Soil Investigation for Bridges	234/2021	6	Completed
5	Topographic survey for roads in Wayanad	1669/2020	1	Completed
6	Consultancy services for design and DPR preparation of Bridges	405/2022	4	In progress
	<b>Total</b>		<b>22</b>	


6. Some Project Photos

## Reconstruction of AV Mukku Sharangakkavu Road in Alappuzha

Before work

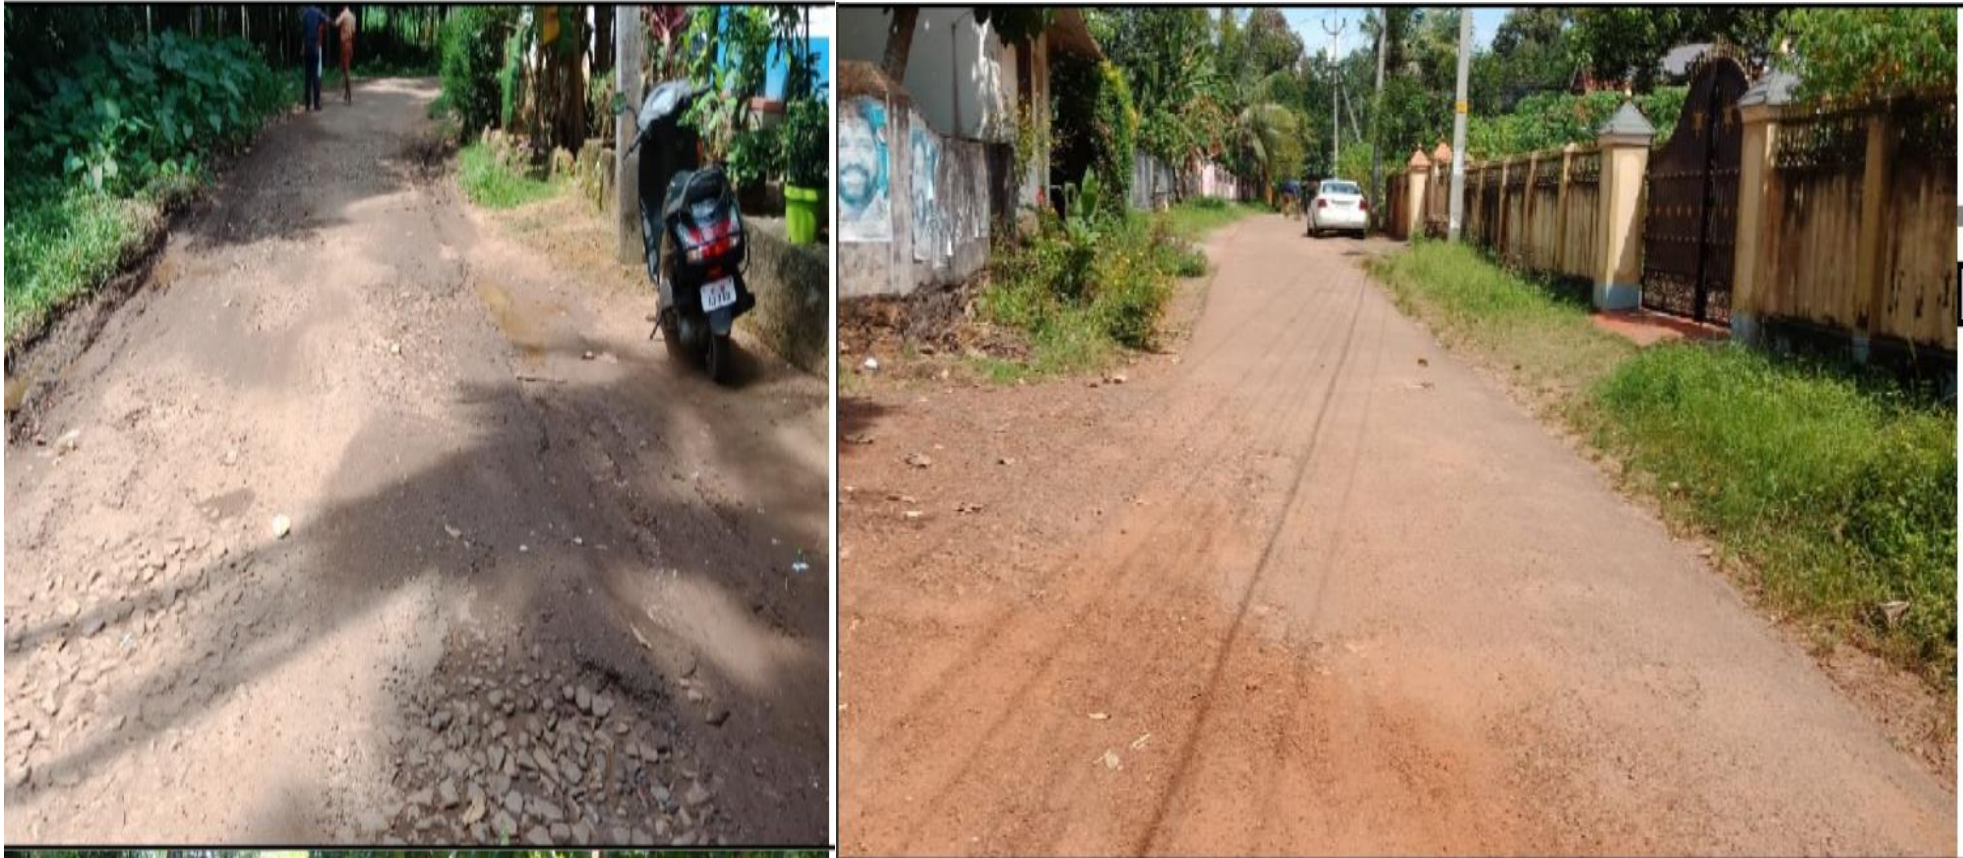

After Completion

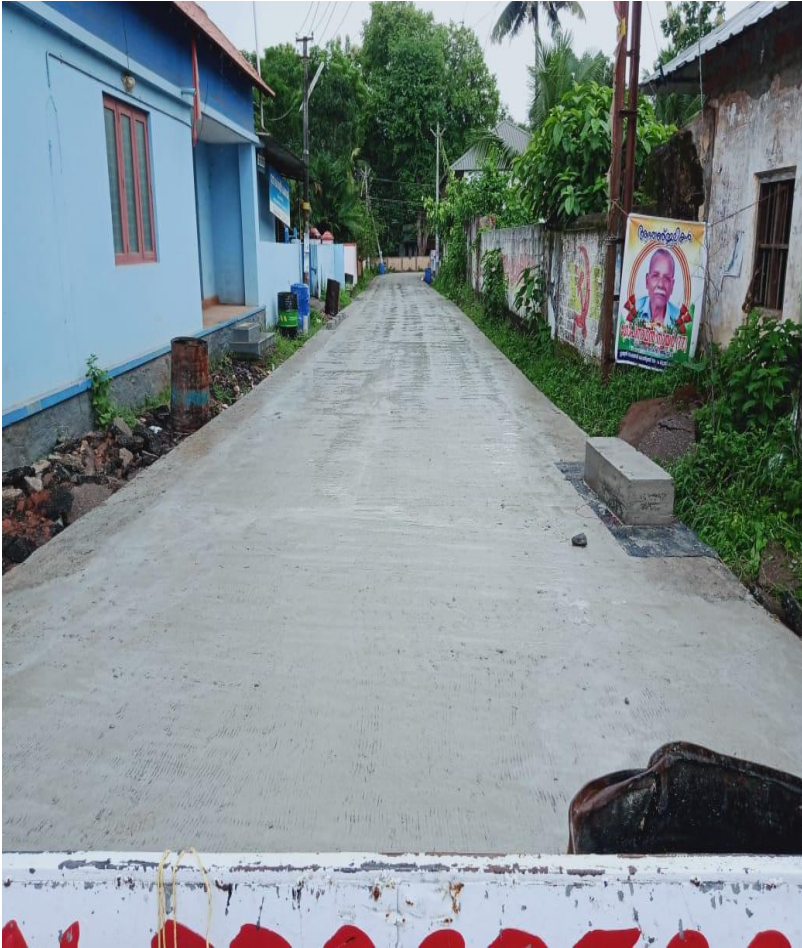

# Improvement of Pilakavu - Pancharakolli Road in Mananthavady LAC, Mananthavady LSGIs, Wayanad

Before Work



After Completion



## Improvement of Panachikuzhy Road in Rajakkad GP, Udumbanchola LAC, Idukki

Before Work



After Completion



# Improvement of Idinjamal companypadi road Udumbanchola LAC Erattayar LSGI Idukki district

Before Work





After Completion



## Renovation of Kulikkanpalam Shappupadi Road in Alappuzha

Before Work



After Completion



## 7. List of works based on Physical Progress

LIST OF COMPLETED WORKS					
SI No.	List of Works	District	LAC	Local Body	Length(Km)
1	Renovation of Kulikkanpalam - Shappumpadi Road	Alappuzha	Chengannur	Cheriyamad GP	1.4
2	Reconstruction of AV Mukku - Sharangakkavu Road	Alappuzha	Mavelikkara	Nooranad GP	1.48
3	Reconstruction of Pennukkara Canal Jn Nettuvaramcode Road	Alappuzha	Chengannur	Alappuzha GP	1.42
4	Upgradation of Madathekkathil Chalukkar Road	Alappuzha	Chengannur	Mulakkuzhy GP	0.375
5	Upgradation of KE Carmel Pulickal Road	Alappuzha	Cherthala	Kanjikkuzhy GP	0.892
6	Reconstruction of Parakkavu Valakkuzhy Road	Pathanamthitta	Ranni	Ezhumattoor GP	1.75
7	Improvement of Girideepam Kadathukadavu Road	Kottayam	Kottayam	Vijayapuram GP	1.86
8	Improvement of Kunnumpuram Mahilasamajam Road	Kottayam	Ettumanoor	Thiruvappu GP	1
9	Renovation of Kavanattinkara Manchira Road	Kottayam	Ettumanoor	Aymanam GP	1.3
10	Renovation of TV Puram Theeradesa Road	Kottayam	Vaikom	TV Puram GP	3.79
11	Malakkunnam Kannanthrappadi Road	Kottayam	Changanassery	Kurichy GP	1.125

12	Improvement of Panachikkuzhy Road	Idukki	Udumbanchola	Rajakkad GP	5.1
13	Upgradation of Pannikkuzhy Kavumthazham Road	Ernakulam	Thrippunithura	Vaduvacode Puthencruz Gp	1.2
14	Upgradation of Vayalodam Thadikkadavu Road	Ernakulam	Kalamassery	Karimannoor GP	0.905
15	Upgradation of Kadungalloor Masjid Road	Ernakulam	Kalamassery	Kadungalloor GP	0.515
16	Renovation of Okkal Juma Masjid Road	Ernakulam	Perumbavoor	Okkal GP	0.165
17	Reconstruction of BJP Kadavu Road	Ernakulam	Perumbavoor	Okkal GP	0.18
18	Panjamkavala Road Ward 18	Ernakulam	Paravur	Chendamangalam GP	1.1
19	Improvement of Edathodu Palli Basilica Road	Ernakulam	Angamaly	Angamaly GP	1.04
20	Rehabilitation of Pavamkulangara Kannankulangara Road	Ernakulam	Thrippunithura	Thrippunithura GP	1.953
21	Upgradation of Anicadu Pravidakunnu Road	Ernakulam	Muvattupuzha	Avoly GP	1.166
22	Rehabilitation of Thandilam Manali Kecheri Road	Thrissur	Kunnamkulam	Velur GP	5
23	Improvement of Chittanda Padinjattumuri Road	Thrissur	Kunnamkulam	Erumappetti GP	5.4
24	Improvement of Puthiyakavu Pozhankavu Road	Thrissur	Kaippamangalam	Mathilakom GP	0.84
25	Chillukarankunnu Road	Thrissur	Guruvayur	Punnayurkulam GP	1.2
26	Rehabilitation and reconstruction of Ex-servicemen Colony centre road	Thrissur	Chalakkudy	Athirappilli GP	2.1
27	Chakram Colony Road	Wayanad	Kalpetta	Pozhuthana GP	0.83

28	Improvement of Kuppadithura Millumukku Kurumani Road	Wayanad	Kalpetta	Padinjarethara GP	1.5
29	Improvement of Chundel Chundel estate Pappala Anoth Road	Wayanad	Kalpetta	Vaithiry GP	5.4
30	Improvement of MH Nagar Cholapuram Road in Vengappally	Wayanad	Kalpetta	Vengappally	2.7
31	Rehabilitation of Thazhathangadi Thanitheruvu Road	Wayanad	Sulthan Bathery	Pulpally	1.33
32	Improvement of Kattimoola Aroola Kolathada Road	Wayanad	Mananthavady	Thavinhjal GP	3.7
33	Improvement of Orappu Evaanikkulam Kattimoola Road	Wayanad	Mananthavady	Thavinjal GP	4.5
34	Improvement of Pilakkavu Pancharakkolli Road	Wayanad	Mananthavady	Mananthavady GP	3.1
35	Improvement of Ediyamvayal Pinangodu Road	Wayanad	Kalpetta	Pozhuthana GP	2.4
36	Improvement of AC canal to Mankuzhy Road	Alappuzha	Kuttanad	Ramankary GP	0.8
37	Rehabilitation of Mithrappuzha Vayanasalapadi Vendoorpad	Alappuzha	Chengannur	Chengannur GP	2.78
38	Kanjikkalmukku Ganam theatre road	Alappuzha	Kayamkulam	Bharanikkavu GP	1.62
39	Improvement of Pathinanchil Kadavu Illikkal Road	Kottayam	Kottayam	Kottayam	2
40	Improvement of Idinjamala Companyyapadi road	Idukki	Udumbanchola	Erattayar GP	8.1
41	Improvement of Illappalli Thottambhagom Road	Idukki	Idukki	Arakkulam GP	1.45
42	Maravayal Chathothu Road	Wayanad	Kalpetta	Pozhuthana GP	1.29
43	Kottomonpara Melekottomonpara Road	Pathanamthitta	Konni	Seethathodu GP	1.79
44	Madukkamood Ayyappa Medical College Road	Pathanamthitta	Konni	Vadasserikkara GP	1

45	Reconstruction of Bangalamkadavu Valiyakulam Road	Pathanamthitta	Ranni	Vadasserikkara GP	2
46	Improvement of Thannithode Plantation Road	Pathanamthitta	Konni	Thannithode GP	4.32
47	Rehabilitation of Valiyaparambil Eettichuvadu Road	Pathanamthitta	Ranni	Pazhavangadi GP	1.33
48	Anthyalankavu Marthomapallipadi Karamvelipadi Road	Pathanamthitta	Aranmula	Narananganam GP	0.978
49	Improvement of Pazhaya Kochira Road	Idukki	Udumbanchola	Vandanmedu GP	0.55
50	Improvement of Vimalagiri Enikuthu Road	Idukki	Idukki	Mariyapuram GP	1.61
51	Rehabilitation of St. Mary's Swaraj Road	Ernakulam	Kochi	Kumbalangi GP	0.567
52	Construction of Musiris Puzhayoram Road	Ernakulam	Paravur	Chendamangalam GP	0.26
53	Sahi Rubber Ambalamukku Kattuman Road	Ernakulam	Aluva	Edathala GP	1.325
54	Nadakkavu Ethiyerakavu Road	Ernakulam	Kunnathunadu	Vazhakkulam GP	0.705
55	Improvement of Ambalappara Kadaplakkal Road	Idukki	Peerumedu	Upputhara GP	0.75
56	Improvement of Perikkankavala Kollamkulambadi Kaikavala Road	Idukki	Idukki	Vathikudy GP	0.6
57	Naalumukku Tunnelsite Road	Idukki	Udumbanchola	Erattayar GP	2.75
58	Kambanikkadavu Pattarmadom Road	Kottayam	Ettumanoor	Ettumanoor GP	1.32
59	Cheepunkal Malikayalchira Road	Kottayam	Ettumanoor	Aymanam GP	1
60	Vattathenpady Nallathupadi Road	Pathanamthitta	Aranmula	Aranmula GP	1.17
61	Reconstruction of Govt. HS Kochalivettom Road	Kottayam	Ettumanoor	Kumarakom GP	0.4
62	Improvement of Varayal Melevarayal Road	Wayanad	Mananthavady	Thavinjal GP	1.5

63	Improvement of Karlad Manjoora Road	Wayanad	Kalpetta	Thariyodu GP	2.1
64	Improvement of Kalpetta Town Jilla Stadium Road	Wayanad	Kalpetta	Kalpetta GP	3.6
65	Improvement of Varyad Thekkumpadi Road	Wayanad	Kalpetta	Muttil GP	1.3
66	Improvement of Cheriyaankolli Kalluvettumthazhe road	Wayanad	Kalpetta	Padinjarethara GP	1.9
67	Improvement of Kottathara Kakkanchal Thekkumthara Road	Wayanad	Kalpetta	Kottathara GP	1.9
68	Improvement of Puthiyedam Makkimala Road	Wayanad	Mananthavady	Thavinjal GP	4.2
69	Improvement of Kollikandam Kunneri Nelom Road	Wayanad	Mananthavady	Thondernad GP	2
70	Improvement of Korome Karimbil Road	Wayanad	Mananthavady	Thondernad GP	4.1
71	Improvement of Changadakadavu Chamadipoyil Road	Wayanad	Mananthavady	Edavaka GP	1.757



**(50-90)% COMPLETED WORKS**

SI No.	List of Works	District	LAC	Local Body
1	Upgradation of Ennakkad Alumoodu Elanjimel Road	Alappuzha	Chengannoor	Budhanoor GP
2	Construction of Pekkali bridge to Kadakam road	Alappuzha	Kuttanad	Veliyanad GP
3	Reconstruction of Manathucad Puthuveedu Road	Alappuzha	Kuttanad	Chambakkulam GP
4	Reconstruction of PWD Road to Arackalchira and Protection wall	Alappuzha	Kuttanad	Chambakkulam GP
5	Upgradation of Kattanam Nambukulangara Road	Alappuzha	Kayamkulam	Bharanickavu GP
6	Reconstruction of Panachamoodu Kochuveetilmukku Road	Alappuzha	Harippad	Cheppad GP
7	Upgradation of Highschool Nannad Eradichira	Alappuzha	Chengannoor	Thiruvandoor GP
8	Reconstruction of Govt.Hospital Road in Kuttanad	Alappuzha	Kuttanad	Thakazhy GP
9	Chirakkarappadi-Chetalapuncha, Pmattipuncha, Pazhamchira Road	Alappuzha	Chengannur	Cheriyana GP
10	Reconstruction of Palangattupadi Mannarathara Road	Alappuzha	Chengannoor	Pondanad GP
11	Upgradation of 45-il Puthuvellil Jetty Road	Alappuzha	Kuttanad	Thakazhy GP
12	Construction of Nalenkalpady to Kunnathuparambu Road	Alappuzha	Kuttanad	Thalavady GP
13	Construction of Manenkarypadi to Kodumkuthuparambu Road	Alappuzha	Kuttanad	Chambakkulam GP
14	Upgradation of Kavumpadi to Perumal Jetty Road	Alappuzha	Kuttanad	Kavalam GP

15	St. Therasas LPS to Nalpathil kalinku Road	Alappuzha	Kuttanad	Kavalam GP
16	Upgradation of Budhanoor Ponnarathara Road	Alappuzha	Chengannoor	Budhanoor GP
17	Rehabilitation of Adoor Gopalakrishnan Road	Pathanamthitta	Adoor	Erathu Gp
18	Paivazhy Nediyaakala Road	Pathanamthitta	Aranmula	Pandalam Thekkekara GP
19	Renovation of Chakrasalakadavu Panachimoottil Road	Pathanamthitta	Thiruvalla	Kuttoor Gp
20	Rehabilitation of Athikkayam Kadumeenchira Road	Pathanamthitta	Ranni	Naranamoozhy GP
21	Chana Kurumpanmoozhy Road	Pathanamthitta	Ranni	Naranammoozhy
22	Reconstruction of Banglamkadavu Stadium Valiyamkulam Road	Pathanamthitta	Ranni	Vadasserikkara GP
23	Reconstruction of Melepadi Chellakkadu Road	Pathanamthitta	Ranni	Pazhavangadi GP
24	Rehabilitation of Ozhukkuneettilpadi Paruthimoottilpadi Road	Pathanamthitta	Thiruvalla	Peringara GP
25	Upgradation of Thiruvaniyoor Meppadam Road	Ernakulam	Kunnathunadu	Thiruvaniyoor GP
26	Renovation of Panchayathupadi Pulluchani Radhapady Road	Pathanamthitta	Konni	Aruvipuram GP
27	Reconstruction of kannankara edamuri Road	Pathanamthitta	Ranni	Pazhavangadi GP
28	Olassa- Cherthalli Road	Kottayam	Ettumanoor	Aymanam GP
29	Improvement of Adivaram Ottalangalpady City Road	Idukki	Udumbanchola	Rajakkad GP
30	Improvement of Illappalli Chellikkal Road	Idukki	Idukki	Arakkulam GP
31	Improvement of Anachal Thokupara Acherikunnu Asramam road	Idukki	Devikulam	Vellathoval GP

32	Improvement of Suryanelli Gundumala Road	Idukki	Devikulam	Chinnakkanal GP
33	Reconstruction of Suryakanthikavala Old Post Office Road	Idukki	Peerumedu	Upputhara GP
34	Upgradation of Kallanchery Tharassery Road	Ernakulam	Konni	Kumbalangi GP
35	Kuranchery Nayarangadi Road	Thrissur	Vadakkanchery	Thekkumkara GP
36	Improvement of Karrorchira Anchalangadi Road	Thrissur	Irinjalakkuda	Aloor GP
37	Improvement of Thazhe Arappetta Mankunnu Road	Wayanad	Kalpetta	Muppianad GP
38	Improvement of Valliyurkavu Varadimoola Road	Wayanad	Mananthavady	Mananthavady GP
39	Improvement of Thannikkal Payyampally Road	Wayanad	Mananthavady	Mananthavady GP
40	Improvement of Erumatherivu-Choottakadavu Road	Wayanad	Mananthavady	Mananthavady GP
41	Footpath Thottuvila First Bridge to Aattutheeram Road	Alappuzha	Kuttanad	Kainakari GP
42	Holy Family School to Pazhoor Temple Road	Alappuzha	Kuttanad	Kainakari GP
43	Rehabilitation of Janaseva Road	Pathanamthitta	Thiruvalla	Peringara GP
44	Kiliyanikkal Thoolikkulam Road	Pathanamthitta	Ranni	Cherukol GP
45	Rehabilitation of Ushuspadi Vellaparamuruppu Kizhakkekkarapalli Road	Pathanamthitta	Adoor	Ezhamkulam GP
46	Reconstruction of Chembikkad Madrasappadi Road	Ernakulam	Kalamasserry	Karimannoor GP



**DETAILED REPORT OF  
WORKS-  
AS WISE**

**G.O.(Rt.)No.224/2020/P&EA dated 26-05-2020(53.136cr)**

SI No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress(%)	Fin.progress(%)	Expenditure(Cr)
1	Upgradation of Ennakkad Alumood Elanjimel road in Budhanoor GP in Alappuzha	Alappuzha	Under construction	6.39	4.9438	4.8004	80	29	1.8655
2	Rehabilitation of Thandilam Manali Kecheri road in Thrisur	Thrisсур	Completed	5	3.6692	3.6479	100	85	4.2559
3	Upgradation of Budhanoor Ponnathara road in Alappuzha	Alappuzha	Under construction	2.91	2.37	2.3	80	16	0.4787
4	Renovation of Kulikkanpalam Shappumpadi road in Alappuzha	Alappuzha	Completed	2.78	2.06	1.8871	100	73	2.0342
5	Reconstruction of AV Mukku Sharangakkavu road in Alappuzha	Alappuzha	Completed	2.82	2.0495	1.873	100	71	1.9991
6	Reconstruction of Pennukkara Canal Jn Nettuvaramcode Road in Alappuzha	Alappuzha	Completed	2.99	1.8603	1.6985	100	68	2.0396
7	Upgradation of Pannikkuzhy Kavumthazham road in Ernakulam	Ernakulam	Completed	1.81	1.42	1.25	100	78	1.4186

8	Improvement of Girideepam kadathukadavu road in Kottayam	Kottayam	Completed	1.75	1.2935	1.2392	100	85	1.4958
9	Rehabilitation of Pavamkulangara Kannankulangara Road in ernakulam	Ernakulam	Completed	1.32	0.97	0.95	100	41	0.5383
10	upgradation of Vayalodam Thadikkadavu Road in Ernakulam	Ernakulam	Completed	1.38	0.914	0.9138	100	72	0.9881
11	Renovation of Valavazhy Road in Ernakulam	Ernakulam	Selection notice issued	0.87	0.658	0.648	0	0	0
12	Rehabilitation of Paduvathil police station Road	Ernakulam	Submitted to Govt. for tender excess	0.66	0.5006	0.4947	0	0	0
13	Upgradation of Kodungalloor masjid road	Ernakulam	Completed	0.72	0.481	0.4809	100	65	0.4684
14	Improvement of Padinjattumuri Chittanda Road	Thrissur	Completed	6.72	5.4	5.09	100	85	5.7033
15	Improvement of Pathinanchilkadavu Illikkal road	Kottayam	Completed	4	2.9446	2.9301	100	87	3.491
16	Improvement of Kunnumpuram Mahilasamajam Road	Kottayam	Completed	1.84	1.3434	1.3247	100	77	1.4233
17	Upgradation of Anicadu Pravidakunnu Road	Ernakulam	Completed	1.3	1.0883	1.075	100	81	1.0517

18	Construction of Udumpuzha Chempassery road	Ernakulam	To be dropped	1.03	0.7666	0.739	33	0	0
19	Renovation of Okkal Juma Masjid Road	Ernakulam	Completed	0.166	0.1409	0.1318	100	89	0.1474
20	Reconstruction of BJP Kadavu road	Ernakulam	Completed	0.12	0.1	0.0928	100	82	0.0982
21	Rehabilitation of St. Mary's Swaraj road	Ernakulam	Under construction	0.53136	0.501	0.501	95	51	0.2696
22	Renovation of Kavanattinkara Manchira road	Kottayam	Completed	0.93	0.6712	0.6501	100	90	0.8393
23	Renovation of TV Puram Theeradesa road	Kottayam	Completed	3.5	2.9401	3.2337	100	100	3.5851
24	Malakkunnam Kannanthrappadi road	Kottayam	Completed	1.19	0.8096	0.8898	100	86	1.0277
	<b>Total</b>			<b>52.72736</b>	<b>39.8956</b>	<b>38.8415</b>			<b>35.2188</b>

**G.O.(Rt.)No.485/2019/P&EA dated 15-11-2019(266.03Cr) Pathanamthitta**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress(%)	Fin.progress(%)	Expenditure(Cr)
1	Rehabilitation of Adoor Gopalakrishnan road	Pathanamthitta	Under Construction	2.46	1.8977	1.9534	78	48	1.1834
2	Renovation of CK Road	Pathanamthitta	Under Construction	2.38	1.7836	1.8925	40	17	0.397
3	Paivazhy Nediya kala road	Pathanamthitta	Under Construction	3.76	2.7723	3.0208	70	33	1.2514
4	Renovation of Chakrasalakadavu Panachimoottil road	Pathanamthitta	Under Construction	2.77	2.094	2.2824	85	54	1.4994
5	Improvement of Thannithode Plantation road	Pathanamthitta	Under Construction	5.27	4.0737	4.2613	95	52	2.7472
6	Reconstruction of Bangalamkadavu Stadium Valiyakulam Road	Pathanamthitta	Under Construction	2.31	1.873	1.8728	58	0	0
7	Reconstruction of Bangalamkadavu Valiyakulam road	Pathanamthitta	Under Construction	2.05	1.6814	1.6433	95	82	1.6899
8	Chana Kurumpanmoozhy road	Pathanamthitta	Under Construction	2.18	1.7904	1.7007	75	21	0.4525
9	Madukkamood Ayyappa Medical College Road	Pathanamthitta	Completed	1.47	1.1821	1.0639	100	67	0.9828



10	Ratiokadappadi Mulanthanam Road	Pathanamthitta	Under Construction	1.4	1.0919	1.1288	6	0	0
11	Arumood Chala Puthenchantha 14th mile	Pathanamthitta	Under Construction	1.88	1.3583	1.4787	20	16	0.2927
12	Anthyalankavu Marthomapallipadi Karamvelipadi road	Pathanamthitta	Under Construction	1.39	1.0759	1.1079	95	19	0.266
13	Kiliyanikkal Thoolikkulam road	Pathanamthitta	Under Construction	1.56	1.1108	1.2585	70	10	0.1531
14	Reconstruction of Parakkavu Valakkuzhy road	Pathanamthitta	Completed	1.97	1.4124	1.5535	100	74	1.4521
15	Reconstruction of Melepadi Chellakkadu road	Pathanamthitta	Under Construction	2.09	1.649	1.7181	60	25	0.5199
16	Erathodu Ashankuzhy road	Pathanamthitta	Under Construction	1.96	1.5591	1.6152	40	31	0.6039
17	Vattathempady Nallathupadi Road	Pathanamthitta	Completed	1.13	0.704	0.8133	100	73	0.8265
	<b>Total</b>			<b>38.03</b>	<b>29.1096</b>	<b>30.3651</b>			<b>14.3178</b>

**G.O.(Rt.)No.485/2019/P&EA dated 15-11-2019(266.03Cr) Idukki**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Improvement of Ashramam Pottanpadi road	Idukki	Terminated	1.63	1.3	1.1995	2	0	0
2	Improvement of Adivaram Ottalangepadi City road	Idukki	Under Construction	2.37	2.2782	2.2511	58	29	0.6851
3	Improvement of Ambalappara kadaplakkal road	Idukki	Completed	1	0.8091	0.6709	100	33	0.3252
4	Improvement of Illappalli Thottambhagom road	Idukki	Completed	1.93	1.556	1.308	100	63	1.2091
5	Improvement of Illappalli Chellikkal Road	Idukki	Under Construction	4.33	3.4625	3.1298	65	25	1.064
6	Improvement of Pazhaya Kochira Road	Idukki	Completed	1.61	1.3136	1.2553	100	90	1.4557
7	Improvement of Vimalagiri Enikuthu Road	Idukki	Under Construction	2.5	2.027	1.8182	98	75	1.8736
8	Improvement of Anachal Thokkupara - Acherikkunnu Asramam road	Idukki	Under Construction	2.11	1.7144	1.5873	78	10	0.2128
9	Improvement of Murikkumthotti Mathekkalpedi Shaliliyil road	Idukki	Under Construction	1.22	0.9643	0.8645	48	0	0.0026
10	Improvement of Kattekkanam Chelamood Road	Idukki	Under Construction	0.925	0.685	0.737	15	0	0.0018
11	Improvement of Idinjamala Companipadi road	Idukki	Completed	7.245	5.1368	5.5859	100	92	6.6792
12	Improvement of Perumbankuthu 6th mile road	Idukki	Under Construction	4.12	2.9094	3.1899	42	1	0.0344

13	Improvement of Kurushupallipadi thannikandam painavu road	Idukki	Under Construction	3.3175	2.3698	2.6029	20	13	0.4469
14	Improvement of Surianelly Gundumala road	Idukki	Under Construction	2.0475	1.4479	1.5891	55	0	0
15	Improvement of Panachikuzhy Road	Idukki	Completed	4.42	3.3761	3.2497	100	91	4.0154
16	Improvement of Padicup Plakkayam Kuttamudi Tribal Colony road	Idukki	Under Construction	5.06	4.0507	3.4994	40	18	0.9318
17	Improvement of Perikkankavala Kollamkulambadi Kaikavala road	Idukki	Under Construction	2.06	1.709	1.5678	98	74	1.5375
18	improvement of Puthed Anoorthodu Footbridge road	Idukki	Under Construction	3.83	2.9954	2.9012	6	0	0
19	Balagram Anyarthulu road	Idukki	Under Construction	7.63	5.8442	5.9702	42	1	0.1086
20	Naalumukku Tunnelsite road	Idukki	Under Construction	2.26	1.6137	1.7247	95	15	0.3311
21	Improvement of Pallikkudicity Mangattupalam road	Idukki	Under Construction	2.7	2.1475	1.9673	35	53	1.4203
22	50th mile Kallakuttikudi Mankulam road	Idukki	Submitted to Govt. for tender excess	8	2.85		0	0	0
23	Mangathotti Kanakapuzha NR city road	Idukki	Submitted to Govt. for tender excess	8	5.61		0	0	0
	<b>Total</b>			<b>80.315</b>	<b>58.17</b>	<b>48.6697</b>			<b>22.335</b>

**G.O.(Rt.)No.485/2019/P&EA dated 15-11-2019(266.03Cr) Wayanad**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Improvement of Cheriya mkolli Kalluvettumthazhe road	Wayanad	Under Construction	1.44	1.09	1.0591	93	66	0.9504
2	Improvement of Idiyamvayal Pinangodu road	Wayanad	Completed	2.22	1.6774	1.5423	100	56	1.2458
3	Improvement of Erumatherivu Choottakadavu road	Wayanad	Under Construction	2.6127	1.7896	1.9682	75	59	1.5475
4	Improvement of Karlad Manjoora Road	Wayanad	Completed	1.89	1.4417	1.3084	100	53	0.9943
5	Improvement of Kuppadithura Millumukku Kurumani road	Wayanad	Completed	1.45	1.1	1.1	100	73	1.0574
6	Improvement of Kottathara Kakkanchal Thekkumthara road	Wayanad	Completed	2.74	2.25	2.2526	100	0	0
7	Improvement of Varyad Thekkumadi road	Wayanad	Under Construction	1.87	1.53	1.5	93	68	1.2681
8	Improvement of Chundel Chundel estate Pappala Anoth Road	Wayanad	Completed	5.661	4.3236	3.8668	100	57	3.2429
9	Improvement of MH Nagar Cholapuram Road	Wayanad	Completed	2.4	1.8558	1.6335	100	44	1.0596
10	Improvement of Varayal Melevarayal road	Wayanad	Completed	1.34	1.0106	0.979	100	56	0.7496

11	Improvement of Kattimoola Aroola Kottathala road	Wayanad	Completed	2.79	2.1266	2.0662	100	74	2.0604
12	Improvement of Korome Karimbil road	Wayanad	Under Construction	5.6	4.4587	4.2993	98	66	3.6821
13	Improvement of Orappu Evaranikkulam Kattimoola road	Wayanad	Completed	3.45	2.6093	2.5173	100	73	2.5097
14	Improvement of Puthiyedam Makkimala Road	Wayanad	Completed	3.89	2.902	2.813	100	46	1.7863
15	Improvement of 44th mile Makkimala Road	Wayanad	Under Construction	3.09	2.39	2.3545	33	3	0.1076
16	Improvement of Panamaram Keenjukadavu palakunnu road	Wayanad	Under Construction	6.22	4.8684	4.7356	55	32	1.962
17	Improvement of Pilakkavu pancharakolli road	Wayanad	Completed	3.09	2.3803	2.3223	100	79	2.4295
18	Improvement of Killokandam Kunneri Nelom road	Wayanad	Under Construction	1.1275	0.7727	0.8213	93	9	0.1026
19	Improvement of Valliurkavu Varadimoola road	Wayanad	Under Construction	1.45	1.1336	0.9963	80	46	0.6737
20	Improvement of Vilanilam pilakkavu Road	Wayanad	Under Construction	3.89	3.0935	2.787	28	15	0.5943
21	Improvement of Thannikkal Payyampalli Road	Wayanad	Under Construction	1.98	1.46058	1.5557	55	8	0.1508
	<b>Total</b>			<b>60.2012</b>	<b>46.26438</b>	<b>44.4784</b>			<b>28.1746</b>

**G.O.(Rt.)No.115/2020/P&EA dated 28-02-2020(4.75Cr)**

SI No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Investigation / Data Collection-Pathanamthitta	Pathanamthitta	Completed	0.4152	0.4152	0.2768	100	30%	0.1261
2	Investigation / Data Collection-Alappuzha	Alappuzha	Completed	0.8174	0.8174	0.5449	100	24%	0.1977
3	Investigation / Data Collection-Kottayam	Kottayam	Completed	0.1208	0.1208	0.0951	100	13%	0.0156
4	Investigation / Data Collection-Idukki	Idukki	Completed	1.9027	1.9027	1.3148	100	33%	0.6196
5	Investigation / Data Collection-Ernakulam	Ernakulam	Completed	0.2057	0.2057	0.1526	100	19%	0.0396
6	Investigation / Data Collection-Thrissur	Thrissur	Completed	0.3854	0.3854	0.2802	100	13%	0.0493
7	Investigation / Data Collection-Wayanad	Wayanad	Completed	0.7243	0.7243	0.5436	100	27%	0.1943
	<b>Total</b>			<b>4.5715</b>	<b>4.5715</b>	<b>3.208</b>			<b>1.2422</b>

**G.O.(Rt.)No.1389/2020/LSGD dated 23-07-2020(1.605Cr)**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Design and DPR Preparation of 218Km Roads in Idukki	Idukki	Completed	0.648	0.648	0.648	100	66	0.4295
2	Design and DPR Preparation of 218Km Roads in Pathanamthitta	Pathanamthitta	Completed	0.3074	0.3074	0.3074	100	83	0.254
3	Design and DPR Preparation of 218Km Roads in Wayanad	Wayanad	Completed	0.3979	0.3979	0.3979	100	92	0.3647
	<b>Total</b>			<b>1.3533</b>	<b>1.3533</b>	<b>1.3533</b>			<b>1.0482</b>

**G.O.(Rt.)No.404/2020/P&EA dated 23-10-2020(40Cr)**

SI No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Olassa Cherthali road	Kottayam	Under Construction	1.21	1.0104	0.9829	65	33	0.395
2	Kambanikkadavu Pattarmadom road	Kottayam	Under Construction	1.14	0.9258	0.8885	93	78	0.8857
3	Chakram Colony Road	Wayanad	Completed	0.93	0.758	0.6821	100	65	0.6089
4	maravayal Chathothu road	Wayanad	Under Construction	1.6	1.335	1.2127	93	62	0.9878
5	Kanjikkalmukku Ganam Theatre road	Alappuzha	Completed	2.14	1.6332	1.6294	100	64	1.3582
6	Reconstruction of AC Canal to Mankuzhy Road	Alappuzha	Completed	1.15	0.9364	1.0205	100	61	0.7031
7	Chirakkarappadi Chetalpuncha, Pmattipuncha, Pazhamchira road	Alappuzha	Under Construction	3.48	2.8405	2.6804	55	31	1.069
8	Reconstruction of Manathucadu Puthuveedu Road and Protection	Alappuzha	Under Construction	2	1.6692	1.7855	70	39	0.7848
9	Reconstruction of Madathilkadavu Mahilasamajam Kandathilpalli Road	Kottayam	Under Construction	1.45	1.2218	1.3046	2	0	0
10	Cheepunkal Malikayalchira Road	Kottayam	Under Construction	1.48	1.2318	1.2195	93	39	0.5825
11	Panjamkaval Ward18 road	Ernakulam	Completed	1.34	1.0426	0.997	100	74	0.9923



12	Chillukarankunnu Road	Thrissur	Completed	0.96	0.7093	0.6754	100	86	0.833
13	Kuranchery Nayarangadi Road	Thrissur	Under Construction	12.5	9.8568	9.8285	68	42	5.3012
14	Reconstruction of LPS Mukkam Kolleri Road	Kottayam	Under Construction	0.562	0.4275	0.4683	45	1	0.0033
15	Harbour road to Manaladi Jetti Road	Alappuzha	Under Construction	1.36	1.0376	1.141	4	0	0
16	Improvement of Karoorchira Anchalangadi road	Thrissur	Under Construction	2.12	1.5563	1.6963	58	28	0.601
17	Rehabilitation of Paris Road	Thrissur	Under Construction	1.85	1.3425	1.4642	30	13	0.2403
18	Construction of Musiris Puzhayoram road	Ernakulam	Completed	1.08	0.8399	0.9156	100	0	0.0019
19	Improvement of Puthiyakavu pozhankavu Road	Thrissur	Completed	0.82255	0.6129	0.6734	100	93	0.7618
	<b>Total</b>			<b>39.17455</b>	<b>30.9875</b>	<b>31.2658</b>			<b>16.1101</b>

**G.O.(Rt.)No.62/2021/P&EA dated 03-02-2021(42.32Cr)**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Renovation of Kottomonpara Melekottomonpara Pandyanpara Road	Pathanamthitta	Completed	2.48	2.0038	1.9291	100	64	1.5917
2	Improvement of Edathod palli Basilica Road	Ernakulam	Completed	0.52	0.4116	0.4039	100	88	0.4554
3	Improvement of Thazhe Arappetta Mankunnu Road	Wayanad	Under Construction	4.2	3.274	3.0978	58	33	1.3799
4	Rehabilitation of Thazhathangadi- thanitheruvu road	Wayanad	Completed	1.2	0.9441	0.9191	100	82	0.9858
5	Reconstruction of PWD Road to Araikkalchira and Protection Wall	Alappuzha	Under Construction	1.22	1.0262	1.025	70	55	0.6648
6	Reconstruction of Govt.HS kochalivettom Road	Kottayam	Under Construction	0.306	0.2259	0.2482	93	40	0.1228
7	Upgradation of Madathekkathil Chaalukkara Road	Alappuzha	Completed	0.29	0.2138	0.2316	100	89	0.259
8	Rehabilitation of Mithrappuzha vayanasalapadi Vendoorparadi Road	Alappuzha	Completed	3.6	2.6043	2.8365	100	93	3.3289
9	Upgradation of Kattanam Nambukulangara Road	Alappuzha	Under Construction	3.48	2.5671	2.8214	80	30	1.0342
10	Reconstruction of Palangattupadi Mannarathara Road	Alappuzha	Under Construction	2.73	2.0215	2.2216	90	49	1.334
11	Reconstruction of Panachimoodu Kochuveetilmukku Road	Alappuzha	Under Construction	3.55	2.631	2.8892	50	31	1.0986

12	Upgradation of Highschool Nannad Eradichira Road	Alappuzha	Under Construction	5.7	4.4847	4.7721	75	19	1.0804
13	Rehabilitation and Reconstruction of Ex- Serviceman Colony Centre road	Thrissur	Under Construction	2.76	1.9077	2.044	93	72	2.003
14	Nadakkavu Ethiyerikkavu Road	Ernakulam	Completed	0.42	0.2877	0.3161	100	0	0
15	Rernovation of Panchayathupadi Pulluchani Radhapadi Road	Pathanamthitta	Under Construction	4.41	3.2808	3.597	70	46	2.0481
16	Renovation of Police stationpadi TVM Hospital Elangavettom Kshethram Road	Pathanamthitta	Under Construction	2.78	1.9547	2.1454	40	0	0
17	Market Jetty Vathikadu Jetty Road	Alappuzha	Re-tendered	1.6	0.9027		0	0	0
	<b>Total</b>			<b>41.246</b>	<b>30.7416</b>	<b>31.498</b>			<b>17.3866</b>

**G.O.(Rt.)No.2257/2020/LSGD dated 02-12-2020(0.0546Cr)**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	CBR Investigation of Roads in Wayanad	Wayanad	Completed	0.0546			100	87	0.0475
	<b>Total</b>			<b>0.0546</b>					<b>0.0475</b>

**G.O.(Rt.)No.234/2021/LSGD dated 28-01-2021(1.2 Cr)**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Soil Investigation for bridges in TSR/PKD/ALP/WYD/KNR		Completed	0.2001		0.2001	100	14	0.0289
2	Soil Investigation in Pathanamthitta 3 bridges	Pathanamthitta	Completed	0.06			100	0	0
3	Soil Investigation in Alappuzha 10 bridges	Alappuzha	Completed	0.25			100	34	0.0859
4	Soil Investigation in Kottayam 2 bridges	Kottayam	Completed	0.04			100	80	0.0319
5	Soil Investigation in Idukki 12 bridges	Idukki	Completed	0.34		0.21	100	53	0.1807
6	Soil Investigation in Ernakulam 9 bridges	Ernakulam	Completed	0.275			100	0	0
	<b>Total</b>			<b>1.1651</b>		<b>0.4101</b>			<b>0.3274</b>

<b>G.O.(Rt.)No.1669/2020/LSGD dated 16-09-2020(0.0246 Cr)</b>									
Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Topographic survey for roads in Wayanad	Wayanad	Completed	0.0246			100	62	0.0153
	<b>Total</b>			<b>0.0246</b>					<b>0.0153</b>

**G.O.(Rt.)No.348/2021/P&EA dated 15-08-2021(30.91 Cr)**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Rehabilitation of Athikkayam Kaddumeenchira Road	Pathanamthitta	Under Construction	3.05	1.8423	1.8506	75	1	0.1186
2	Reconstruction of Factorypadi Karintharuvi Road	Idukki	Under Construction	3.22	2.6584	2.4446	40	12	0.3984
3	Reconstruction of Suryakanthikavala Old postoffice Road	Idukki	Under Construction	1.3	1.0761	0.9889	78	0	0
4	Rehabilitation of Valiyaparambil Eetichuvadu Road	Pathanamthitta	Under Construction	1.7	1.1769	1.1664	95	25	0.4337
5	Rehabilitation of Janaseva Road	Pathanamthitta	Under Construction	3.1	2.3319	2.3218	50	24	0.7588
6	Improvement of Kalpetta Town Jilla Stadium Road	Wayanad	Under Construction	2.97	2.1802	2.3231	93	74	2.2036
7	Rehabilitation of Ushuspadi Vellaparamuruppu Kizhakkekkarapalli Road	Pathanamthitta	Under Construction	2.25	1.5712	1.6261	50	25	0.5715
8	Upgradation of 45-il Puthuvel Jetty Road	Alappuzha	Under Construction	2.01	1.6508	1.7983	60	41	0.818
9	Reconstruction of Govt. Hospital Road	Alappuzha	Under Construction	2.19	1.8226	1.9648	60	53	1.1605
10	Construction of Nalenkalpadi to Kunnathuparambu Road	Alappuzha	Under Construction	1.98	1.6008	1.7636	60	48	0.9504

11	Construction of Manenkarypadi to Kodumkuthuparambu Road	Alappuzha	Under Construction	1.35	1.0432	1.1407	75	36	0.486
12	Ambiyathupadi Ikkara Boatjetty Road	Alappuzha	Under Construction	3.6	2.8969	3.186	15	11	0.3889
13	Reconstruction of Kannankara Idamuri Road	Pathanamthitta	Under Construction	1.13	0.8596	0.9451	60	29	0.3315
14	Malayuman Vazhayilpadi Road	Pathanamthitta	Submitted to Govt. for tender excess	1.06	0.6512		0	0	0
	<b>Total</b>			<b>30.91</b>	<b>23.3621</b>	<b>23.52</b>			<b>8.6196</b>



**G.O.(Rt.)No.18/2022/P&EA dated 07-01-2022(49.34 Cr)**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Rehabilitation of Koipalli Melethilpadi Road	Pathanamthitta	Under Construction	1.44	1.1745	1.1146	4	0	0
2	Rehabilitation of Ozhukkuneettilpadi Paruthimoottilpadi Road	Pathanamthitta	Under Construction	3.47	2.3329	2.25	50	42	1.4719
3	Rehabilitation of Kannamplackalpadi Puthenpalam Road	Idukki	Under Construction	1.13	0.8631	0.8221	33	1	0.0128
4	Upgradation of KE Carmel Pulikkal Road	Alappuzha	Completed	0.99	0.7717	0.7461	100	91	0.8972
5	Upgradation of Kavumpadi to Perumal Jetty Road	Alappuzha	Under Construction	2.01	1.7106	1.5968	68	48	0.9572
6	Karichira to Puthusseri Road	Alappuzha	Under Construction	2.61	2.2172	2.1828	10	0	0
7	St. Therasas LPS to Nalpathikalinku Road	Alappuzha	Under Construction	1.74	1.4799	1.4097	60	51	0.8905
8	Eranjoli Pulikkal Road	Wayanad	Under Construction	3.38	2.7585	2.6115	0	0	0
9	Improvement of Changadakadavu Chamadipoyi Road	Wayanad	Under Construction	3.04	2.3899	2.1842	93	23	0.7085
10	Upgradation of Kallanchery Tharasserri Road	Ernakulam	Under Construction	3.1	2.5728	2.83	70	39	1.2059
11	Upgradation of Thiruvaniyoor Meppadam Road	Ernakulam	Under Construction	3.42	2.5597	2.6811	60	27	0.9281

12	Anchalangadi Bridge to Mancomp LPS Road	Alappuzha	Under Construction	3.22	2.7025	2.9652	33	21	0.6799
13	Construction of Amarathodu Pathilchira Road	Alappuzha	Under Construction	2.5	2.1142	2.3232	40	40	0.9904
14	Construction of Pekkali Bridge to Kadakam Road	Alappuzha	Under Construction	0.95	0.7924	0.8225	90	24	0.2292
15	Upgradation of PS Kavala Chudukattumpuram Chooramana Road	Alappuzha	Under Construction	3.17	2.6942	2.9633	2	0	0
16	Construction of Kumaramkari Society Road	Alappuzha	Under Construction	3.79	3.2144	3.492	30	15	0.5746
17	Therambilpadi Road	Alappuzha	Under Construction	2.42	1.988	2.1868	30	0	0
18	Footpath Thottuvila First Bridge to Aattutheeram Road	Alappuzha	Under Construction	1.62	1.262	1.375	80	53	0.8667
19	Kanichukulangara kavala Kalathilveedu Road	Alappuzha	Under Construction	1.81	1.263	1.387	20	12	0.1871
20	Kainadpally Karumathra Kshethram Road	Alappuzha	Under Construction	1.98	1.5102	1.6555	30	16	0.2867
21	Holy family School to Pazhoor Temple Road	Alappuzha	Under Construction	1.47	1.143	1.253	68	27	0.362
	<b>Total</b>			<b>49.26</b>	<b>39.5147</b>	<b>40.8519</b>			<b>11.2487</b>

**G.O.(Rt.)No.300/2022/P&EA dated 02-08-2022(25.85Cr)**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Valiyapalli Kayalpuram School Road	Alappuzha	Submitted to Govt.	4.3			0	0	0
2	Ramapuram Illathupadi Valiyathupadi Road	Pathanamthitta	Under Construction	0.92	0.626	0.652	4	0	0
3	Pulikeezhu Road	Pathanamthitta	Under Construction	3.04	2.14	2.26	2	0	0
4	Papanattupadi Panchayathupadi Road	Pathanamthitta	Under Construction	2.22	1.533	1.531	15	0	0
5	Thattakallu Ponnezhuthan	Idukki	Under Construction	3.25	2.604	2.206	8	0	0
6	Bhoomiyamkulam Keshamini Road	Idukki	Under Construction	1.9	1.593	1.312	8	0	0
7	Araikkalpadai Ambikavilasam Estatepadai Road	Idukki	Under Construction	5.65	4.598	3.815	20	0	0.0028
8	Sahi Rubber Ambalamukku Kattuman Road	Ernakulam	Completed	1.7	1.331	1.301	100	0	0
9	Kuzhur Iranikulam Indira Gandhi Road	Thrissur	Under Construction	3.38	2.7	2.505	30	0	0
	<b>Total</b>			<b>26.36</b>	<b>17.125</b>	<b>15.582</b>			<b>0.014</b>

**G.O.(Rt.)No.405/2022LSGD dated 22-02-2022(0.721Cr)**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Consultancy Services for design and Preparation of DPR of Bridges	Alappuzha	DPR Preparation		0.0923	0.0905	0	0	0
2	Consultancy Services for design and Preparation of DPR of Bridges	Ernakulam, Thrissur	DPR Preparation		0.0401	0.0397	0	0	0
3	Consultancy Services for design and Preparation of DPR of Bridges	Idukki	DPR Preparation		0.0998	0.0978	0	0	0
4	Consultancy Services for design and Preparation of DPR of Bridges	Kannur, Palakkad ,Wayanad	DPR Preparation		0.0579	0.0567	0	0	0
	<b>Total</b>				<b>0.2901</b>	<b>0.2847</b>			

**G.O.(Rt.)No.422/2022/P&EA dated 10-11-2022(1.6Cr)**

Sl No	Name of Work	District	Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Reconstruction of Chembikkad Madrasappadi Road(Vayalodam Thadikkadavu Reach II)	Ernakulam	Under Construction	1.76	1.266	1.325	50	0	0.003
	<b>Total</b>			<b>1.76</b>					<b>0.003</b>



## DETAILED REPORT OF WORKS- DISTRICT WISE

## ALAPPUZHA

Sl No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Status	AS Amt.	TS amt	Tendered Amt.	Contract Amt.	Phy. Progress (%)	Fin. Progress (%)	Expenditure (Cr)
1	Upgradation of Ennakkad Alumood Elanjimel Road	Budhanoor GP	Chengannor	G.O.(Rt).No.224 /2020/P&EA	3.225	Under Construction	6.39	6.39	4.9438	4.8004	80	29	1.8655
2	Upgradation of Budhanoor Ponnathara Road	Budhanoor GP	Chengannor	G.O.(Rt).No.224 /2020/P&EA	1.933	Under Construction	2.91	2.91	2.37	2.3	80	16	0.4787
3	Renovation of Kulikkanpalam Shappumpadi Road	Cheriyana GP	Chengannor	G.O.(Rt).No.224 /2020/P&EA	1.4	Completed	2.78	2.78	2.06	1.8871	100	73	2.0351
4	Reconstruction of AV mukku - Sharangakkavu Road	Nooranad GP	Mavelikkara	G.O.(Rt).No.224 /2020/P&EA	1.48	Completed	2.82	2.82	2.0495	1.873	100	71	1.9991
5	Reconstruction of Pennukkara Canal Jn. Nettuvaramcode Road	Ala GP	Chengannor	G.O.(Rt).No.224 /2020/P&EA	1.42	Completed	2.99	2.99	1.8603	1.6985	100	68	2.0411
6	Kanjikkalmukku Ganam Theatre Road	Bharanikkavu GP	Kayamkulam	G.O.(Rt).No.404 /2020/P&EA	1.62	Under Construction	2.14	2.14	1.6332	1.6294	100	64	1.3582
7	Reconstruction of AC Canal to MAnkuzhy Road	Ramankary GP	Kuttanad	G.O.(Rt).No.404 /2020/P&EA	0.8	Completed	1.15	1.15	0.9364	1.0205	100	61	0.7029
8	Chirakkarappadi-Chetalapuncha-Pmattipuncha, Pazhamchira Road	Cheriyana GP	Chengannor	G.O.(Rt).No.404 /2020/P&EA	2.75	Under Construction	3.48	3.48	2.8405	2.6804	55	31	1.069

9	Reconstruction of Manathucadu-Puthuveedu Road	Chambakkulam GP	Kuttanad	G.O.(Rt).No.404/2020/P&EA	1.15	Under Construction	2	2	1.6692	1.7855	70	39	0.7847
10	Reconstruction of PWD Road to Araickalchira and Protection wall	Chambakkulam GP	Kuttanad	G.O.(Rt).No.62/2021/P&EA	0.49	Under Construction	1.22	1.22	1.0262	1.025	70	55	0.6648
11	Harbour road to Manaladi Jetty Road	Ramankary GP	Kuttanad	G.O.(Rt).No.404/2020/P&EA	2	Under Construction	1.36	1.24	1.0376	1.141	4	0	0
12	Upgradation of Madathekkathil Chalukkara Road	Mulakuzha GP	Chengannor	G.O.(Rt).No.62/2021/P&EA	0.375	Completed	0.29	0.27	0.2138	0.2316	100	89	0.259
13	Rehabilitation of Mithrapuzha Vayanasalapadi Vendoorpad Road	Chengannor GP	Chengannor	G.O.(Rt).No.62/2021/P&EA	2.78	Completed	3.6	3.32	2.6043	2.8365	100	93	3.3289
14	Upgradation of Kattanam Nambukulangara Road	Bharanikkavu GP	Kayamkulam	G.O.(Rt).No.62/2021/P&EA	3.35	Under Construction	3.48	3.17	2.5671	2.8214	80	30	1.0342
15	Reconstruction of Palangattupadi Mannarathara Road	Pondanad GP	Chengannor	G.O.(Rt).No.62/2021/P&EA	1.6	Under Construction	2.73	2.49	2.0215	2.2216	90	49	1.334
16	Reconstruction of Panachamoodu Kochuveettilmukku Road	Cheppad GP	Haripad	G.O.(Rt).No.62/2021/P&EA	2.59	Under Construction	3.55	3.24	2.631	2.8892	50	31	1.0986
17	Upgradation of Highschool Nannad Eradichira Road	Thiruvandoor GP	Chengannor	G.O.(Rt).No.62/2021/P&EA	2.4	Under Construction	5.7	5.37	4.4847	4.7721	75	19	1.0804
18	Upgradation of 45-il Puthuvellil Jetty Road	Thakazhy GP	Kuttanad	G.O.(Rt).No.348/2021/P&EA	1.295	Under Construction	2.01	2.01	1.6508	1.7983	60	41	0.818
19	Reconstruction of Govt. Hospital Road	Thakazhy GP	Kuttanad	G.O.(Rt).No.348/2021/P&EA	1.02	Under Construction	2.19	2.19	1.8226	1.9648	60	53	1.1605



20	Construction of Nalenkalpadi to Kunnathuparambu Road	Thalavady GP	Kuttanad	G.O.(Rt).No.348 /2021/P&EA	0.913	Under Construction	1.98	1.98	1.6008	1.7636	60	48	0.9504
21	Construction of Manenkarypadi to Kodumkuthuparambu Road	Chambakkulam GP	Kuttanad	G.O.(Rt).No.348 /2021/P&EA	0.742	Under Construction	1.35	1.35	1.0432	1.1407	75	36	0.486
22	Ambiyathupadi Ikkara Boat jetty Road	Edathva GP	Kuttanad	G.O.(Rt).No.348 /2021/P&EA	2.55	Under Construction	3.6	3.6	2.8969	3.186	15	11	0.3886
23	Upgradation of KE Carmel Pulickal Road	Kanjikkuzhy GP	Cherthala	G.O.(Rt).No.18/2022/P&EA	0.892	Completed	0.99	0.99	0.7717	0.7461	100	91	0.8972
24	Upgradation of Kavumpadi to Perumal Jetty Road	Kavalam GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	0.865	Under Construction	2.01	2.01	1.7106	1.5968	68	48	0.9572
25	Karichira to Puthusseri Road	Ambalapuzha South GP	Ambalappuzha	G.O.(Rt).No.18/2022/P&EA	1.23	Under Construction	2.61	2.61	2.2172	2.1828	10	0	0
26	St. Therasas LPS to Nalpathil Kalinku Road	Kavalam GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	0.766	Under Construction	1.74	1.74	1.4799	1.4097	60	51	0.8905
27	Anchalangadi Bridge to Mancomp Govt.LPS Road	Pulinkunnu GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	1.365	Under Construction	3.22	3.22	2.7025	2.9652	33	21	0.6799
28	Construction of Amarathod Pathilchira Road	Chambakkulam GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	1.125	Under Construction	2.5	2.5	2.1142	2.3232	40	40	0.9904
29	Construction of Pekkali Bridge to Kadakom Road	Veliyanad GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	0.896	Under Construction	0.95	0.95	0.7924	0.8225	90	24	0.2292
30	Upgradation of PS Kavala chudukattumpuram Chooramana Road	Thycattussery GP	Aroor	G.O.(Rt).No.18/2022/P&EA	0.9	Under Construction	3.17	3.17	2.6942	2.9633	2	0	0

31	Construction of Kumaramkary Society road	Veliyanad GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	1.777	Under Construction	3.79	3.79	3.2144	3.492	30	15	0.5746
32	Therambilpadi Road	Thalavady GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	0.892	Under Construction	2.42	2.42	1.988	2.1868	30	0	0
33	Footpath Thottuvila First Bridge to Aattutheeram Road	Kainakary GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	0.645	Under Construction	1.49	1.49			80	53	0.8667
34	Kanichukulangara Kavala Kalathilveedu Road	Kanjikkuzhy GP	Cherthala	G.O.(Rt).No.18/2022/P&EA	1.222	Under Construction	1.57	1.57	1.263		20	12	0.1871
35	Kainad Pally-Karumathra Kshethram Road	Neelamperoor GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	0.974	Under Construction	1.81	1.81	1.5102		30	16	0.2867
36	Holy family school to Pazhoor temple road	Kainakary GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	0.758	Under Construction	1.35	1.35			68	27	0.362
37	Valiyapalli Kayalpuram School Road	Pulinkunnu GP	Kuttanad	G.O.(Rt).No.300/2022/P&EA	1.275	Submitted to Gov.	4.3	4.3			0	0	0
38	Market Jetty Vathikadu jetty Road	Perumbalam GP	Aroor	G.O.(Rt).No.62/2021/P&EA		To be retender	1.6	1.14	0.9027		0	0	0
39	Investigation/data collection			G.O.(Rt).No.115/2020/P&EA		Completed	0.82		0.8174	0.5449	100	24	0.1977
40	Soil Investigation in Alappuzha 10 Bridges			G.O.(Rt).No.234/2021/P&EA		Completed	0.25	0.25			100	34	0.0859
41	Moorthitta Mukkathery Vazhayi (Chackittapadi bridge)	Mannar GP	Chengannur	G.O.(Rt).No.221/2020/P&EA	4.2	AS received	15.2				0	0	0
42	Naduvath Moon Bridge	Muttar GP	Kuttanad	G.O.(Rt).No.221/2020/P&EA	0.035	DPR Preparation					0	0	0

43	Nellanickal Ambalam Road	Muttar GP	Kuttanad	G.O.(Rt).No.221 /2020/P&EA	0.035	DPR Preparation					0	0	0
44	SNDP to Nadukkod	Muttar GP	Kuttanad	G.O.(Rt).No.221 /2020/P&EA	0.015	DPR Preparation					0	0	0
45	SNDP to Vadaparambu Culvert Road	Muttar GP	Kuttanad	G.O.(Rt).No.221 /2020/P&EA	0.0105	DPR Preparation					0	0	0
46	Vallamkadavu Chillithuruth Swamithara road	Chenganno or- Thriperumthura Gp	Chenganno or	G.O.(Rt).No.221 /2020/P&EA	0.02	DPR Preparation					0	0	0
47	SN Jn. to Tsunami smaraka road	Arattupuzha GP	Harippad	G.O.(Rt).No.221 /2020/P&EA		DPR Preparation					0	0	0
<b>TOTAL</b>					<b>53.59</b>		<b>120.24</b>	<b>93.42</b>	<b>70.142</b>	<b>68.7</b>			<b>32.143</b>

## PATHANAMTHITTA

SI No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Status	AS Amt.	TS amt	Tendered Amt.	Contract Amt.	Phy. Progress (%)	Fin. Progress (%)	Expenditure(Cr)
1	Renovation of Kottomonpara Melekottomonpara Pandyanpara road	Seethathodu GP	Konni	G.O.(Rt.)No.62/2021/P&EA	1.79	Under Construction	2.48	2.48	2.0038	1.9291	100	64	1.5917
2	Rehabilitation of Adoor Gopalakrishnan Road	Erathu GP	Adoor	G.O.(Rt.)No.485/2019/P&EA	1.86	Under Construction	2.4574	2.4	1.8977	1.9534	78	48	1.1834
3	Renovation of CK Road	Kottangal GP	Ranni	G.O.(Rt.)No.485/2019/P&EA	2	Under Construction	2.3775	2.25	1.7836	1.8925	40	17	0.397
4	Paivazhy Nediya kala Road	Thekkekkara GP	Aranmula	G.O.(Rt.)No.485/2019/P&EA	2.7	Under Construction	3.758	3.46	2.7723	3.0208	70	33	1.2513
5	Renovation of Panchayathpadi Pulluchani Radhapady Road	Aruvappulam GP	Konni	G.O.(Rt.)No.62/2021/P&EA	3.06	Under Construction	4.41	4.04	3.2808	3.597	70	46	2.0481
6	Renovation of Police stationpadi TVM hospital Elangavattom Kshetra Road	Konni GP	Konni	G.O.(Rt.)No.62/2021/P&EA	2.89	Under Construction	2.78	2.57	1.9547	2.1454	40	0	0
7	Renovation of Chakrasalakadavu Panachimoottil Road	Kuttoor GP	Thiruvalla	G.O.(Rt.)No.485/2019/P&EA	2.4	Under Construction	2.769	2.55	2.094	2.2824	85	54	1.4994
8	Improvement of Thannithodu Plantation Road	Thannithodu GP	Konni	G.O.(Rt.)No.485/2019/P&EA	4.32	Under Construction	5.2695	5.05	4.0737	4.2613	95	52	2.7472
9	Reconstruction of Bangalamkadavu Stadium Valiyakulam Road	Vadasserikkar GP	Ranni	G.O.(Rt.)No.485/2019/P&EA	2.9	Under Construction	2.31	2.31	1.873	1.8728	58	0	0

10	Reconstruction of Bangalamkadavu Valiyakulam Road	Vadasserikkar GP	Ranni	G.O.(Rt.)No.485 /2019/P&EA	2	Under Construction	2.05	2.05	1.6814	1.6433	95	82	1.6899
11	Chana Kurumpanmoozhy Road	Naranamoozhy	Ranni	G.O.(Rt.)No.485 /2019/P&EA	2	Under Construction	2.18	2.18	1.7904	1.7007	75	21	0.4524
12	Madukkamood Ayyappa Medical College Road	Vadasserikkar GP	Ranni	G.O.(Rt.)No.485 /2019/P&EA	1	Under Construction	1.47	1.47	1.1821	1.0639	100	67	0.9828
13	Rationkadapadi Mulanthanam Road	Perunadu GP	Ranni	G.O.(Rt.)No.485 /2019/P&EA	1	Under Construction	1.401	1.36	1.0919	1.1288	6	0	0
14	Arummood-Chala Puthenchantha 14th mile road	Pallikkal GP	Adoor	G.O.(Rt.)No.485 /2019/P&EA	1.29	Under Construction	1.875	1.73	1.3583	1.4787	20	16	0.2927
15	Rehabilitation of Athikkayam kadumeenchira Road	Naranamoozhy	Ranni	G.O.(Rt.)No.348 /2021/P&EA	1.83	Under Construction	3.05	2.4	1.8423	1.8506	75	4	0.1186
16	Rehabilitation of Valiyaparambil Eetichuvadu Road	Pazhavangadi GP	Ranni	G.O.(Rt.)No.348 /2021/P&EA	1.33	Under Construction	1.7	1.5	1.1769	1.1664	95	25	0.4337
17	Rehabilitation of Janaseva Road	Peringara GP	Thiruvalla	G.O.(Rt.)No.348 /2021/P&EA	1.54	Under Construction	3.1	2.84	2.3319	2.3218	50	24	0.7588
18	Anthyalankavu Marthomappallipadi Karamvelipadi road	Narananganam GP	Aranmula	G.O.(Rt.)No.485 /2019/P&EA	0.978	Under Construction	1.3868	1.35	1.0759	1.1079	95	19	0.266
19	Kiliyanikal Thoolikulam Road	Cherukol GP	Ranni	G.O.(Rt.)No.485 /2019/P&EA	1.4	Under Construction	1.5625	1.45	1.1108	1.2585	70	10	0.1531
20	Reconstruction of Parakkavu Valakuzhy Road	Ezhumattoor GP	Ranni	G.O.(Rt.)No.485 /2019/P&EA	1.75	Completed	1.9716	1.8	1.4124	1.5535	100	74	1.4521
21	Reconstruction of Melepadi Chellakadu Road	Pazhavangadi GP	Ranni	G.O.(Rt.)No.485 /2019/P&EA	1.558	Under Construction	2.092	2.01	1.649	1.7181	60	25	0.5199
22	Rehabilitation of Ushuspadi Vellaparamuruppu	Ezhamkulam GP	Adoor	G.O.(Rt.)No.348 /2021/P&EA	1.6	Under Construction	2.25	2.03	1.5712	1.6261	50	25	0.5715

	Kizhakkekkarapalli road												
23	Erathodu Ashankuzhy Road	Niranam GP	Thiruvalla	G.O.(Rt.)No.485 /2019/P&EA	1.2	Under Construction	1.9645	1.9	1.5591	1.6152	40	31	0.6039
24	Rehabilitation of Koipallimelethilpadi road	Ayroor GP	Ranni	G.O.(Rt.)No.18/2022/P&EA	0.86	Under Construction	1.44	1.43	1.1745	1.1146	4	0	0
25	Rehabilitation of Ozhukkuneettilpadi Paruthimoottilpadi Road	Peringara GP	Thiruvalla	G.O.(Rt.)No.18/2022/P&EA	0.93	Under Construction	3.47	2.82	2.3329	2.25	50	42	1.4719
26	Reconstruction of Kannankara Edamuri Road	Pazhavangadi GP	Ranni	G.O.(Rt.)No.348 /2021/P&EA	0.82	Under Construction	1.13	1.13	0.8596	0.9451	60	29	0.3315
27	Vattathenpadi Nallathupadi Road	Aranmula GP	Aranmula	G.O.(Rt.)No.485 /2019/P&EA	1.17	Under Construction	1.128	1.01	0.704	0.8133	100	73	0.8265
28	Malayuman Vazhayilpadi Road	Aranmula GP	Aranmula	G.O.(Rt.)No.348 /2021/P&EA	0.93	Tender process	1.16	0.92	0.714		0	0	0
29	Ramapuram Illathupadi Valiyathupadi road	Ranni GP	Ranni	G.O.(Rt.)No.300 /2022/P&EA	1.245	Site handedover	0.92	0.85	0.626	0.652	4	0	0
30	Pulikkeezhu Road	Kottangal GP	Thiruvalla	G.O.(Rt.)No.300 /2022/P&EA	2.25	Site handedover	3.05	2.6	2.14	2.26	2	0	0
31	Papanattupadi Panchayathupadi Road	Kottangal GP	Ranni	G.O.(Rt.)No.300 /2022/P&EA	2.02	Under Construction	2.22	2.22	1.533	1.531	15	0	0
32	Investigation/ Data collection			G.O.(Rt.)No.115 /2020/P&EA		Completed	0.4152		0.4152	0.2768	100	30	0.1261
33	Design and DPR preparation of 218km Roads			G.O.(Rt.)No.138 9/2020/LSGD		Completed	0.3074		0.3074	0.3074	100	83	0.254
34	Soil investigation of 3 Bridges			G.O.(Rt.)No.234 /2021/P&EA		Completed	0.06	0.06			100	0	0
	<b>TOTAL</b>				<b>54.62</b>		<b>71.96</b>	<b>66.22</b>	<b>53.4</b>	<b>54.34</b>			<b>22.02</b>

## KOTTAYAM

Sl No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Status	AS Amt.	TS Amt	Tendered Amt.	Contract Amt.	Phy. Progress (%)	Fin. Progress (%)	Expenditure(Cr)
1	Improvement of Girideepam Kadathukadavu Road	Vijayapuram GP	Kottayam	G.O.(Rt.)No.224 /2020/P&EA	1.86	Completed	1.75	1.75	1.2935	1.2392	100	85	1.4958
2	Improvement of Pathinanchilkadavu Illikkal Road	Kottayam GP	Kottayam	G.O.(Rt.)No.224 /2020/P&EA	2	Completed	4	4	2.9446	2.9301	100	87	3.491
3	Improvement of Kunnumpuram Mahilaamajam Road	Thiruvvarppu GP	Ettumanoor	G.O.(Rt.)No.224 /2020/P&EA	1	Completed	1.84	1.84	1.3434	1.3247	100	77.35	1.4233
4	Renovation of kavanattinkara Manchira Road	Aymanam GP	Ettumanoor	G.O.(Rt.)No.224 /2020/P&EA	1.3	Completed	0.93	0.93	0.6712	0.6501	100	90	0.8393
5	Renovation of TV Puram Theeradesam Road	TV Puram GP	Vaikom	G.O.(Rt.)No.224 /2020/P&EA	3.79	Completed	3.5	3.5	2.9401	3.2337	100	100	3.5851
6	Malakkunnam Kannanthrappadi Road	Kurichy GP	Changanassery	G.O.(Rt.)No.224 /2020/P&EA	1.125	Completed	1.19	1.19	0.8096	0.8898	100	86	1.0277
7	Olassa Cherthalli Road	Aymanam GP	Ettumanoor	G.O.(Rt.)No.404 /2020/P&EA	0.968	Under Construction	1.21	1.21	1.0104	0.9829	65	33	0.395
8	Kambanikkadavu Pattarmadon Road	Ettumanoor GP	Ettumanoor	G.O.(Rt.)No.404 /2020/P&EA	1.32	Under Construction	1.14	1.14	0.9258	0.8885	96	78	0.8857
9	Reconstruction of Madathilkadavu Mahilasamajam Kandathilpalli Road	Thiruvvarppu GP	Ettumanoor	G.O.(Rt.)No.404 /2020/P&EA	0.85	Under Construction	1.45	1.45	1.2218	1.3046	2	0	0
10	Cheepunkal-Malikayalchira Road	Aymanam GP	Ettumanoor	G.O.(Rt.)No.404 /2020/P&EA	1	Under Construction	1.48	1.48	1.2318	1.2195	97	39	0.5825
11	Reconstruction of LPS Mukkam Kollori Road	Chempu GP	Vaikom	G.O.(Rt.)No.404 /2020/P&EA	0.33	Under Construction	0.5618	0.52	0.4275	0.4683	45	1	0.0033

12	Reconstruction of Govt. HS Kochalivattom road	Kumarakom GP	Ettumanoor	G.O.(Rt.)No.62/2021/P&EA	0.4	Under Construction	0.306	0.28	0.2259	0.2482	93	40	0.1228
13	Investigation / Data Collection			G.O.(Rt.)No.115/2020/P&EA		Completed	0.1208		0.1208	0.0951	100	13	0.0156
14	Soil Investigation of 2 Bridges			G.O.(Rt.)No.234/2021/P&EA		Completed	0.04	0.04			100	80	0.031
	<b>TOTAL</b>				<b>15.94</b>		<b>19.52</b>	<b>19.33</b>	<b>15.16</b>	<b>15.47</b>			<b>13.89</b>



## IDUKKI

SI No.	Name of Work	Local Body	LAC	Length(Km)	AS No.	Status	AS Amt.	TS amt	Tendered Amt.	Contract Amt.	Phy. Progress (%)	Fin. Progress (%)	Expenditure (Cr)
1	Improvement of Asramam Pottanpadi Road	Arakkulam GP	Idukki	1.5	G.O.(Rt.)No.485 /2019/P&EA	Terminated	1.63	1.63	1.3	1.1995	2	0	0
2	Improvement of Adivaram Ottalangalady city Road	Rajakkad GP	Udumbanchola	0.878	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	2.37	2.97	2.2782	2.2511	58	29	0.6851
3	Improvement of Ambalappara Kadaplackal Road	Upputhara GP	Peerumedu	0.75	G.O.(Rt.)No.485 /2019/P&EA	Completed	1	1	0.8091	0.6709	100	33	0.3252
4	Improvement of Ellappallithottam bhagom Road	Arakkulam GP	Idukki	1.45	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	1.93	1.93	1.556	1.308	100	63	1.2091
5	Improvement of Ellappalli Chellikkal Road	Arakkulam GP	Idukki	5.225	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	4.33	4.33	3.4625	3.1298	65	25	1.064
6	Improvement of Pazhaya Kochira Road	Vandanmedu GP	Udumbanchola	0.55	G.O.(Rt.)No.485 /2019/P&EA	Completed	1.61	1.61	1.3136	1.2553	100	90	1.4557
7	Improvement of Vimalagiri - Enikuthu Road	Mariyapuram GP	Idukki	1.61	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	2.5	2.5	2.027	1.8182	98	75	1.8736
8	Improvement of Anachal Thokkupara Acherikunnu Asramam Road	Vellathooval GP	Devikulam	1.6	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	2.11	2.11	1.7144	1.5873	78	10	0.2128

9	Improvemnt of Murikkumthotti-Mathekkalpadi Shallyil Road	Rajakumari GP	Udumban chola	1.8	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	1.22	1.22	0.9643	0.8645	48	0	0.0026
10	Improvement of Kattekkanam Chelamoodu Road	Karunapuram GP	Udumban chola	1.9	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	0.92	0.89	0.685	0.737	15	0	0.0018
11	Improvement of Idinjamala Companyadi road	Erattayar GP	Udumban chola	8.1	G.O.(Rt.)No.485 /2019/P&EA	Completed	7.24	6.77	5.1368	5.5859	100	92	6.6792
12	Improvement of Perumbankuthu 6th mile Road	Mankulam GP	Devikulam	3.9	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	4.12	3.71	2.9094	3.1899	42	1	0.0344
13	Improvement of Kurishupallipadi Thannikkandam Painavu Road	Vazhathoppu GP	Idukki	3.5	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	3.32	3.05	2.3698	2.6029	20	13	0.4469
14	Improvement of Suryanelli Gundumala Road	Chinnakkanal GP	Devikulam	2.4	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	2.04	1.89	1.4479	1.5891	55	0	0
15	Reconstruction of Factoryadi karintharuvi Road	Upputhara GP	Peerumedu	3.3	G.O.(Rt.)No.348 /2021/P&EA	Under Construction	3.22	3.22	2.6584	2.4446	40	12	0.3984
16	Reconstruction of Suryakanthikavala Old Post office Road	Upputhara GP	Peerumedu	1.3	G.O.(Rt.)No.348 /2021/P&EA	Under Construction	1.3	1.3	1.0761	0.9889	78	0	0
17	Improvemnt of Panachikuzhi road	Rajakkad GP	Udumban chola	5.1	G.O.(Rt.)No.485 /2019/P&EA	Completed	4.42	4.42	3.3761	3.2497	100	91	4.0154
18	Improvement of Padicup Plakkayam Kuttamudi Tribal Colony road	Adimaly GP	Devikulam	4.2	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	5.06	5.06	4.0507	3.4994	40	18	0.9318

19	Improvement of Perikkankavala Kollamkulambadi Kaikavala Road	Vathikudy GP	Idukki	0.6	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	2.06	2.06	1.709	1.5678	98	74	1.5379
20	Improvement of Puthed Anoothode Footbridge Road	Arakkulam GP	Idukki	5	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	3.83	3.83	2.9954	2.9012	6	0	0
21	Balagram Anyarthulu road	Pampadumpara GP	Udumbanchola	6.4	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	7.64	7.56	5.8442	5.9702	42	1	0.1086
22	Naalumukku- Tunnelsite Road	Erattayar GP	Udumbanchola	2.75	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	2.26	2.14	1.6137	1.7247	95	15	0.3311
23	Improvement of pallikudicity Mangathupalam Road	Vathikudy GP	Idukki	1	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	2.7	2.7	2.1475	1.9673	35	53	1.4203
24	Rehabilitation of Kannamplackaladi Puthenpalam Road	Nedumkandam GP	Udumbanchola	0.86	G.O.(Rt.)No.18/2022/P&EA	Under Construction	1.13	1.1	0.8631	0.8221	33	1	0.0128
25	Thattekkallu Ponnezhuthan	Kanjikkuzhy GP	Idukki	2.205	G.O.(Rt.)No.300 /2022/P&EA	Under Construction	3.25	3.25	2.604	2.206	8	0	0
26	Bhoomiyamkulam Keshamini Road	Kanjikkuzhy GP	Idukki	1.95	G.O.(Rt.)No.300 /2022/P&EA	Under Construction	1.9	1.9	1.593	1.312	8	0	0
27	Araikkaladi Ambikavilasam Estatepadi Road	Senapathy GP	Udumbanchola	1.95	G.O.(Rt.)No.300 /2022/P&EA	Under Construction	5.65	5.65	4.598	3.815	20	0	0.0028
28	50th mile Kallakuttykudi Mankulam Road	Mankulam GP	Devikulam	2.5	G.O.(Rt.)No.485 /2019/P&EA	Tender process	8	3.602	2.85		0	0	0
29	Mangathotti Kanakapuzha NR City Road	Senapathy GP	Udumbanchola	4	G.O.(Rt.)No.485 /2019/P&EA	Submitted to Govt. for tender excess	8	7.394	5.61		0	0	0

30	Investigation /Data collection				G.O.(Rt.)No.115 /2020/P&EA	Completed	1.90		1.9027	1.3148	100	33	0.6196
31	Design and DPR preparation of 218km Roads				G.O.(Rt.)No.138 9/2020/LSGD	Completed	0.64		0.648	0.648	100	66	0.4295
32	Soil investigation of 12 bridges				G.O.(Rt.)No.234 /2021/P&EA	Completed	0.34	0.341		0.21	100	53	0.1807
33	Kallarmukku bridge	Nedumkandom GP	Udumbanchola	0.0125	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
34	Panthrandammile mezhukunnel palam and approach Road	Adimaly GP	Devikulam	0.0403	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
35	Thooval bridge	Nedumkandom GP	Udumbanchola	0.022	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
36	Upputhodu Ponnachipadi Bridge	Vathikudy GP	Idukki	0.0133	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
37	Mulakuvalli-PulavanalluKokkarakulam Bridge	Vazhathoppu GP	Idukki	0.01	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
38	Moozhikkal - Thoppilkadavu Bridge	Peruvanthanam GP	Peerumedu	0.038	G.O.(Rt.)No.221 /2020/P&EA	DPR submitted to RKI for AS	7.65				0	0	0
39	Maniyanpara - Kanjiraveli bridge	Adimaly GP	Devikulam	0.078	G.O.(Rt.)No.221 /2020/P&EA	DPR submitted to RKI for AS	5				0	0	0
40	Hanging bridge in 11th ward	Munnar GP	Devikulam	0.06	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0

41	Chittoor- Madathinkadavu	Manakkad GP	Thodupuzha	0.055	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
42	Olamattom Thekkumbhagomkadavu bridge	Edavetty GP	Thodupuzha	0.066	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
<b>TOTAL</b>				<b>78.67</b>			<b>113.13</b>	<b>91.14</b>	<b>74.11</b>	<b>62.43</b>			<b>23.98</b>

## ERNAKULAM

SI No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Status	AS Amt.	TS amt	Tender Amt.	Contract Amt.	Phy. Progress(%)	Fin. Progress (%)	Expenditure (Cr)
1	Upgradation of Pannikkuzhy Kavumthazhom Road	Vadavucode Puthencruz GP	Thrippunithura	G.O.(Rt.)No.224 /2020/P&EA	1.2	Completed	1.81	1.81	1.42	1.25	100	78	1.42
2	Rehabilitation of Pavamkulangara Kannankulangara Road	Thrippunithura	Thrippunithura	G.O.(Rt.)No.224 /2020/P&EA	1.953	Completed	1.32	1.32	0.97	0.95	100	41	0.539
3	Upgradation of Vayalodam Thadikkadavu Road	Karimannoor GP	Kalamasserry	G.O.(Rt.)No.224 /2020/P&EA	0.905	Completed	1.38	1.38	0.914	0.9138	100	72	0.988
4	Renovation of Valavazhy Road	Angamaly	Angamaly	G.O.(Rt.)No.224 /2020/P&EA	0.835	Submitted to Govt. for tender excess	0.87	0.87	0.658	0.648	0	0	0
5	Rehabilitation of Paduvathil Police station Road	Kadungalloor GP	Kalamasserry	G.O.(Rt.)No.224 /2020/P&EA	0.625	Tender process	0.66	0.66	0.5006	0.4947	0	0	0
6	Upgradation of Kadungalloor Masjid Road	Kadungalloor GP	Kalamasserry	G.O.(Rt.)No.224 /2020/P&EA	0.515	Completed	0.72	0.72	0.481	0.4809	100	65	0.469
7	Upgradation of Anicadu Pravidakunnu Road	Avoly GP	Muvattupuzha	G.O.(Rt.)No.224 /2020/P&EA	1.166	Completed	1.3	1.3	1.0883	1.075	100	81	1.051
8	Construction of Udumpuzha Chempassery Road	Kalady GP	Angamaly	G.O.(Rt.)No.224 /2020/P&EA	0.596	To be dropped	1.03	1.03	0.7666	0.739	33	0	0
9	Renovation of Okkal Juma masjid Road	Okkal GP	Perumbavoor	G.O.(Rt.)No.224 /2020/P&EA	0.165	Completed	0.166	0.166	0.1409	0.1318	100	89	0.147

10	Reconstruction of BJP Kadavu Road	Okkal GP	Perumbavoor	G.O.(Rt.)No.224 /2020/P&EA	0.18	Completed	0.12	0.12	0.1	0.0928	100	82	0.098
11	Rehabilitation of St. Mary's Swaraj Road	Kumbalangi GP	Kochi	G.O.(Rt.)No.224 /2020/P&EA	0.567	Completed	0.53136	0.6	0.501	0.501	100	51	0.272
12	Panjamkavala Ward18 Road	Chendamangalam GP	Paravur	G.O.(Rt.)No.404 /2020/P&EA	1.1	Completed	1.34	1.34	1.0426	0.997	100	74	0.992
13	Improvement of Edathod palli basilica road	Angamaly	Angamaly	G.O.(Rt.)No.62/ 2021/P&EA	1.04	Completed	0.52	0.52	0.4116	0.4039	100	88	0.455
14	Construction of Musiris Puzhayoram Road	Chendamangalam GP	Paravur	G.O.(Rt.)No.404 /2020/P&EA	0.26	Under Construction	1.08	1	0.8399	0.9156	100	0	0.0019
15	Nadakkavu Ethiyerakavu road	Vazhakulam GP	Kunnathunadu LAC	G.O.(Rt.)No.62/ 2021/P&EA	0.705	Under Construction	0.42	0.41	0.2877	0.3161	100	0	0
16	Upgradation of Kallanchery Tharassery Road	Kumbalangi GP	Kochi	G.O.(Rt.)No.18/ 2022/P&EA	1.55	Under Construction	3.1	3.1	2.5728	2.83	70	39	1.205
17	Upgradation of Thiruvaniyoor Meppadom Road	Thiruvaniyoor GP	Kunnathunadu LAC	G.O.(Rt.)No.18/ 2022/P&EA	3.1	Under Construction	3.42	3.42	2.5597	2.6811	60	27	0.93
18	Sahi Rubber Ambalamukku Kattuman Road	Edathala GP	Aluva	G.O.(Rt.)No.300 /2022/P&EA	1.325	Under Construction	1.7	1.7	1.331	1.301	100	0	0
19	Investigation/ Data collection			G.O.(Rt.)No.115 /2020/P&EA		Completed	0.2057		0.2057	0.1526	100	19	0.039
20	Soil Investigation of 9 bridges			G.O.(Rt.)No.234 /2021/P&EA		Completed	0.275	0.271			100	0	0
21	Construction of Kaipettipalam	Karimannoor GP	Kalamasserry	G.O.(Rt.)No.221 /2020/P&EA	0.028	DPR Submitted to RKI for AS	3.4				0	0	0
22	Construction of Varatupadi Colony Padi Palam	Alangad GP	Kalamasserry	G.O.(Rt.)No.221 /2020/P&EA	0.017	DPR Submitted to RKI for AS	3.85				0	0	0
23	Reconstruction of Chembikkad Madrasappadi Road	Karimannoor GP	Kalamasserry	G.O.(Rt.)No.422 /2022/P&EA	0.982	Under Construction	1.76	1.6	1.26	1.325	50	0	0.003

(Extension of Vayalodam Thadikkadavu Road)													
<b>TOTAL</b>				<b>18.81</b>		<b>31.06</b>	<b>23.34</b>	<b>18.05</b>	<b>18.19</b>				<b>8.61</b>



**THRISSUR**

SI No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Status	AS Amt.	TS Amt	Tendered Amt.	Contract Amt.	Phy. Progress(%)	Fin. Progress(%)	Expenditure (Cr)
1	Rehabilitation of Thandilam Manali Kecheri Road	Velur GP	Kunnamkulam	G.O.(Rt.)No.2 24/2020/P&EA	5	Completed	5	5	3.6692	3.6479	100	85	4.2559
2	Improvement of Chittanda Padinjattumuri Road	Erumapetty GP	Kunnamkulam	G.O.(Rt.)No.2 24/2020/P&EA	5.4	Completed	6.72	6.72	5.4	5.09	100	85	5.7032
3	Chillukarankunnu Road	Punnayurkulam GP	Guruvayoor	G.O.(Rt.)No.4 04/2020/P&EA	1.2	Completed	0.96	0.96	0.7093	0.6754	100	87	0.833
4	kuranchery Nayarangadi Road	Thekkumkara GP	Vadakkanchery	G.O.(Rt.)No.4 04/2020/P&EA	4.99	Under Construction	12.5	12.5	9.8568	9.8285	75	42	5.3012
5	Improvement of Karoorchira Anchalangadi Road	Aloor GP	Irinjalakuda	G.O.(Rt.)No.4 04/2020/P&EA	1.65	Under Construction	2.12	1.95	1.5563	1.6963	58	28	0.601
6	Rehabilitation of Paris Road	Kandanassery GP	Manalur	G.O.(Rt.)No.4 04/2020/P&EA	1.31	Under Construction	1.85	1.7	1.3425	1.4642	30	13	0.2403
7	Improvement of Puthiyakavu pozhankavu Road	Mathilakom GP	Kaipamangalam	G.O.(Rt.)No.4 04/2020/P&EA	0.84	Completed	0.823	0.75	0.6129	0.6734	100	93	0.7618
8	Rehabilitation and Reconstruction of Ex- Servicemen Colony centre Road	Athirappilli GP	Chalakkudy	G.O.(Rt.)No.6 2/2021/P&EA	2.1	Under Construction	2.76	2.6	1.9077	2.044	93	72	2.003
9	Kuzhur Iranikulam Indhira gandhi Road	Kuzhur GP	Kodungalloor	G.O.(Rt.)No.3 00/2022/P&EA	1.92	Under Construction	3.38	3.38			32	0	0.0112
10	Chottilappara Bridge	Choondal GP	Manalur	G.O.(Rt.)No.2 21/2020/P&EA	0.012	Re-tendered	2.9				0	0	0
11	Investigation/Data collection			G.O.(Rt.)No.1 15/2020/P&EA		Completed	0.3854		0.3854	0.2802	100	13	0.0493
12	Thali Viruttanam Road	Varavoor GP	Vadakkanchery	G.O.(Rt.)No.2 21/2020/P&EA	0.013	DPR Preparation					0	0	0
	<b>TOTAL</b>				<b>24.43</b>		<b>39.39</b>	<b>38.46</b>	<b>30.34</b>	<b>27.9</b>			<b>19.76</b>

## WAYANAD

SI No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Status	AS Amt.	TS amt	Tendered Amt.	Contract Amt.	Phy. Progress(%)	Fin. Progress (%)	Expenditure(Cr)
1	Chakram Colony Road	Pozhuthana GP	Kalpetta	G.O.(Rt.)No.404 /2020/P&EA	0.83	Completed	0.93	0.93	0.758	0.6821	100	65	0.6089
2	Maravayal Chathothu Road	Pozhuthana GP	Kalpetta	G.O.(Rt.)No.404 /2020/P&EA	1.29	Under Construction	1.6	1.6	1.335	1.2127	93	62	0.9878
3	Improvement of Cheriyamkolli Kalluvettumthazhe Road	Padinjarethara GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	1.9	Under Construction	1.44	1.44	1.09	1.0591	93	66	0.9504
4	Improvement of Ediyamvayal Pinangodu Road	Pozhuthana GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	2.4	Completed	2.22	2.22	1.6774	1.5423	100	56	1.2458
5	Improvement of Erumatherivu Choottakadavu Road	Mananthavady GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	1.8	Under Construction	2.6127	2.46	1.7896	1.9682	75	59	1.5475
6	Improvement of Karlad Manjoora Road	Thariod GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	2.1	Under Construction	1.89	1.89	1.4417	1.3084	100	53	0.9943
7	Improvement of Kuppadithura Millumukku Kurumani Road	Padinjarethara GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	1.5	Completed	1.45	1.45	1.1	1.1	100	73	1.0574
8	Improvement of Kottathara Kakkanchal Thekkumthara road	Kottathara GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	1.9	Under Construction	2.74	2.74	2.2526	2.2526	100	0	0
9	Improvement of Varayad Thekkumpadi Road	Muttill GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	1.3	Under Construction	1.87	1.87	1.53	1.5	93	68	1.2681

10	Improvement of Chundel Chundel estate pappala Anoth Road	Vythiri GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	5.4	Completed	5.661	5.661	4.3236	3.8668	100	57	3.2429
11	Improvement of MH Nagar - Cholapuram Road	Vengappally GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	2.7	Completed	2.4	2.4	1.8558	1.6335	100	44	1.0596
12	Improvement of Thazhe Arappetta Mankunnu Road	Muppianad GP	Kalpetta	G.O.(Rt.)No.62/ 2021/P&EA	3.656	Under Construction	4.2	4.2	3.274	3.0978	58	33	1.3799
13	Rehabilitation of Thazhathangadi Thanitheruvu Road	Pulpalli GP	Sulthan Bathery	G.O.(Rt.)No.62/ 2021/P&EA	1.33	Completed	1.2	1.2	0.9441	0.9191	100	82	0.9858
14	Improvement of Varayal - Melevarayal Road	Thavinjal GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	1.5	Under Construction	1.34	1.34	1.0106	0.979	100	56	0.7496
15	Improvement of Kattimoola Aroola Kolathada Road	Thavinhal GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	3.7	Completed	2.79	2.79	2.1266	2.0662	100	74	2.064
16	Improvement of Korome Karimbil Road	Thondernad GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	4.1	Under Construction	5.6	5.6	4.4587	4.2993	98	66	3.6821
17	Improvement of Orappu Evaranikkulam Kattimoola Road	Thavinjal GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	4.5	Completed	3.45	3.45	2.6093	2.5173	100	73	2.5097
18	Improvement of Puthiyedam Makkimala Road	Thavinjal GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	4.2	Under Construction	3.89	3.89	2.902	2.813	100	46	1.7863
19	Improvement of 44th mile Makkimala Road	Thavinjal GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	5.5	Under Construction	3.09	3.09	2.39	2.3545	33	3	0.1076
20	Improvement of Panamaram Keenjukadavu Road	Panamaram GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	4.7	Under Construction	6.22	6.22	4.8684	4.7356	48	32	1.962

21	Improvement of Pilakkavu Pancharakolli Road	Mananthavady GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	3.1	Completed	3.09	3.09	2.3803	2.3223	100	79	2.4295
22	Improvement of Kollikandam Kunneri Nelom Road	Thondernad GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	2	Under Construction	1.1275	1.1	0.7727	0.8213	93	9	0.1026
23	Improvement of Valliyurkavu Varadimoola Road	Mananthavady GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	1.6	Under Construction	1.45	1.45	1.1336	0.9963	80	46	0.6737
24	Improvement of Vilanilam Pilakkavu Road	Mananthavady GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	2.6	Under Construction	3.89	3.89	3.0935	2.787	28	15	0.5943
25	Improvement of Thannikkal Payyampalli Road	Mananthavady GP	Manant havady	G.O.(Rt.)No.485 /2019/P&EA	1.8	Under Construction	1.9861	1.91	1.4605 8	1.5557	55	8	0.1508
26	Improvement of Kalpetta Town Jilla Stadium Road	Kalpetta GP	Kalpetta	G.O.(Rt.)No.348 /2021/P&EA	3.6	Under Construction	2.97	2.97	2.1802	2.3231	93	74	2.2036
27	Eranjoli pulikkal Road	Kaniyambetta GP	Kalpetta	G.O.(Rt.)No.18/ 2022/P&EA	2.269	Under Construction	3.38	3.38	2.7585	2.6115	0	0	0
28	Improvement of Changadakadavu Chamadipoyil Road	Edavaka GP	Manant havady	G.O.(Rt.)No.18/ 2022/P&EA	1.757	Under Construction	3.04	3.04	2.3899	2.1842	93	23	0.7085
29	Investigation/ Data Collection			G.O.(Rt.)No.115 /2020/P&EA		Completed	0.7243		0.7243	0.5436	100	27	0.1943
30	Design and DPR Preparation of 218km Roads			G.O.(Rt.)No.138 9/2020/LSGD		Completed	0.3979		0.3979	0.3979	100	92	0.3647
31	CBR investigation of Roads			G.O.(Rt.)No.225 7/2020/LSGD		Completed	0.0546				100	87	0.0475
32	Topographic survey for Roads			G.O.(Rt.)No.166 9/2020/LSGD		Completed	0.0246				100	62	0.0153

33	41Mile Varayal Bridge	Thavinjal GP	Manant havady	G.O.(Rt.)No.221 /2020/P&EA	0.015	AS Recieved	2				0	0	0
<b>TOTAL</b>					<b>75.05</b>		<b>80.73</b>	<b>77.27</b>	<b>61.03</b>	<b>58.45</b>			<b>35.67</b>

## 10.LIST OF BRIDGES

Sl. No.	District	LAC	Local Body	Name of bridge	Type of Bridge	Approximate span	Remarks	Amount (Lakhs)
1	Alappuzha	Chengannur	Mannar Gp	Moorthitta Mukkatheri Vazhayi(Chackittapady Bridge)	RCC	12	AS Received & TS required	1520
2	Alappuzha	Kuttanad	Neelamperoor GP	Naduvath moon bridge	RCC	20	Design work in progress	
3	Alappuzha	Kuttanad	Nellar GP	Nellanickal Ambalam Road	RCC	35	Design work in progress	
4	Alappuzha	Kuttanad	Muttar GP	SNDP to Nadukkodu	RCC	15	Design work in progress	
5	Alappuzha	Kuttanad	Muttar GP	SNDP to Vadaparambu Culvert Road	RCC	10.5	Design work in progress	
6	Alappuzha	Haripad	Arattupuzha GP	SN Junction Tsunami Smaraka Road			Design work in progress	
7	Alappuzha	Chenganoor	Chennithala GP	Vallamkadavu Chillithuruth Swamithara Road	RCC	21	Design work in progress	
8	Idukki	Udumbunchola	Nedumkandam	Kallarmukku Bridge	RCC	12.5	Design work in progress	
9	Idukki	Devikulam	Adimaly	Panthrandam mile mezhukunel palam and approach road	RCC	40.3	Design work in progress	
10	Idukki	Udumbunchola	Nedumkandam	Thooval Bridge	RCC	22	Design work in progress	
11	Idukki	Idukki	Vathikudy GP	Upputhodu-Ponnachipadi Bridge	RCC	13.3	Design work in progress	
12	Idukki	Idukki	Vazhathoppu GP	Mulakuvalli-PulavanalluKokkarakkulam Bridge	RCC	10	Design work in progress	

13	Idukki	Peermedu	Peruvanthanam GP	Moozhikkal-Thoppilkadavu Bridge	RCC	38	DPR Submitted to RKI for AS	765
14	Idukki	Devikulam	Adimaly GP	Maniyampara-Kanjiraveli Bridge	Steel footbridge	78	DPR submitted to RKI for AS	500
15	Idukki	Devikulam	Munnar GP	Hanging Bridge in 11th Ward	Steel footbridge	60	Tendered 3 times. No response. Decided to prepare DPR in-house.	
16	Idukki	Thodupuzha	Manakkad GP	Chittoor-Madathinkadavu	Steel footbridge	55	Tendered 3 times. No response. Decided to prepare DPR in-house.	
17	Idukki	Thodupuzha	Idavetty GP	OlamattomThekkumbhagom kadavu bridge	Steel footbridge	60	Tendered 3 times. No response. Decided to prepare DPR in-house.	
18	Ernakulam	Kalamaserry	Karimalur	Construction of kaipettipalam	RCC	28	DPR submitted to RKI for AS	340
19	Ernakulam	Kalamaserry	Alangad GP	Construction of Varatupadi Coloni padi palam	RCC	17	DPR submitted to RKI for AS	385
20	Palakkad	Nenmara	Vadavannur GP	Allambalampalam road	RCC	55	DPR submitted to RKI for AS	550
21	Thrissur	Vadakkanchery	Varavoor GP	Thali Viruttanam Road	RCC	13	Design work in progress	
22	Wayanad	Mananthavady	Thovinhal GP	41-mile varayal bridge	RCC	15	AS received & TS required	200
23	Kannur	Peravoor	Aralam GP	Manchuvadu bridge	RCC	12	DPR submitted to RKI for AS	310
24	Thrissur	Manalur	Choondal GP	Chottilappara Bridge	RCC	12	Submitted to Govt. for tender excess	290
25	Alappuzha	Alappuzha	Mannancherry GP	Mannancherry Jn Puthanparambu Thaikkavu Road	RCC	9.6	Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km	

26	Alappuzha	Haripad	Pallipad GP	Anjilimoodu Sudheesh Bhavanam road	RCC	10.2	Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km	
27	Pathanamthitta	Aranmula	Mallapuzhaserry	Chakkittapadi korakodepadi road( kolakuzhy bridge)-walk way bridge	RCC	8.6	Bridge work taken up by other agency. Reported by EE PIU Kottayam	
28	Pathanamthitta	Thiruvalla	Kaloo para	Shastangal vakkayil kadavu thottipara( managed by irrigation department)	RCC	9.3	Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km	
29	Ernakulam	Muvattupuzha	Ayavana GP	Suspension bridge at Keecherikadavu	Steel footbridge	66	Bridge work taken up by other agency (PMGSY). Reported by EE PIU Thrissur	
30	Ernakulam	Kalamaserry	Eloor Municipality	Construction of pachamukku unthithodu palam and approach road	RCC	13.5	Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km	
31	Ernakulam	Kothamangalam	Kuttampuzha	Manikandanchal Vellaramkuthu St Colony road	RCC	8.5	Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km	
32	Ernakulam	Kunnathuadu	Thiruvaniyoor GP	Thiruvaniyoor Mepadam Road	RCC	8.3	No new Bridge required. Reported by EE PIU Thrissur.	
