


PROJECT MANAGEMENT UNIT-REBUILD KERALA INITIATIVE

PROGRESS REPORT OF PROJECTS

As on 03/10/2024

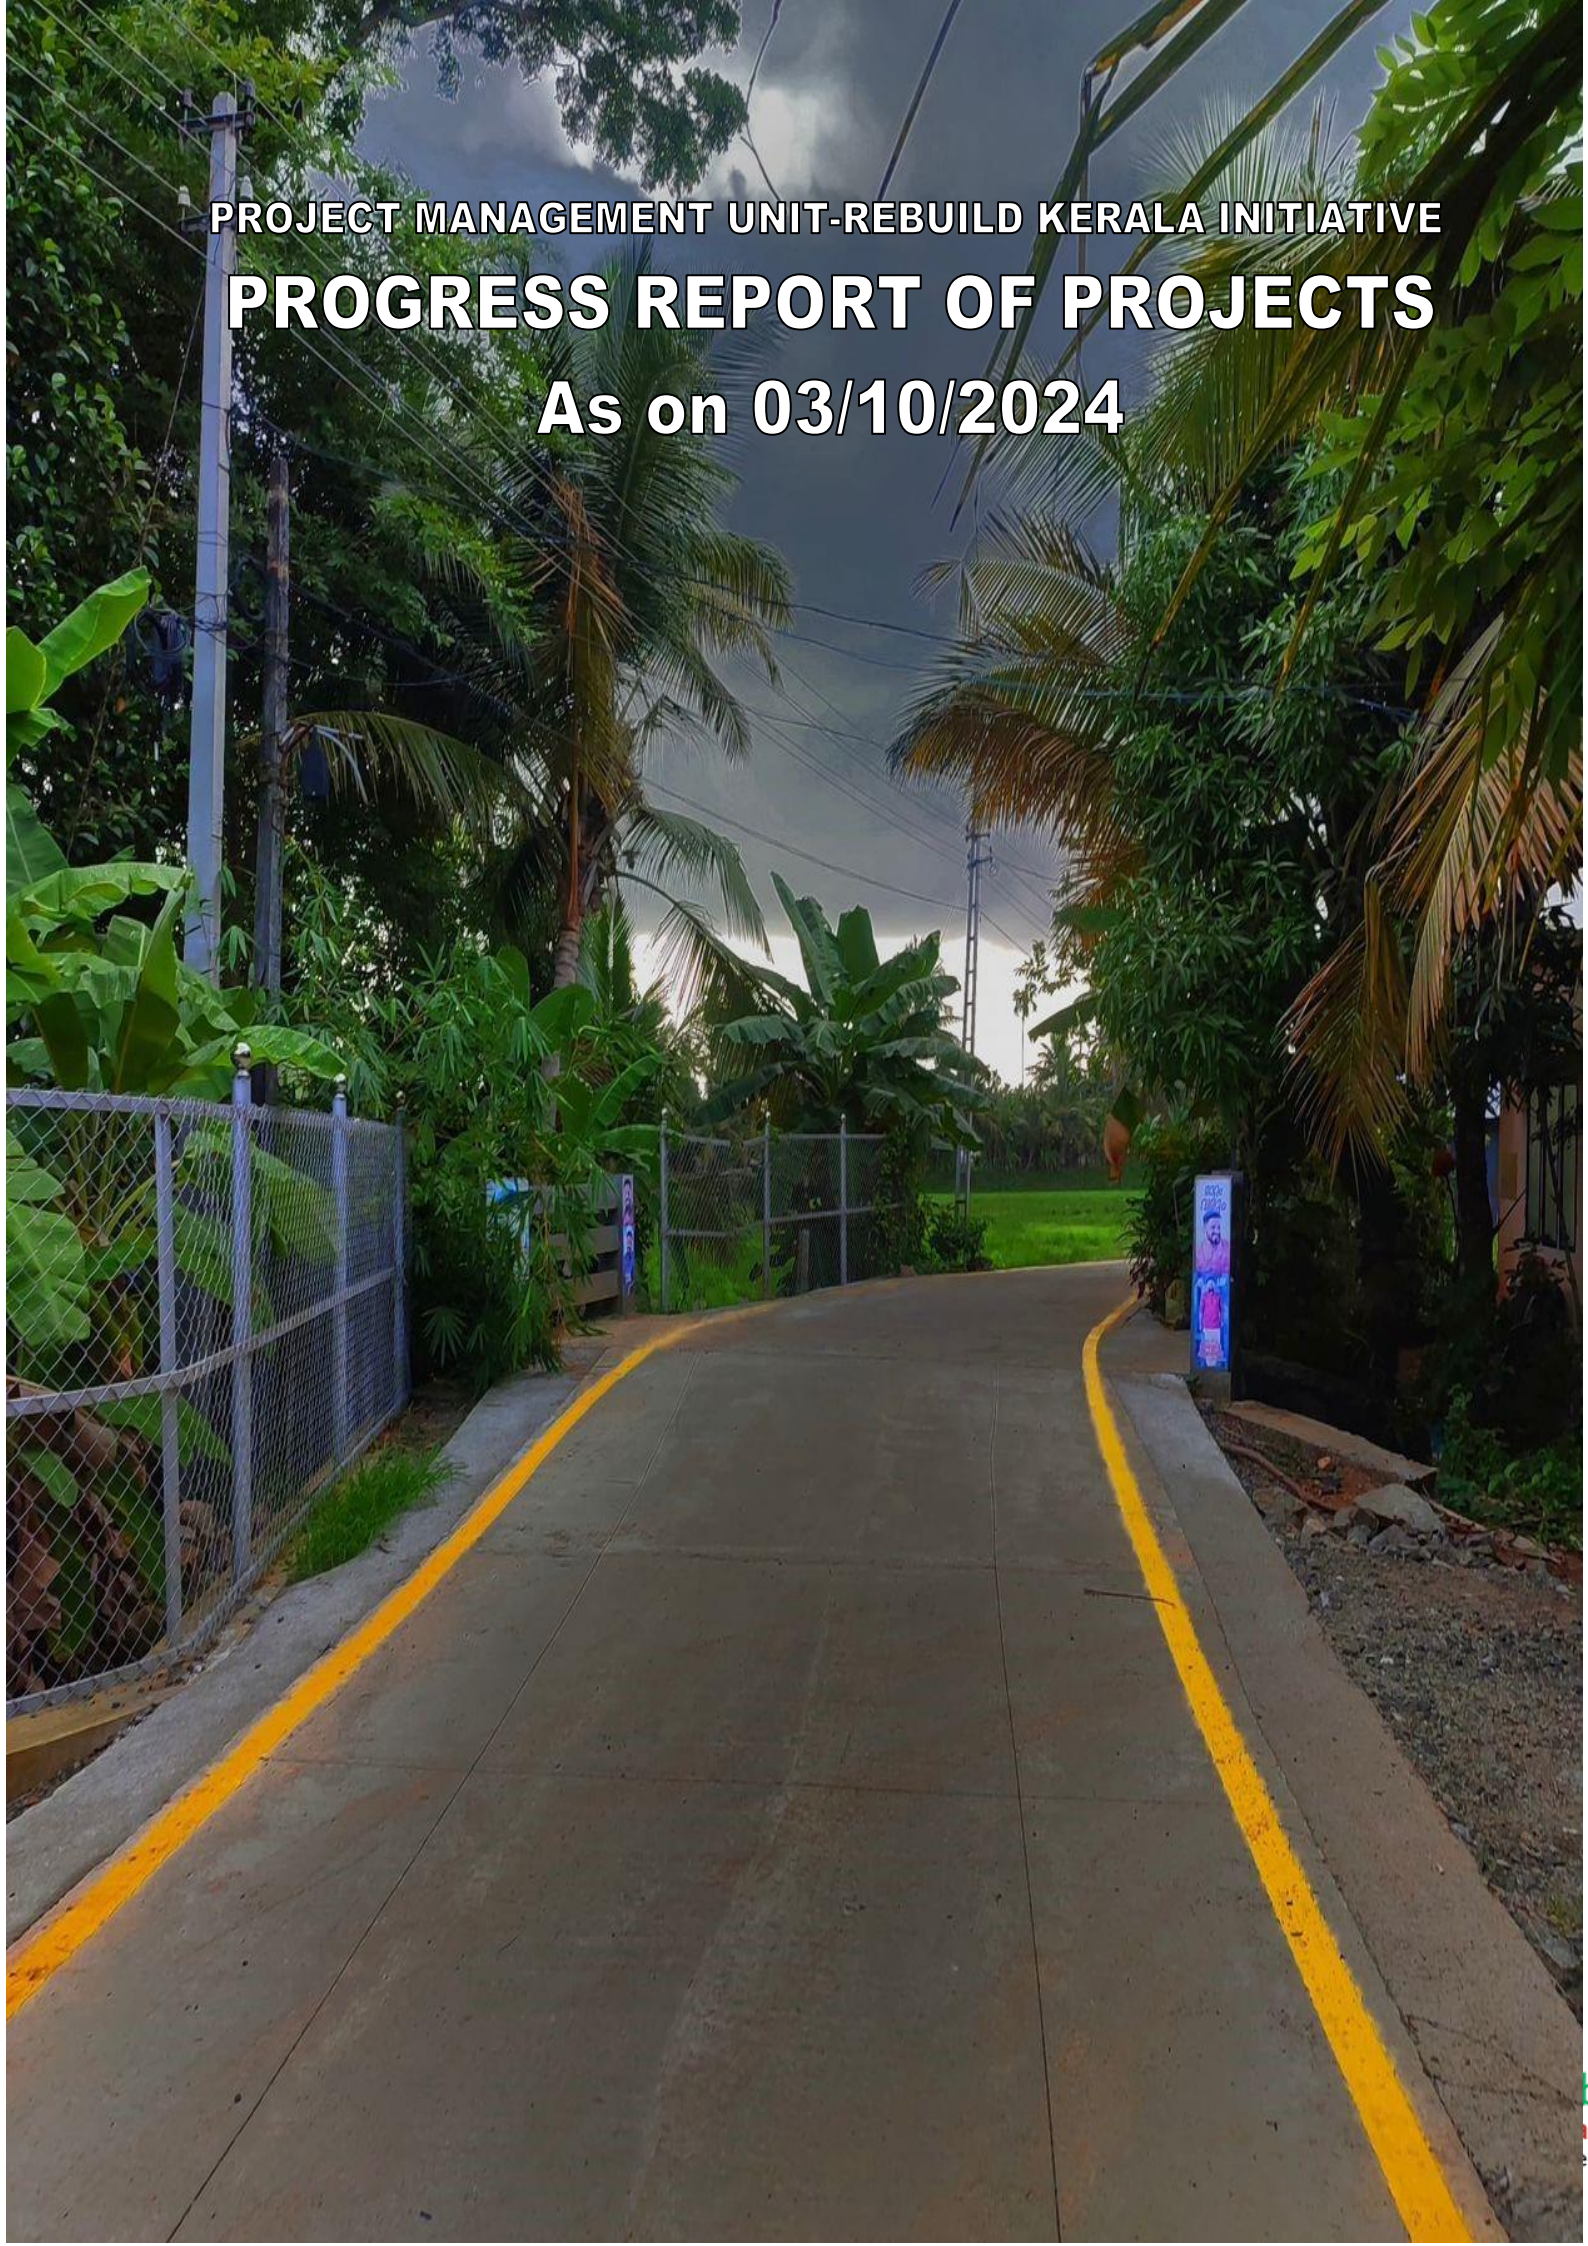


CONTENTS

1. INTRODUCTION	3
2. OVERVIEW OF STATUS OF WORKS – AS WISE	4
3. CONSOLIDATED AS WISE STATUS	5
4. LENGTHWISE DETAILS OF WORKS	6
5. OVERVIEW OF STATUS OF WORKS – DISTRICT WISE	7
6. DISTRICT WISE STATUS OF PROJECTS	8
7. FUND ALLOCATION FROM RKI	11
8. SOME PROJECT PHOTOS	12
9. LIST OF WORKS BASED ON PHYSICAL PROGRESS.....	25
10. DETAILED REPORT OF WORKS- AS WISE	35
11. DETAILED REPORT OF WORKS- DISTRICT WISE	61
12. LIST OF BRIDGES.....	83

1. INTRODUCTION

Between June 1 and 19 August 2018, our State of Kerala went through the worst ever floods in history since 1924. One sixth of the State's population — about 5.4 million of us, Keralites — were affected. The floods and the accompanying landslides were catastrophic in terms of loss of lives, livelihoods, property and infrastructure. Govt: of Kerala addressed the phenomena in a comprehensive and systematic way by formulating REBUILD KERALA DEVELOPMENT PROGRAMME, a Resilient Recovery Policy Framework and Action Plan for Shaping Kerala's Resilient, Risk-Informed Development and Recovery from 2018 Floods . The key sectors identified in the RKDP are:, Integrated Water Resource Management, Water Supply, Sanitation, Urban, Roads and Bridges, Transportation, Forestry, Agriculture, Animal Husbandry and Dairy Development, Fisheries, Livelihoods and Land.RURAL ROADS which are back bone to the rural economy were drastically affected by the flood and are given due consideration by Kerala Government. As a part of Rebuild Kerala Initiative, the Government constituted a Project Management Unit (PMU) under Local Self Government Department for the effective management of projects assigned to the department.

2. OVERVIEW OF STATUS OF WORKS – AS WISE

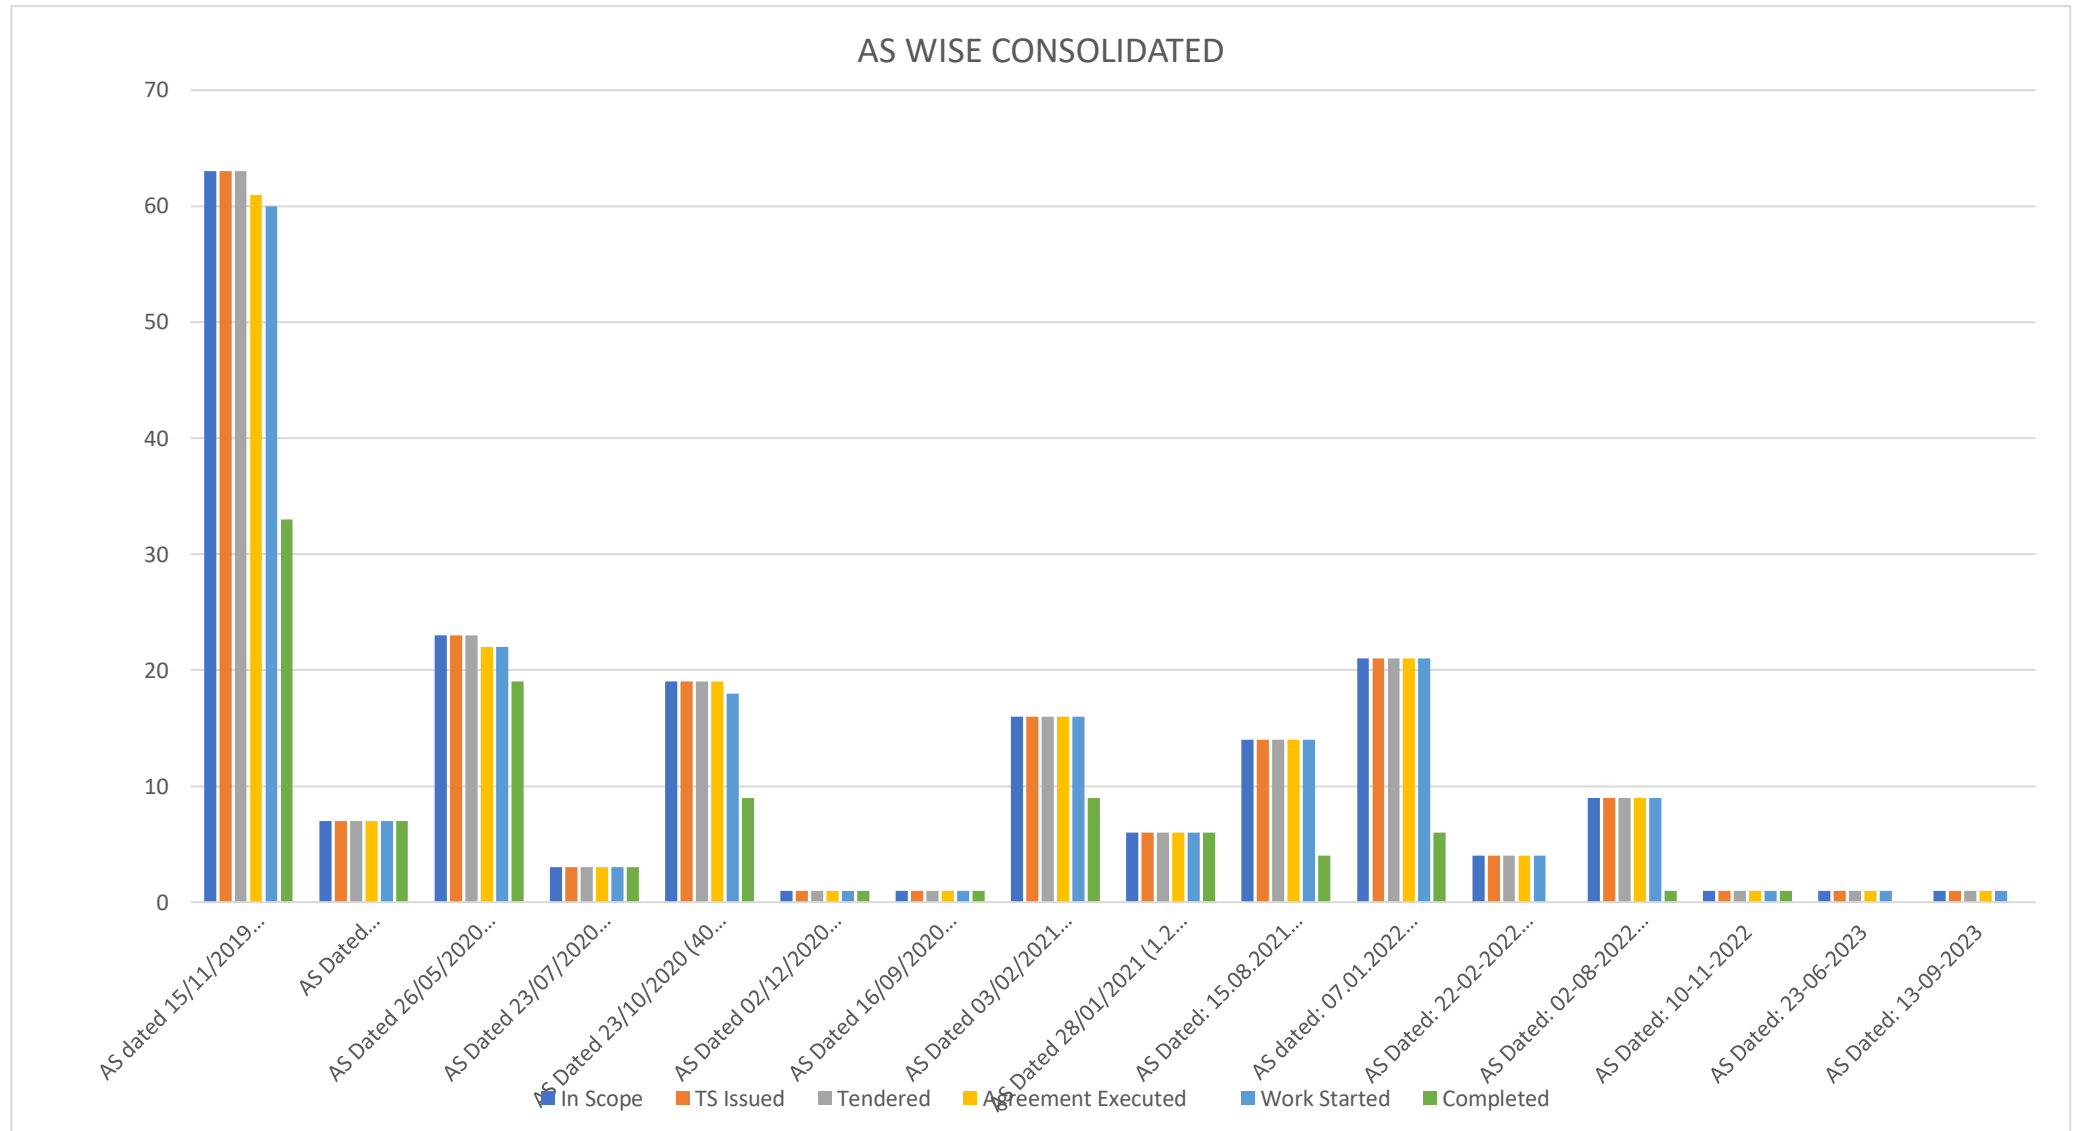


3. CONSOLIDATED AS WISE STATUS

Project Status (AS Wise Consolidated Numbers)																
Sl No	AS No	Description	AS Amount (Crores)	Actual Amount after savings	Total Nos	Drop ped	In Scope	No TS Issued	Nos Tendered	Nos Tender Excess Approval Required	Nos Agreement Executed	Nos Work Started	Nos Completed	Tender Amount (cr)	Agreement Amount(cr)	Total Expenditure (Crore)
1	GO(Rt) No 485/2019/P&EA dated 15/11/2019,	Reconstruction of various LSG roads in DBMT mode in Pathanamthitta, Idukki and Wayanad districts-77 nos,	266.306	201.33	77	14	63	63	63	0	61(2 Nos.to be retender)	60(1No. terminated)	33	133.54	123.5	94.635
2	G.O. (Rt.)No. 115/2020/P&EA, Thiruvananthapuram, Dated 28/02/2020	Conducting investigation/ data collection of roads identified in 7 districts, AS issued for 4.75 Crore, details as follows	4.75	4.75	7	0	7	7	7	0	7	7	7	4.57	3.2	1.24
3	G.O. (Rt.) No. 224/2020/P&EA, Thiruvananthapuram, Dated 26/05/2020	Rebuilding LSG Roads in 4 districts viz., Alappuzha, Kottayam, Ernakulam and Thrissur, Total AS Issued for Rs. 53.136 Crore, for 25 roads details as follows	53.136	53.136	25	2	23	23	23	0	22 (1No. tender excess received)	22	19	39.89	38.84	35.945
4	G.O.(Rt)No.1389/ 2020/ LSGD Dated, Thiruvananthapuram, 23/07/2020	Consultancy services for design and DPR preparation of flood affected roads in Pathanamthitta, Idukki and Wayanad districts, AS issued for 1.605 Crores, details as follows.	1.605	1.605	3	0	3	3	3	0	3	3	3	1.35	1.35	1.05
5	G.O. (Rt.) No. 404/2020/P&EA, Thiruvananthapuram, Dated 23/10/2020	Rebuilding LSG Roads in 5 districts viz., Alappuzha, Kottayam, Ernakulam, Thrissur and Wayanad, AS issued for Rs. 40 Core. Details as follows	40	40	21	2	19	19	19	0	19	18(1No. Terminated)	9	30.98	31.26	24.29
6	GO (Rt) No. 62/2021P&EA , Dated 03/02/2021	rebuilding 19 number of LSGD Roads in 6 districts viz., Pathanamthitta, Kottayam, Ernakulam, Alappuzha, Thrissur & Wayanad	42.32	42.32	19	3	16	16	16	0	16	16	9	30.74	31.5	27.662
7	G.O.(Rt)No.2257/2020/LSGD dated 02.12.2020	CBR Investigation of Roads in Wayanad	0.0546	0.546	1	0	1	1	1	0	1	1	1			0.048
8	GO(Rt) No 234/2021/LSGD dated 28/01/2021	Soil Investigation for Bridges	1.2	1.2	6	0	6	6	6	0	6	6	6			0.33
9	GO(Rt) No 1669/2020/LSGD dated 16.09.2020	Topographic Survey for roads in Wayanad	0.0246	0.0246	1	0	1	1	1	0	1	1	1			0.015
10	G.O.(Rt)No.348/2021P&EA, 15.08.2021	rebuilding 14 LSG Roads in 4 districts viz., Alappuzha, Pathanamthitta, Idukki and Wayanad	30.91	30.91	14	0	14	14	14	0	14	14	4	23.36	23.51	15.617
11	G.O.(Rt)No.18/2022/P&EA, 07.01.2022	rebuilding 22 number of LSGD Roads in 5 districts viz, Alappuzha, Pathanamthitta, Ernakulam, Idukki	49.34	49.34	22	1	21	21	21	0	21	21	6	39.51	40.85	18.85
12	GO (Rt) No. 405/2022/LSGD, dt: TVM 22-02-2022	Engaging consultants for Designing bridges - 31 Nos	0.721	0.721	4	0	4	4	4	0	4	4	0	0.29	0.284	0.0603
13	GO(Rt) No. 300/2022P&EA , dt: 02/08/2022	9 roads			9	0	9	9	9	0	9	9	1	17.125	15.582	5.116
14	G.O.(Rt).No.422/2022/P&EA	Extension of Vayalodam Thadikkadavu Road			1	0	1	1	1	0	1	1	1	1.266	1.325	1.154
15	G.O.(Rt).No.241/2023/P&EA, dt: 23/06/2023	Reconstruction of Chottilappara Bridge in Thrissur district	3.0877		1	0	1	1	1	0	1	1	0	2.203	2.366	0.0297
16	G.O.(Rt).No.357/2023P&EA, dt: 13/09/2023	Reconstruction of 41st mile Varayal Bridge in Wayanad district	2		1	0	1	1	1	0	1	1	0	1.588	1.436	0.0099
		Totals	495.454	425.8826	212	22	190	190	190	0	187	185	100	326.412	315.003	226.0519

4. LENGTHWISE DETAILS

SI No	AS No	Description	AS Amount (Crores)	Actual Amt (Cr)	Total No. of Works.	Length (Km)	Dropped	Length (Km)	In Scope	Length of Roads (Km)	Completed	Length (Km)
1	GO(Rt) No 485/2019/P&EA dated 15/11/2019,	Reconstruction of various LSG roads in DBMT mode in Pathanamthitta, Idukki and Wayanad districts-77 nos,	266.3055	188.62	77	218.29	14	57.315	63	160.975	33	82.306
2	G.O. (Rt.) No.224/2020/P&EA, Thiruvananthapuram, Dated 26/05/2020	Rebuilding LSG Roads in 4 districts viz., Alappuzha, Kottayam, Ernakulam and Thrissur, Total AS Issued for Rs. 53.136 Crore, for 25 roads details as follows	53.136	53.237	25	39.893	1	0.275	24	39.618	19	32.426
3	G.O. (Rt.) No.404/2020/P&EA, Thiruvananthapuram, Dated 23/10/2020	Rebuilding LSG Roads in 5 districts viz., Alappuzha, Kottayam, Ernakulam, Thrissur and Wayanad, AS issued for Rs. 40 Core. Details as follows	40	39.51	21	26.85	2	1.48	19	25.37	9	9.07
4	GO (Rt) No. 62/2021/P&EA , Dated 03/02/2021	rebuilding 19 number of LSGD Roads in 6 districts viz., Pathanamthitta, Kottayam, Ernakulam, Alappuzha, Thrissur & Wayanad	42.32	41.246	19	36.383	3	5.715	16	30.668	9	12.32
5	G.O.(Rt)No.348/2021/P&EA, 15.08.2021	rebuilding 14 LSG Roads in 4 districts viz., Alappuzha, Pathanamthitta, Idukki and Wayanad	30.91	32.09	14	22.2795	0	0	14	22.2795	4	9.037
6	G.O.(Rt)No.18/2022/P&EA, 07.01.2022	rebuilding 22 number of LSGD Roads in 5 districts viz, Alappuzha, Pathanamthitta, Ernakulam, Idukki and Wayanad	49.34	51.166	22	27.405	1	0.73	21	26.675	6	6.178
7	GO(Rt) No. 300/2022/P&EA , dt: 02/08/2022	9 roads	(-)25.85	26.893	9	16.082	0	0	9	16.082	1	1.325
8	G.O.(Rt).No.422/2022/P&EA	Extension of Vayalodam Thadikkadavu Road	(-)1.76	1.76	1	0.9	0	0	1	0.9	1	0.982
				434.522	188	388.083	21	65.515	167	322.5675	82	153.644

5. OVERVIEW OF STATUS OF WORKS – DISTRICT WISE

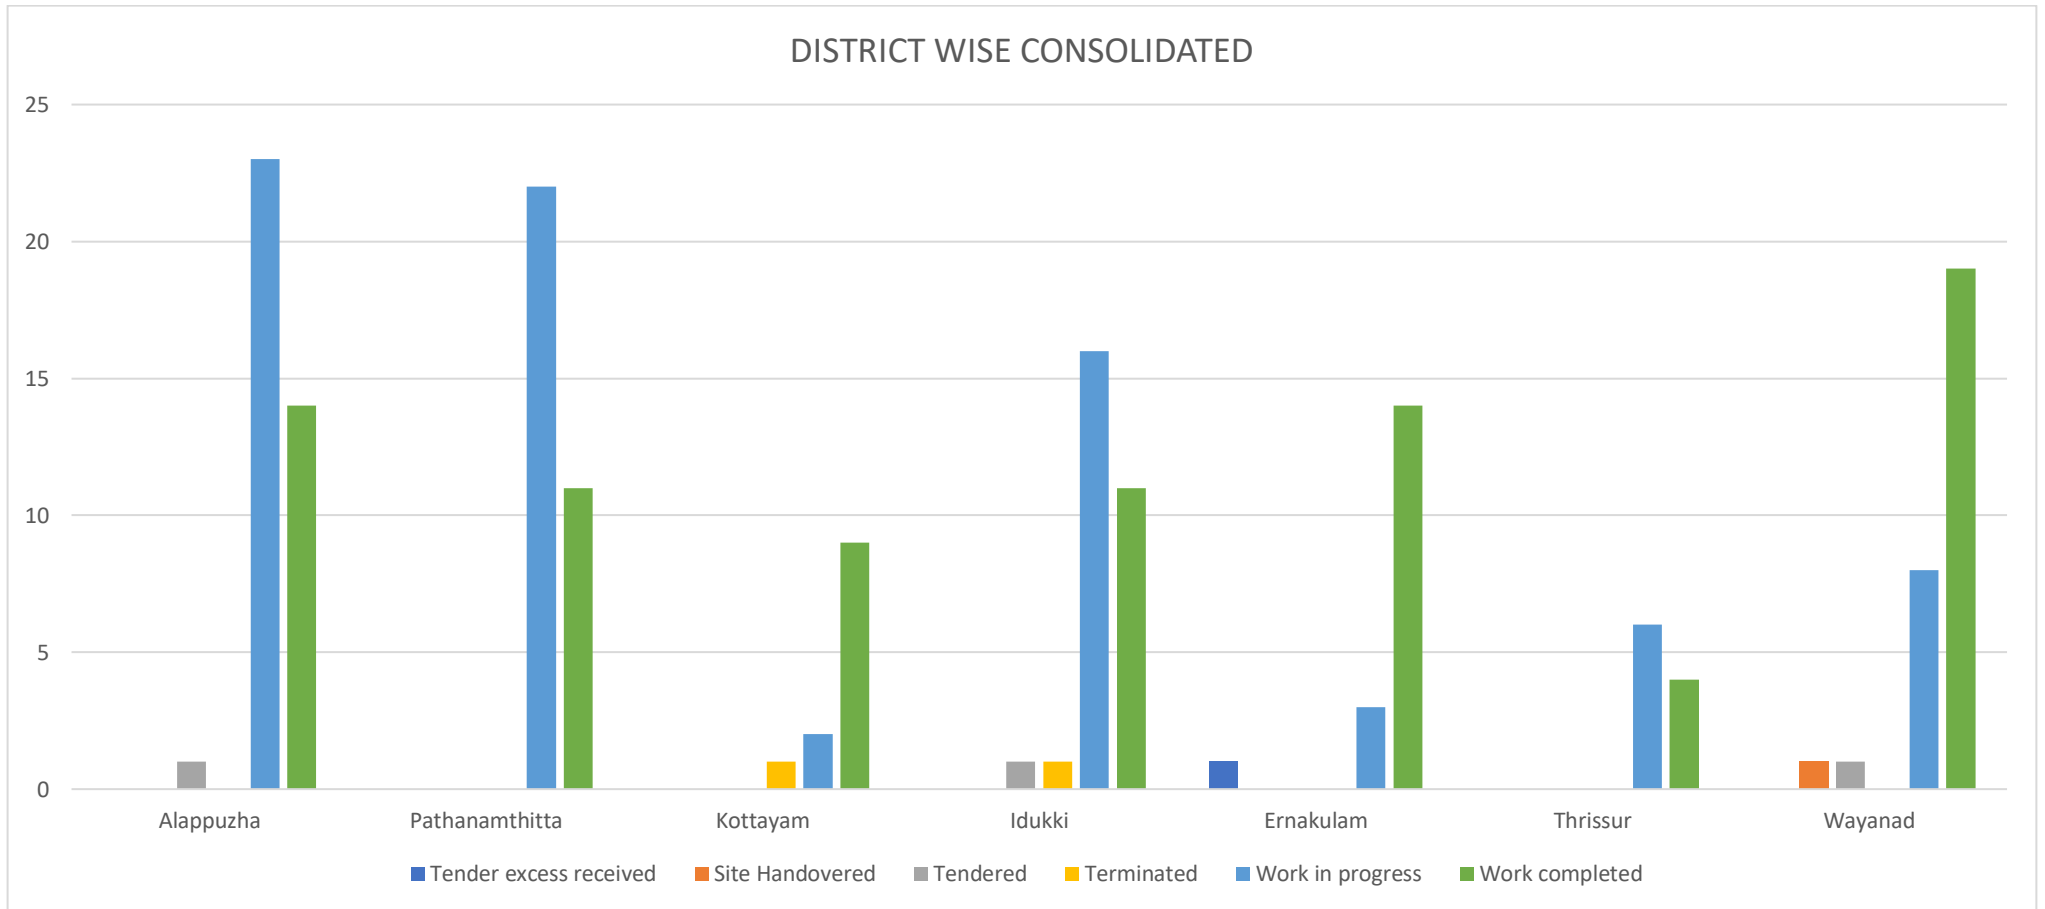

6. DISTRICT WISE STATUS OF WORKS

SI No.	Description	Alappuzha	Pathanamthitta	Kottayam	Idukki	Ernakulam	Thrissur	Wayanad	Total	Remarks
1	Tender excess received	0	0	0	0	1	0	0	1	Paduvathil Policestationpadi Road, EKM: Re-arranged at risk & cost of contractor
2	Site Handovered	0	0	0	0	0	0	1	1	Eranjoli Pulikkal Road, WYD; Site handovered
3	Tendered	1*	0	0	1	0	0	1	3	Vilanilam Pilakkavu Road, WYD: Re-arranged at risk and cost of contractor and re-tendered for balance work, The High court of Kerala issued stay to re-tender; Puthed Anoothode Road, IDK: Terminated with risk and cost of contractor and re-tendered, Writ petition pending in HC. Moorthitta Mukkatheri Bridge, ALP: Re-tendered.
5	Terminated	0	0	1	1	0	0	0	2	Asramam Pottanpadi Road, IDK: Terminated with risk and cost of contractor, Writ petition pending in HC; Olassa Cherthali road, KTM: Terminated with risk and cost of contractor
6	Work in progress	23	22	2	12	3	6*	8*	80	
7	Work Completed	14	11	9	15	14	4	19	82	
	Total	38	33	12	29	18	10	29	169	

*Bridges included

STATUS OF BRIDGES

District	Design Work in Progress	DPR Submitted to Govt.	Tendered	Under Construction	Total
Alappuzha	6	0	1	0	7
Idukki	7	2	0	0	9
Ernakulam	0	2	0	0	2
Thrissur	1	0	0	1	2
Palakkad	0	1	0	0	1
Wayanad	0	0	0	1	1
Kannur	0	1	0	0	1
Total	14	6	1	2	23

STATUS OF OTHER WORKS

SI No.	Description	G.O No.	Nos.	Status
1	Investigation/ data collection of roads in 7 districts	115/2020	7	Completed
2	Consultancy services for design and DPR preparation of roads	1389/2020	3	Completed
3	CBR Investigation of Roads in Wayanad	2257/2020	1	Completed
4	Soil Investigation for Bridges	234/2021	6	Completed
5	Topographic survey for roads in Wayanad	1669/2020	1	Completed
6	Consultancy services for design and DPR preparation of Bridges	405/2022	4	In progress
	Total		22	


7. Fund Allocation From RKI and Expenditure

FY	Fund Allocation From RKI(Cr)	Expenditure (Cr)
2019-20	1.5	0.2535
2020-21	15	4.44
2021-22	25	24.72
2022-23	73.2786	72.34
2023-24	90.27	89.881
2024-25	65	52.998
Total	270.0486	244.6325


8. Project Photos

Reconstruction of AV Mukku Sharangakkavu Road in Alappuzha

Before work

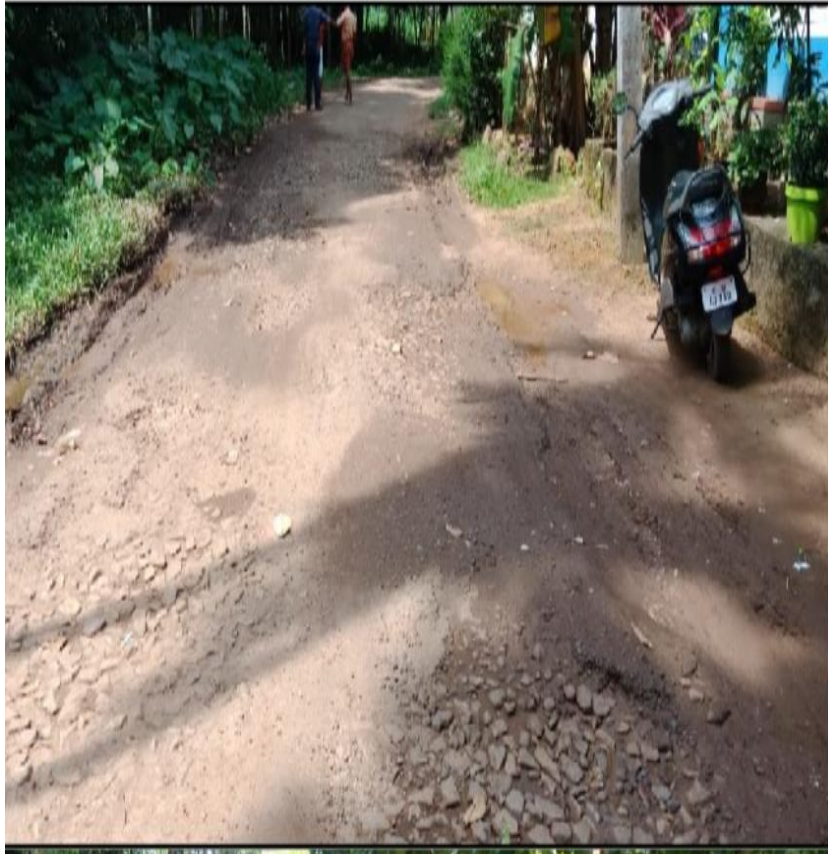

After Completion

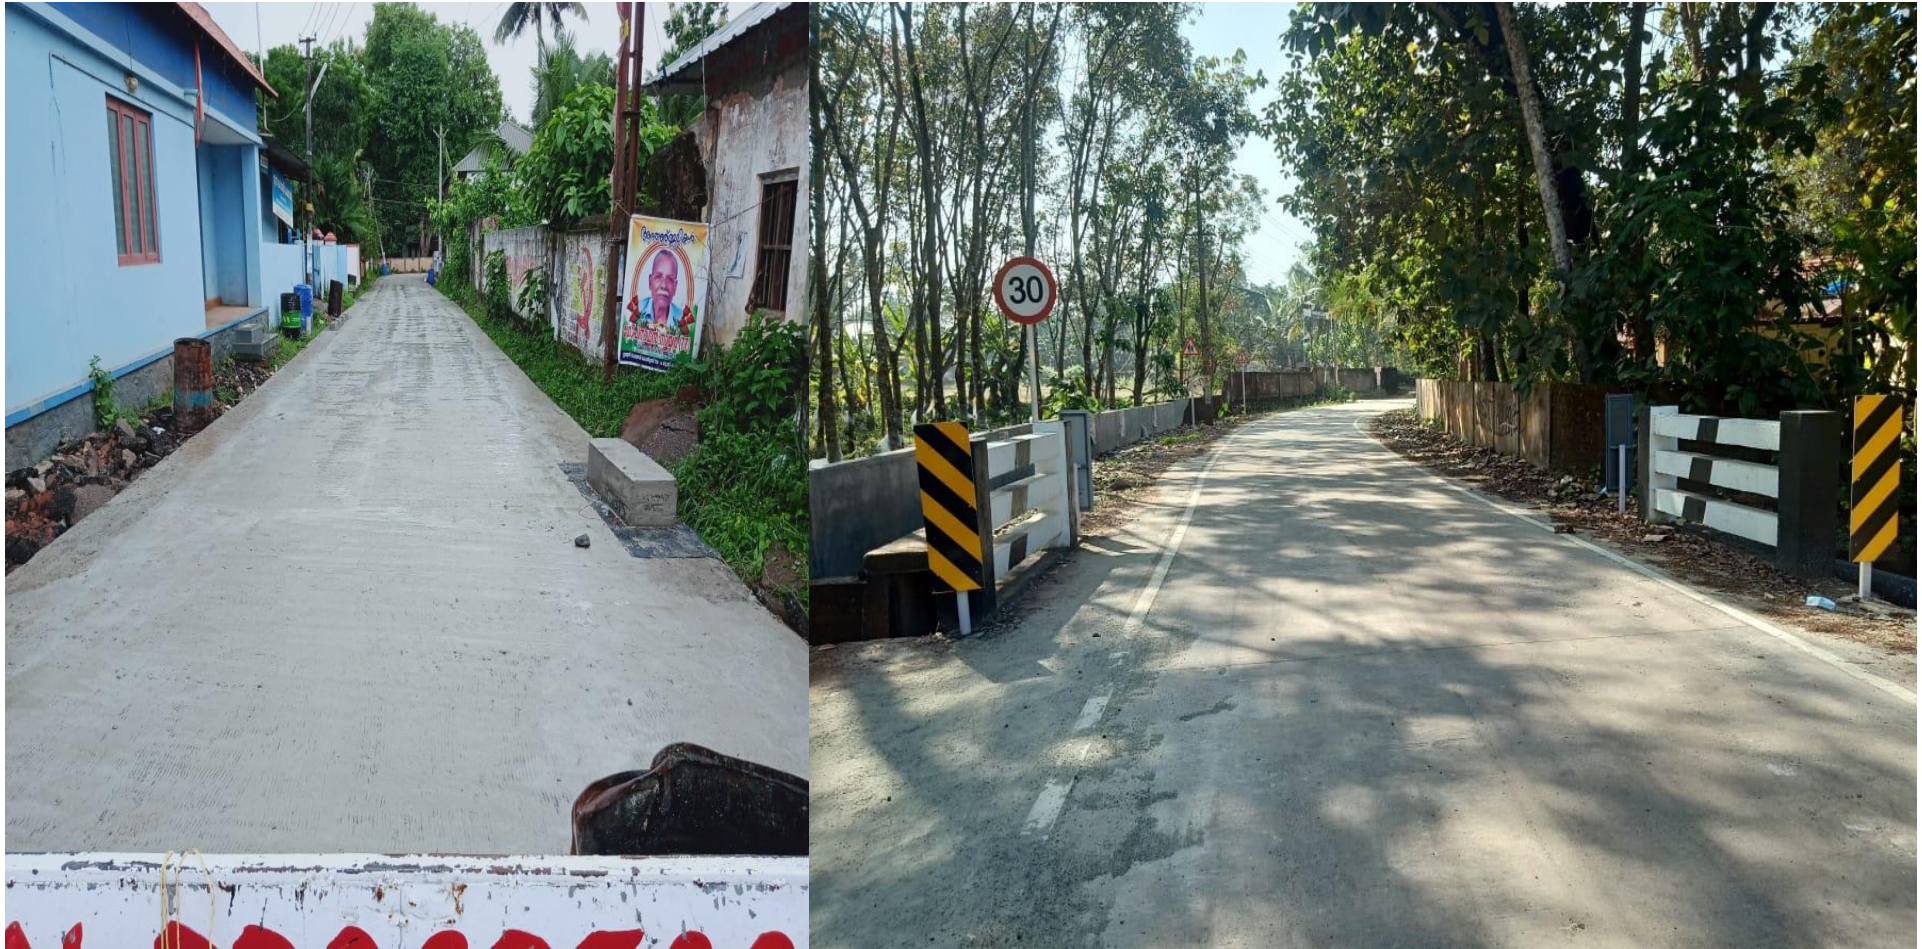

Improvement of Pilakavu - Pancharakolli Road in Mananthavady LAC, Mananthavady LSGIs, Wayanad

Before Work



After Completion



Improvement of Panachikuzhy Road in Rajakkad GP, Udumbanchola LAC, Idukki

Before Work



After Completion



IMPROVEMENT OF IDINJAMAL COMPANYPADI ROAD UDUMBANCHOLA LAC ERATTAYAR LSGI IDUKKI DISTRICT

Before Work



After Completion



RENOVATION OF KULIKKANPALAM SHAPPUPADI ROAD IN ALAPPUZHA

Before Work



After Completion



Footpath Thottuvila Road, Alappuzha



Kavumpadi to Perumal Jetty Road, Alappuzha



Pekkali Bridge to Kadakom Road, Alappuzha



PWD Road to Arakkalchira



St. Theresa's LPS Road



9. List of works based on Physical Progress

LIST OF COMPLETED WORKS					
SI No.	List of Works	District	LAC	Local Body	Length(Km)
1	Renovation of Kulikkanpalam - Shappumpadi Road	Alappuzha	Chengannur	Cheriyamad GP	1.4
2	Reconstruction of AV Mukku - Sharangakkavu Road	Alappuzha	Mavelikkara	Nooranad GP	1.48
3	Reconstruction of Pennukkara Canal Jn Nettuvaramcode Road	Alappuzha	Chengannur	Alappuzha GP	1.42
4	Upgradation of Madathekkathil Chalukkara Road	Alappuzha	Chengannur	Mulakkuzhy GP	0.375
5	Upgradation of KE Carmel Pulickal Road	Alappuzha	Cherthala	Kanjikkuzhy GP	0.892
6	Reconstruction of Parakkavu Valakkuzhy Road	Pathanamthitta	Ranni	Ezhumattoor GP	1.75
7	Improvement of Girideepam Kadathukadavu Road	Kottayam	Kottayam	Vijayapuram GP	1.86
8	Improvement of Kunnumpuram Mahilasamajam Road	Kottayam	Ettumanoor	Thiruvappu GP	1
9	Renovation of Kavanattinkara Manchira Road	Kottayam	Ettumanoor	Aymanam GP	1.3
10	Renovation of TV Puram Theeradesa Road	Kottayam	Vaikom	TV Puram GP	3.79

11	Malakkunnam Kannanthrappadi Road	Kottayam	Changanasserry	Kurichy GP	1.125
12	Improvement of Panachikkuzhy Road	Idukki	Udumbanchola	Rajakkad GP	5.1
13	Upgradation of Pannikkuzhy Kavumthazham Road	Ernakulam	Thrippunithura	Vaduvacode Puthencruz Gp	1.2
14	Upgradation of Vayalodam Thadikkadavu Road	Ernakulam	Kalamassery	Karimannoor GP	0.905
15	Upgradation of Kadungalloor Masjid Road	Ernakulam	Kalamassery	Kadungalloor GP	0.515
16	Renovation of Okkal Juma Masjid Road	Ernakulam	Perumbavoor	Okkal GP	0.165
17	Reconstruction of BJP Kadavu Road	Ernakulam	Perumbavoor	Okkal GP	0.18
18	Panjamkavala Road Ward 18	Ernakulam	Paravur	Chendamangalam GP	1.1
19	Improvement of Edathodu Palli Basilica Road	Ernakulam	Angamaly	Angamaly GP	1.04
20	Rehabilitation of Pavamkulangara Kannankulangara Road	Ernakulam	Thrippunithura	Thrippunithura GP	1.953
21	Upgradation of Anicadu Pravidakunnu Road	Ernakulam	Muvattupuzha	Avoly GP	1.166
22	Rehabilitation of Thandilam Manali Kecheri Road	Thrissur	Kunnamkulam	Velur GP	5
23	Improvement of Chittanda Padinjattumuri Road	Thrissur	Kunnamkulam	Erumappetti GP	5.4
24	Improvement of Puthiyakavu Pozhankavu Road	Thrissur	Kaippamangalam	Mathilakom GP	0.84
25	Chillukarankunnu Road	Thrissur	Guruvayur	Punnayurkulam GP	1.2
26	Chakram Colony Road	Wayanad	Kalpetta	Pozhuthana GP	0.83
27	Improvement of Kuppadithura Millumukku Kurumani Road	Wayanad	Kalpetta	Padinjarethara GP	1.5

28	Improvement of Chundel Chundel estate Pappala Anoth Road	Wayanad	Kalpetta	Vaithiry GP	5.4
29	Improvement of MH Nagar Cholapuram Road in Vengappally	Wayanad	Kalpetta	Vengappally	2.7
30	Rehabilitation of Thazhathangadi Thanitheruvu Road	Wayanad	Sulthan Bathery	Pulpally	1.33
31	Improvement of Kattimoola Aroola Kolathada Road	Wayanad	Mananthavady	Thavinjal GP	3.7
32	Improvement of Orappu Evaanikkulam Kattimoola Road	Wayanad	Mananthavady	Thavinjal GP	4.5
33	Improvement of Pilakkavu Pancharakkolli Road	Wayanad	Mananthavady	Mananthavady GP	3.1
34	Improvement of Ediyamvayal Pinangodu Road	Wayanad	Kalpetta	Pozhuthana GP	2.4
35	Improvement of AC canal to Mankuzhy Road	Alappuzha	Kuttanad	Ramankary GP	0.8
36	Rehabilitation of Mithrappuzha Vayanasalapadi Vendoorpati	Alappuzha	Chengannur	Chengannur GP	2.78
37	Kanjikkalmukku Ganam theatre road	Alappuzha	Kayamkulam	Bharanikkavu GP	1.62
38	Improvement of Pathinanchil Kadavu Illikkal Road	Kottayam	Kottayam	Kottayam	2
39	Improvement of Idinjamala Companypadi road	Idukki	Udumbanchola	Erattayar GP	8.1
40	Improvement of Illappalli Thottambhagom Road	Idukki	Idukki	Arakkulam GP	1.45
41	Kottomonpara Melekottomonpara Road	Pathanamthitta	Konni	Seethathodu GP	1.79
42	Madukkamood Ayyappa Medical College Road	Pathanamthitta	Konni	Vadasserikkara GP	1
43	Reconstruction of Bangalamkadavu Valiyakulam Road	Pathanamthitta	Ranni	Vadasserikkara GP	2
44	Improvement of Thannithode Plantation Road	Pathanamthitta	Konni	Thannithode GP	4.32

45	Rehabilitation of Valiyaparambil Eettichuvadu Road	Pathanamthitta	Ranni	Pazhavangadi GP	1.33
46	Anthyalankavu Marthomapallipadi Karamvelipadi Road	Pathanamthitta	Aranmula	Narananganam GP	0.978
47	Improvement of Pazhaya Kochira Road	Idukki	Udumbanchola	Vandanmedu GP	0.55
48	Improvement of Vimalagiri Enikuthu Road	Idukki	Idukki	Mariyapuram GP	1.61
49	Rehabilitation of St. Mary's Swaraj Road	Ernakulam	Kochi	Kumbalangi GP	0.567
50	Construction of Musiris Puzhayoram Road	Ernakulam	Paravur	Chendamangalam GP	0.26
51	Sahi Rubber Ambalamukku Kattuman Road	Ernakulam	Aluva	Edathala GP	1.325
52	Nadakkavu Ethiyerakavu Road	Ernakulam	Kunnathunadu	Vazhakkulam GP	0.705
53	Improvement of Ambalappara Kadaplakkal Road	Idukki	Peerumedu	Upputhara GP	0.75
54	Improvement of Perikkankavala Kollamkulambadi Kaikavala Road	Idukki	Idukki	Vathikudy GP	0.6
55	Naalumukku Tunnelsite Road	Idukki	Udumbanchola	Erattayar GP	2.75
56	Kambanikkadavu Pattarmadom Road	Kottayam	Ettumanoor	Ettumanoor GP	1.32
57	Cheepunkal Malikayalchira Road	Kottayam	Ettumanoor	Aymanam GP	1
58	Vattathenpady Nallathupadi Road	Pathanamthitta	Aranmula	Aranmula GP	1.17
59	Reconstruction of Govt. HS Kochalivettom Road	Kottayam	Ettumanoor	Kumarakom GP	0.4
60	Improvement of Varayal Melevarayal Road	Wayanad	Mananthavady	Thavinjal GP	1.5
61	Improvement of Karlad Manjoora Road	Wayanad	Kalpetta	Thariyodu GP	2.1
62	Improvement of Kalpetta Town Jilla Stadium Road	Wayanad	Kalpetta	Kalpetta GP	3.6

63	Improvement of Varyad Thekkumpadi Road	Wayanad	Kalpetta	Muttill GP	1.3
64	Improvement of Cheriyaankolli Kalluvettumthazhe road	Wayanad	Kalpetta	Padinjarethara GP	1.9
65	Improvement of Kottathara Kakkanchal Thekkumthara Road	Wayanad	Kalpetta	Kottathara GP	1.9
66	Improvement of Puthiyedam Makkimala Road	Wayanad	Mananthavady	Thavinjal GP	4.2
67	Improvement of Kollikandam Kunneri Nelom Road	Wayanad	Mananthavady	Thondernad GP	2
68	Improvement of Korome Karimbil Road	Wayanad	Mananthavady	Thondernad GP	4.1
69	Improvement of Changadakadavu Chamadipoyil Road	Wayanad	Mananthavady	Edavaka GP	1.757
70	St. Theresa's LPS to Nalpathil Kalinku Road	Alappuzha	Kuttanad	Kavalam GP	0.766
71	Footpath Thottuvila First Bridge to Aattutheeram Road	Alappuzha	Kuttanad	Kainakary GP	0.645
72	Reconstruction of Suryakanthikavala Old Post Office Road	Idukki	Peerumedu	Upputhara GP	1.3
73	Reconstruction of PWD Road to Araikkalchira and protection wall	Alappuzha	Kuttanad	Chambakkulam GP	0.49
74	Construction of Pekkali Bridge to Kadakom Road	Alappuzha	Kuttanad	Veliyanad GP	0.896
75	Kiliyanikkal Thoolikkulam Road	Pathanamthitta	Ranni	Cherukol GP	1.4
76	Improvement of Adivaram Ottalagalpadi city Road	Idukki	Udumbanchola	Rajakkad GP	0.878

77	Kanichukulangara Kavala Kalathilveedu Road	Alappuzha	Cherthala	Kanjikkuzhy GP	1.222
78	Chembikkad Madrasapadi Road (Vayalodam Reach 2)	Ernakulam	Kalamasseri	Karimannoor GP	0.982
79	Upgradation of Kattanam Nambukulangara Road	Alappuzha	Kayamkulam	Bharanikkavu GP	3.35
80	Reconstruction of Banglamkadavu Stadium Valiyakulam Road	Pathanamthitta	Ranni	Vadasserikkara GP	2.9
81	Reconstruction of Factorypadi Karintharuvi Road	Idukki	Peerumedu	Upputhara GP	3.3
82	Paivazhy Nediyaakala Road	Pathanamthitta	Aranmula	Thekkekkara GP	2.7

(50-99)% COMPLETED WORKS

SI No.	List of Works	District	LAC	Local Body
1	Upgradation of Ennakkad Alumoodu Elanjimel Road	Alappuzha	Chengannoor	Budhanoor GP
2	Reconstruction of Manathucad Puthuveedu Road	Alappuzha	Kuttanad	Chambakkulam GP
3	Reconstruction of Govt.Hospital Road in Kuttanad	Alappuzha	Kuttanad	Thakazhy GP
4	Chirakkarappadi-Chetalapuncha, Pmattipuncha, Pazhamchira Road	Alappuzha	Chengannur	Cheriyana GP
5	Upgradation of 45-il Puthuvelil Jetty Road	Alappuzha	Kuttanad	Thakazhy GP
6	Construction of Nalenkalpady to Kunnathuparambu Road	Alappuzha	Kuttanad	Thalavady GP
7	Upgradation of Budhanoor Ponnarathara Road	Alappuzha	Chengannoor	Budhanoor GP
8	Rehabilitation of Adoor Gopalakrishnan Road	Pathanamthitta	Adoor	Erathu Gp
9	Rehabilitation of Athikkayam Kadumeenchira Road	Pathanamthitta	Ranni	Naranamoozhy GP
10	Chana Kurumpanmoozhy Road	Pathanamthitta	Ranni	Naranammoozhy
11	Reconstruction of Melepadi Chellakkadu Road	Pathanamthitta	Ranni	Pazhavangadi GP
12	Upgradation of Thiruvaniyoor Meppadam Road	Ernakulam	Kunnathunadu	Thiruvaniyoor GP
13	Improvement of Illappalli Chellikkal Road	Idukki	Idukki	Arakkulam GP
14	Improvement of Suryanelli Gundumala Road	Idukki	Devikulam	Chinnakkana GP

15	Upgradation of Kallanchery Tharassery Road	Ernakulam	Konni	Kumbalangi GP
16	Improvement of Karrorchira Anchalangadi Road	Thrissur	Irinjalakkuda	Aloor GP
17	Improvement of Valliyurkavu Varadimoola Road	Wayanad	Mananthavady	Mananthavady GP
18	Improvement of Thannikkal Payyampally Road	Wayanad	Mananthavady	Mananthavady GP
19	Improvement of Erumatherivu-Choottakadavu Road	Wayanad	Mananthavady	Mananthavady GP
20	Holy Family School to Pazhoor Temple Road	Alappuzha	Kuttanad	Kainakari GP
21	Rehabilitation of Janaseva Road	Pathanamthitta	Thiruvalla	Peringara GP
22	Rehabilitation of Ushuspadi Vellaparamuruppu Kizhakkekkarapalli Road	Pathanamthitta	Adoor	Ezhamkulam GP
23	Kainadpally Karumathrakshethram Road	Alappuzha	Kuttanad	Neelamperoor GP
24	Construction of Amarathodu Pathilchira Road	Alappuzha	Kuttanad	Chambakkulam GP
25	Papanattupadi Panchayathupadi Road	Pathanamthitta	Ranni	Kottangal GP
26	Improvement of Perumbankuthu 6 th mile Road	Idukki	Devikulam	Mankulam GP
27	Improvement of Panamaram Keenjukuradavu Road	Wayanad	Mananthavady	Panamaram GP
28	Erathod Ashankuzhy Road	Pathanamthitta	Thiruvalla	Niranam GP
29	Renovation of CK Road	Pathanamthitta	Ranni	Kottangal GP
30	Policestationpadi TVM Hospital Road	Pathanamthitta	Konni	Konni GP

31	Kattekkanam Chelamoodu Road	Idukki	Udumpanchola	Karunapuram GP
32	Improvement of 44 th mile Makkimala Road	Wayanad	Mananthavady	Thavinjal GP
33	Anchalangadi Bridge to Mancomp Govt. LPS Road	Alappuzha	Kuttanad	Pulinkunnu GP
34	Thattekkallu Ponnezhuthan	Idukki	Idukki	Kanjikkuzhy GP
35	Arummood – Chala Puthenchantha 14 th mile Road	Pathanamthitta	Adoor	Pallikkal GP
36	Ramapuram Illathupadi Valiyathupadi Road	Pathanamthitta	Ranni	Ranni GP
37	Araikkalpadi Ambikavilasam Estatepadi Road	Idukki	Udumbanchola	Senapathy GP
38	Improvement of Padicup Plakkayam Kuttamudi Tribal Colony Road	Idukki	Devikulam	Adimaly GP
39	Improvement of Kurishupallipadi Thannikkandam Painavu Road	Idukki	Idukki	Vazhathoppu GP
40	Rehabilitation and reconstruction of Ex-servicemen Colony centre road	Thrissur	Chalakkudy	Athirappilli GP
41	Maravayal Chathothu Road	Wayanad	Kalpetta	Pozhuthana GP
42	Kuranchery Nayarangadi Road	Thrissur	Vadakkanchery	Thekkumkara GP
43	Renovation of Chakrasalakadavu Panachimoottil Road	Pathanamthitta	Thiruvalla	Kuttoor GP
44	Improvement of Thazhe Arappetta Mankunnu Road	Wayanad	Kalpetta	Muppianad GP
45	Renovation of Panchayathupadi Pulluchani Radhapadi Road	Pathanamthitta	Konni	Aruvappulam GP
46	Improvement of Anachal Thokkupara Road	Idukki	Devikulam	Vellathooval GP

47	Balagram Anyarthulu Road	Idukki	Udumpanchola	Pampadumpara GP
48	Reconstruction of Palangattupadi Mannarathara Road	Alappuzha	Chengannoor	Pondanad GP
49	Manenkaripadi to Kodumkuthuparambu Road	Alappuzha	Kuttanad	Chambakkulam GP
50	Improvement of Murikkumthotti Mathekkalpadi Shalilyil Road	Idukki	Udumbanchola	Rajakumari GP
51	Reconstruction of Panachamoodu Kochuveetilmukku Road	Alappuzha	Harippad	Cheppad GP
52	Improvement of Pallikkudicity Mangattupalam Road	Idukki	Idukki	Vathikudy GP
53	Upgradation of Highschool Jn. Nannad Eradichira Road	Alappuzha	Chengannoor	Thiruvandoor GP
54	Upgradation of Kavumpadi to Perumal Jetty Road	Alappuzha	Kuttanad	Kavalam GP
55	Rehabilitation of Ozhukkuneettilpadi Paruthimoottilpadi Road	Pathanamthitta	Thiruvalla	Peringara GP
56	Reconstruction of Kannankara Edamuri Road	Pathanamthitta	Ranni	Pazhavangadi GP
57	Karichira to Puthusseri Road	Alappuzha	Ambalappuzha	Ambalappuzha South GP



**DETAILED REPORT OF
WORKS-
AS WISE**

G.O.(Rt.)No.224/2020/P&EA dated 26-05-2020(53.136cr)

SI No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress(%)	Fin.progress(%)	Expenditure(Cr)
1	Upgradation of Ennakkad Alumood Elanjimel road in Budhanoor GP in Alappuzha	Alappuzha	Under construction	6.39	4.9438	4.8004	80	29	1.8655
2	Rehabilitation of Thandilam Manali Kecheri road in Thrisur	Thrisur	Completed	5	3.6692	3.6479	100	85	4.282
3	Upgradation of Budhanoor Ponnathara road in Alappuzha	Alappuzha	Under construction	2.91	2.37	2.3	85	38	1.108
4	Renovation of Kulikkanpalam Shappumpadi road in Alappuzha	Alappuzha	Completed	2.78	2.06	1.8871	100	73	2.0342
5	Reconstruction of AV Mukku Sharangakkavu road in Alappuzha	Alappuzha	Completed	2.82	2.0495	1.873	100	71	1.9991
6	Reconstruction of Pennukkara Canal Jn Nettuvaramcode Road in Alappuzha	Alappuzha	Completed	2.99	1.8603	1.6985	100	68	2.0396
7	Upgradation of Pannikkuzhy Kavumthazham road in Ernakulam	Ernakulam	Completed	1.81	1.42	1.25	100	79	1.431

8	Improvement of Girideepam kadathukadavu road in Kottayam	Kottayam	Completed	1.75	1.2935	1.2392	100	85	1.4958
9	Rehabilitation of Pavamkulangara Kannankulangara Road in ernakulam	Ernakulam	Completed	1.32	0.97	0.95	100	41	0.5383
10	upgradation of Vayalodam Thadikkadavu Road in Ernakulam	Ernakulam	Completed	1.38	0.914	0.9138	100	72	0.9881
11	Renovation of Valavazhy Road in Ernakulam	Ernakulam	Under Construction	0.9596	0.658	0.648	2	0	0
12	Rehabilitation of Paduvathil police station Road	Ernakulam	Tender excess received	0.66	0.5006	0.4947	0	0	0
13	Upgradation of Kodungalloor masjid road	Ernakulam	Completed	0.72	0.481	0.4809	100	66	0.4736
14	Improvement of Padinjattumuri Chittanda Road	Thrissur	Completed	6.72	5.4	5.09	100	85	5.74
15	Improvement of Pathinanchilkadavu Illikkal road	Kottayam	Completed	4	2.9446	2.9301	100	87	3.491
16	Improvement of Kunnumpuram Mahilasamajam Road	Kottayam	Completed	1.84	1.3434	1.3247	100	78	1.4322
17	Upgradation of Anicadu Pravidakunnu Road	Ernakulam	Completed	1.3	1.0883	1.075	100	81	1.0517

18	Renovation of Okkal Juma Masjid Road	Ernakulam	Completed	0.166	0.1409	0.1318	100	89	0.1474
19	Reconstruction of BJP Kadavu road	Ernakulam	Completed	0.12	0.1	0.0928	100	82	0.0982
20	Rehabilitation of St. Mary's Swaraj road	Ernakulam	Under construction	0.53136	0.501	0.501	100	51	0.2696
21	Renovation of Kavanattinkara Manchira road	Kottayam	Completed	0.93	0.6712	0.6501	100	90	0.8393
22	Renovation of TV Puram Theeradesa road	Kottayam	Completed	3.84	2.9401	3.2337	100	100	3.5851
23	Malakkunnam Kannanthrappadi road	Kottayam	Completed	1.27	0.8096	0.8898	100	87	1.0352
	Total			53.237	39.8956	38.8415			35.945

G.O.(Rt.)No.485/2019/P&EA dated 15-11-2019(266.03Cr) Pathanamthitta

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress(%)	Fin.progress(%)	Expenditure(Cr)
1	Rehabilitation of Adoor Gopalakrishnan road	Pathanamthitta	Under Construction	2.7581	1.8977	1.9534	78	60	1.473
2	Renovation of CK Road	Pathanamthitta	Under Construction	2.82	1.7836	1.8925	70	28	0.657
3	Paivazhy Nediya kala road	Pathanamthitta	Completed	4.2017	2.7723	3.0208	100	72	3.025
4	Renovation of Chakrasalakadavu Panachimoottil road	Pathanamthitta	Under Construction	2.95	2.094	2.2824	98	71	2.091
5	Improvement of Thannithode Plantation road	Pathanamthitta	Completed	5.94	4.0737	4.2613	100	68	4.07
6	Reconstruction of Bangalamkadavu Stadium Valiyakulam Road	Pathanamthitta	Under Construction	2.46	1.873	1.8728	100	50	1.24
7	Reconstruction of Bangalamkadavu Valiyakulam road	Pathanamthitta	Completed	2.14	1.6814	1.6433	100	91	1.94
8	Chana Kurumpanmoozhy road	Pathanamthitta	Under Construction	2.19	1.7904	1.7007	90	79	1.736
9	Madukkamood Ayyappa Medical College Road	Pathanamthitta	Completed	1.39	1.1821	1.0639	100	81	1.125

10	Ratiokadappadi Mulanthanam Road	Pathanamthitta	Under Construction	1.49	1.0919	1.1288	35	0	0
11	Arumood Chala Puthenchantha 14th mile	Pathanamthitta	Under Construction	2.0679	1.3583	1.4787	95	16	0.2927
12	Anthyalankavu Marthomapallipadi Karamvelipadi road	Pathanamthitta	Completed	1.47	1.0759	1.1079	100	89	1.313
13	Kiliyanikkal Thoolikkulam road	Pathanamthitta	Under Construction	1.73	1.1108	1.2585	100	59	1.02
14	Reconstruction of Parakkavu Valakkuzhy road	Pathanamthitta	Completed	2.13	1.4124	1.5535	100	74	1.4521
15	Reconstruction of Melepadi Chellakkadu road	Pathanamthitta	Under Construction	2.23	1.649	1.7181	80	56	1.25
16	Erathodu Ashankuzhy road	Pathanamthitta	Under Construction	2.09	1.5591	1.6152	70	31	0.6039
17	Vattathempady Nallathupadi Road	Pathanamthitta	Completed	1.15	0.704	0.8133	100	100	1.8411
18	Poovanmala Panamplackal Road	Pathanamthitta	Under Construction	1.19			2	0	0
19	Reconstruction of Kalarikode Pallana Puthenvelipadi Road	Pathanamthitta	Under Construction	1.96			5	0	0
	Total			44.3577	29.1096	30.3651			25.13

G.O.(Rt.)No.485/2019/P&EA dated 15-11-2019(266.03Cr) Idukki

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Improvement of Ashramam Pottanpadi road	Idukki	Terminated	1.5945	1.3	1.1995	0	0	0
2	Improvement of Adivaram Ottalangepadi City road	Idukki	Completed	3.12	2.2782	2.2511	100	71	2.21
3	Improvement of Ambalappara kadaplakkal road	Idukki	Completed	0.877	0.8091	0.6709	100	33	0.3252
4	Improvement of Illappalli Thottambhagom road	Idukki	Completed	1.73	1.556	1.308	100	88	1.53
5	Improvement of Illappalli Chellikkal Road	Idukki	Under Construction	4.67	3.4625	3.1298	72	28	1.322
6	Improvement of Pazhaya Kochira Road	Idukki	Completed	1.63	1.3136	1.2553	100	90	1.4557
7	Improvement of Vimalagiri Enikuthu Road	Idukki	Completed	2.38	2.027	1.8182	100	79	1.89
8	Improvement of Anachal Thokkupara - Acherikkunnu Asramam road	Idukki	Under Construction	2.24	1.7144	1.5873	98	10	0.2128
9	Improvement of Murikkumthotti Mathekkalpadi Shaliliyil road	Idukki	Under Construction	1.26	0.9643	0.8645	98	0	0.0026
10	Improvement of Kattekkanam Chelamood Road	Idukki	Under Construction	0.9808	0.685	0.737	60	0	0.0018
11	Improvement of Idinjamala Companipadi road	Idukki	Completed	7.87	5.1368	5.5859	100	92	6.6792
12	Improvement of Perumbankuthu 6th mile road	Idukki	Under Construction	4.44	2.9094	3.1899	70	24	1.065

13	Improvement of Kurushupallipadi thannikandam painavu road	Idukki	Under Construction	3.61	2.3698	2.6029	60	19	0.684
14	Improvement of Surianelly Gundumala road	Idukki	Under Construction	2.21	1.4479	1.5891	65	21	0.466
15	Improvement of Panachikuzhy Road	Idukki	Completed	4.57	3.3761	3.2497	100	91	4.0154
16	Improvement of Padicup Plakkayam Kuttamudi Tribal Colony road	Idukki	Under Construction	4.66	4.0507	3.4994	65	18	0.9318
17	Improvement of Perikkankavala Kollamkulambadi Kaikavala road	Idukki	Completed	1.98	1.709	1.5678	100	93	1.85
18	improvement of Puthed Anoorthodu Footbridge road	Idukki	Terminated	3.95	2.9954	2.9012	0	0	0
19	Balagram Anyarthulu road	Idukki	Under Construction	8.66	5.8442	5.9702	95	56	4.83
20	Naalumukku Tunnelsite road	Idukki	Completed	2.47	1.6137	1.7247	100	84	2.075
21	Improvement of Pallikkudicity Mangattupalam road	Idukki	Under Construction	2.62	2.1475	1.9673	98	53	1.4203
22	50th mile Kallakuttikudi Mankulam road	Idukki	Under construction	3.86	2.85		2	0	0
23	Mangathotti Kanakapuzha NR city road	Idukki	Under Construction	7.59	5.61		28	3	0.244
	Total			78.9723	58.17	48.6697			33.211

G.O.(Rt.)No.485/2019/P&EA dated 15-11-2019(266.03Cr) Wayanad

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Improvement of Cheriyaankolli Kalluvettumthazhe road	Wayanad	Completed	1.52	1.09	1.0591	100	66	0.9504
2	Improvement of Idiyamvayal Pinangodu road	Wayanad	Completed	2.22	1.6774	1.5423	100	77	1.707
3	Improvement of Erumatherivu Choottakadavu road	Wayanad	Under Construction	2.87	1.7896	1.9682	85	59	1.5475
4	Improvement of Karlad Manjoora Road	Wayanad	Completed	1.89	1.4417	1.3084	100	53	0.9943
5	Improvement of Kuppadithura Millumukku Kurumani road	Wayanad	Completed	1.44	1.1	1.1	100	74	1.06
6	Improvement of Kottathara Kakkanchal Thekkumthara road	Wayanad	Completed	2.57	2.25	2.2526	100	57	1.5582
7	Improvement of Varyad Thekkumadi road	Wayanad	Completed	1.92	1.53	1.5	100	68	1.2681
8	Improvement of Chundel Chundel estate Pappala Anoth Road	Wayanad	Completed	5.56	4.3236	3.8668	100	74	4.12
9	Improvement of MH Nagar Cholapuram Road	Wayanad	Completed	2.33	1.8558	1.6335	100	80	1.86
10	Improvement of Varayal Melevarayal road	Wayanad	Completed	1.39	1.0106	0.979	100	67	0.9

11	Improvement of Kattimoola Aroola Kottathala road	Wayanad	Completed	2.95	2.1266	2.0662	100	74	2.0604
12	Improvement of Korome Karimbil road	Wayanad	Completed	5.82	4.4587	4.2993	100	84	4.87
13	Improvement of Orappu Evaranikkulam Kattimoola road	Wayanad	Completed	3.63	2.6093	2.5173	100	82	2.997
14	Improvement of Puthiyedam Makkimala Road	Wayanad	Completed	4.08	2.902	2.813	100	78	3.0403
15	Improvement of 44th mile Makkimala Road	Wayanad	Under Construction	3.31	2.39	2.3545	80	3	0.1076
16	Improvement of Panamaram Keenjukadavu palakunnu road	Wayanad	Under Construction	6.61	4.8684	4.7356	75	47	3.114
17	Improvement of Pilakkavu pancharakolli road	Wayanad	Completed	3.31	2.3803	2.3223	100	79	2.4295
18	Improvement of Killokandam Kunneri Nelom road	Wayanad	Completed	1.24	0.7727	0.8213	100	9	0.1026
19	Improvement of Valliurkavu Varadimoola road	Wayanad	Under Construction	1.39	1.1336	0.9963	80	62	0.8622
20	Improvement of Vilanilam pilakkavu Road	Wayanad	Stay to re-tender	3.84	3.0935	2.787	28	15	0.5943
21	Improvement of Thannikkal Payyampalli Road	Wayanad	Under Construction	2.26	1.46058	1.5557	75	8	0.1508
	Total			62.15	46.26438	44.4784			36.294

G.O.(Rt.)No.115/2020/P&EA dated 28-02-2020(4.75Cr)

SI No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress(%)	Expenditure(Cr)
1	Investigation / Data Collection-Pathanamthitta	Pathanamthitta	Completed	0.4152	0.4152	0.2768	100	30%	0.1261
2	Investigation / Data Collection-Alappuzha	Alappuzha	Completed	0.8174	0.8174	0.5449	100	24%	0.1977
3	Investigation / Data Collection-Kottayam	Kottayam	Completed	0.1208	0.1208	0.0951	100	13%	0.0156
4	Investigation / Data Collection-Idukki	Idukki	Completed	1.9027	1.9027	1.3148	100	33%	0.6196
5	Investigation / Data Collection-Ernakulam	Ernakulam	Completed	0.2057	0.2057	0.1526	100	19%	0.0396
6	Investigation / Data Collection-Thrissur	Thrissur	Completed	0.3854	0.3854	0.2802	100	13%	0.0493
7	Investigation / Data Collection-Wayanad	Wayanad	Completed	0.7243	0.7243	0.5436	100	27%	0.1943
	Total			4.5715	4.5715	3.208			1.2422

G.O.(Rt.)No.1389/2020/LSGD dated 23-07-2020(1.605Cr)

SI No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Design and DPR Preparation of 218Km Roads in Idukki	Idukki	Completed	0.648	0.648	0.648	100	66	0.4295
2	Design and DPR Preparation of 218Km Roads in Pathanamthitta	Pathanamthitta	Completed	0.3074	0.3074	0.3074	100	83	0.254
3	Design and DPR Preparation of 218Km Roads in Wayanad	Wayanad	Completed	0.3979	0.3979	0.3979	100	92	0.3647
	Total			1.3533	1.3533	1.3533			1.0482

G.O.(Rt.)No.404/2020/P&EA dated 23-10-2020(40Cr)

SI No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Olassa Cherthali road	Kottayam	Terminated	1.21	1.0104	0.9829	65	33	0.395
2	Kambanikkadavu Pattarmadom road	Kottayam	Completed	1.14	0.9258	0.8885	100	90	1.0211
3	Chakram Colony Road	Wayanad	Completed	0.93	0.758	0.6821	100	66	0.6111
4	maravayal Chathothu road	Wayanad	Under Construction	1.6	1.335	1.2127	93	66	1.054
5	Kanjikkalmukku Ganam Theatre road	Alappuzha	Completed	2.14	1.6332	1.6294	100	64	1.3582
6	Reconstruction of AC Canal to Mankuzhy Road	Alappuzha	Completed	1.2485	0.9364	1.0205	100	95	1.097
7	Chirakkappadi Chetalpuncha, Pmattipuncha, Pazhamchira road	Alappuzha	Under Construction	3.48	2.8405	2.6804	65	55	1.913
8	Reconstruction of Manathucadu Puthuveedu Road and Protection	Alappuzha	Under Construction	2.1311	1.6692	1.7855	70	61	1.229
9	Reconstruction of Madathilkadavu Mahilasamajam Kandathilpalli Road	Kottayam	Under Construction	1.5431	1.2218	1.3046	2	0	0
10	Cheepunkal Malikayalchira Road	Kottayam	Completed	1.48	1.2318	1.2195	100	94	1.3864
11	Panjamkaval Ward18 road	Ernakulam	Completed	1.34	1.0426	0.997	100	74	0.9923

12	Chillukarankunnu Road	Thrissur	Completed	0.96	0.7093	0.6754	100	86	0.833
13	Kuranchery Nayarangadi Road	Thrissur	Under Construction	12.5	9.8568	9.8285	96	83	10.388
14	Reconstruction of LPS Mukkam Koller Road	Kottayam	Under Construction	0.562	0.4275	0.4683	45	1	0.0033
15	Harbour road to Manaladi Jetti Road	Alappuzha	Under Construction	1.36	1.0376	1.141	10	0	0
16	Improvement of Karoorchira Anchalangadi road	Thrissur	Under Construction	2.12	1.5563	1.6963	58	28	0.601
17	Rehabilitation of Paris Road	Thrissur	Under Construction	1.85	1.3425	1.4642	30	13	0.2403
18	Construction of Musiris Puzhayoram road	Ernakulam	Completed	1.08	0.8399	0.9156	100	37	0.4035
19	Improvement of Puthiyakavu pozhankavu Road	Thrissur	Completed	0.82255	0.6129	0.6734	100	93	0.7618
	Total			39.5078	30.9875	31.2658			24.288

G.O.(Rt.)No.62/2021/P&EA dated 03-02-2021(42.32Cr)

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Renovation of Kottomonpara Melekottomonpara Pandyanpara Road	Pathanamthitta	Completed	2.48	2.0038	1.9291	100	64	1.5917
2	Improvement of Edathod palli Basilica Road	Ernakulam	Completed	0.52	0.4116	0.4039	100	88	0.4554
3	Improvement of Thazhe Arappetta Mankunnu Road	Wayanad	Under Construction	4.2	3.274	3.0978	93	64	2.71
4	Rehabilitation of Thazhathangadi-thanitheruvu road	Wayanad	Completed	1.2	0.9441	0.9191	100	82	0.9858
5	Reconstruction of PWD Road to Araikkalchira and Protection Wall	Alappuzha	Completed	1.22	1.0262	1.025	100	81	0.987
6	Reconstruction of Govt.HS kochalivettom Road	Kottayam	Under Construction	0.306	0.2259	0.2482	99	98	0.299
7	Upgradation of Madathekkathil Chaalukkara Road	Alappuzha	Completed	0.29	0.2138	0.2316	100	89	0.259
8	Rehabilitation of Mithrappuzha vyanasalapadi Vendoorpadi Road	Alappuzha	Completed	3.6	2.6043	2.8365	100	93	3.3289
9	Upgradation of Kattanam Nambukulangara Road	Alappuzha	Completed	3.48	2.5671	2.8214	100	62	2.174
10	Reconstruction of Palangattupadi Mannarathara Road	Alappuzha	Under Construction	2.73	2.0215	2.2216	97	76	2.07
11	Reconstruction of Panachimoodu Kochuveettilmukku Road	Alappuzha	Under Construction	3.55	2.631	2.8892	95	80	2.853
12	Upgradation of Highschool Nannad Eradichira Road	Alappuzha	Under Construction	5.7	4.4847	4.7721	95	59	3.383

13	Rehabilitation and Reconstruction of Ex- Serviceman Colony Centre road	Thrissur	Under Construction	2.76	1.9077	2.044	98	81	2.24
14	Nadakkavu Ethiyerikkavu Road	Ernakulam	Completed	0.42	0.2877	0.3161	100	62	0.268
15	Rernovation of Panchayathupadi Pulluchani Radhapadi Road	Pathanamthitta	Under Construction	4.41	3.2808	3.597	95	77	3.141
16	Renovation of Police stationpadi TVM Hospital Elangavettom Kshethram Road	Pathanamthitta	Under Construction	2.78	1.9547	2.1454	60	23	0.643
	Total			39.646	29.8389	31.498			27.66

G.O.(Rt.)No.2257/2020/LSGD dated 02-12-2020(0.0546Cr)

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	CBR Investigation of Roads in Wayanad	Wayanad	Completed	0.0546			100	87	0.0475
	Total			0.0546					0.0475

G.O.(Rt.)No.234/2021/LSGD dated 28-01-2021(1.2 Cr)

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Soil Investigation for bridges in TSR/PKD/ALP/WYD/KNR		Completed	0.2001		0.2001	100	14	0.0289
2	Soil Investigation in Pathanamthitta 3 bridges	Pathanamthitta	Completed	0.06			100	0	0
3	Soil Investigation in Alappuzha 10 bridges	Alappuzha	Completed	0.25			100	34	0.0859
4	Soil Investigation in Kottayam 2 bridges	Kottayam	Completed	0.04			100	80	0.0319
5	Soil Investigation in Idukki 12 bridges	Idukki	Completed	0.34		0.21	100	53	0.1807
6	Soil Investigation in Ernakulam 9 bridges	Ernakulam	Completed	0.275			100	0	0
	Total			1.1651		0.4101			0.3274

G.O.(Rt.)No.1669/2020/LSGD dated 16-09-2020(0.0246 Cr)

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Topographic survey for roads in Wayanad	Wayanad	Completed	0.0246			100	62	0.0153
	Total			0.0246					0.0153

G.O.(Rt.)No.348/2021/P&EA dated 15-08-2021(30.91 Cr)

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Rehabilitation of Athikkayam Kaddumeenchira Road	Pathanamthitta	Under Construction	3.05	1.8423	1.8506	75	34	1.034
2	Reconstruction of Factorypadi Karintharuvi Road	Idukki	Completed	3.22	2.6584	2.4446	100	77	2.473
3	Reconstruction of Suryakanthikavala Old postoffice Road	Idukki	Under Construction	1.3	1.0761	0.9889	100	58	0.754
4	Rehabilitation of Valiyaparambil Eetichuvadu Road	Pathanamthitta	Completed	1.7	1.1769	1.1664	100	61	1.0448
5	Rehabilitation of Janaseva Road	Pathanamthitta	Under Construction	3.1	2.3319	2.3218	50	24	0.7588
6	Improvement of Kalpetta Town Jilla Stadium Road	Wayanad	Completed	3.026	2.1802	2.3231	100	78	2.35
7	Rehabilitation of Ushuspadi Vellaparamuruppu Kizhakkekkarapalli Road	Pathanamthitta	Under Construction	2.25	1.5712	1.6261	90	50	1.12
8	Upgradation of 45-il Puthuvel Jetty Road	Alappuzha	Under Construction	2.1834	1.6508	1.7983	60	41	0.818
9	Reconstruction of Govt. Hospital Road	Alappuzha	Under Construction	2.3572	1.8226	1.9648	65	71	1.665
10	Construction of Nalenkalpadi to Kunnathuparambu Road	Alappuzha	Under Construction	2.1629	1.6008	1.7636	60	48	0.9504

11	Construction of Manenkarypadi to Kodumkuthuparambu Road	Alappuzha	Under Construction	1.4647	1.0432	1.1407	95	79	1.155
12	Ambiyathupadi Ikkara Boatjetty Road	Alappuzha	Under Construction	3.94	2.8969	3.186	30	18	0.718
13	Reconstruction of Kannankara Idamuri Road	Pathanamthitta	Under Construction	1.23	0.8596	0.9451	95	63	0.776
14	Malayuman Vazhayilpadi Road	Pathanamthitta	Under Construction	1.11	0.6512		20	0	0
	Total			32.0492	23.3621	23.52			15.62

G.O.(Rt.)No.18/2022/P&EA dated 07-01-2022(49.34 Cr)

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Rehabilitation of Koipalli Melethilpadi Road	Pathanamthitta	Under Construction	1.44	1.1745	1.1146	4	0	0
2	Rehabilitation of Ozhukkuneettilpadi Paruthimoottilpadi Road	Pathanamthitta	Under Construction	3.47	2.3329	2.25	95	42	1.4719
3	Rehabilitation of Kannamplackalpadi Puthenpalam Road	Idukki	Under Construction	1.13	0.8631	0.8221	42	22	0.254
4	Upgradation of KE Carmel Pulikkal Road	Alappuzha	Completed	0.99	0.7717	0.7461	100	91	0.8972
5	Upgradation of Kavumpadi to Perumal Jetty Road	Alappuzha	Under Construction	2.01	1.7106	1.5968	95	68	1.366
6	Karichira to Puthusseri Road	Alappuzha	Under Construction	2.61	2.2172	2.1828	50	34	0.90
7	St. Therasas LPS to Nalpathikalinku Road	Alappuzha	Completed	1.74	1.4799	1.4097	100	84	1.47
8	Eranjoli Pulikkal Road	Wayanad	Site handedover	3.38	2.7585	2.6115	0	0	0
9	Improvement of Changadakadavu Chamadipoyi Road	Wayanad	Under Construction	3.04	2.3899	2.1842	93	57	1.7436
10	Upgradation of Kallanchery Tharasseri Road	Ernakulam	Under Construction	3.39	2.5728	2.83	90	39	1.2059
11	Upgradation of Thiruvaniyoor Meppadam Road	Ernakulam	Under Construction	3.57	2.5597	2.6811	85	58	2.074

12	Anchalangadi Bridge to Mancomp LPS Road	Alappuzha	Under Construction	3.53	2.7025	2.9652	70	46	1.62
13	Construction of Amarathodu Pathilchira Road	Alappuzha	Under Construction	2.74	2.1142	2.3232	50	40	0.9904
14	Construction of Pekkali Bridge to Kadakam Road	Alappuzha	Under Construction	0.9857	0.7924	0.8225	100	80	0.7596
15	Upgradation of PS Kavala Chudukattumpuram Chooramana Road	Alappuzha	Under Construction	3.49	2.6942	2.9633	2	0	0
16	Construction of Kumaramkari Society Road	Alappuzha	Under Construction	4.12	3.2144	3.492	30	15	0.5746
17	Therambilpadi Road	Alappuzha	Under Construction	2.65	1.988	2.1868	40	0	0
18	Footpath Thottuvila First Bridge to Aattutheeram Road	Alappuzha	Completed	1.62	1.262	1.375	100	74	1.197
19	Kanichukulangara kavala Kalathilveedu Road	Alappuzha	Completed	1.81	1.263	1.387	100	43	0.7734
20	Kainadpally Karumathra Kshethram Road	Alappuzha	Under Construction	1.98	1.5102	1.6555	60	73	0.8472
21	Holy family School to Pazhoor Temple Road	Alappuzha	Under Construction	1.47	1.143	1.253	90	48	0.703
	Total			51.1657	39.5147	40.8519			18.85

G.O.(Rt.)No.300/2022/P&EA dated 02-08-2022(25.85Cr)

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Valiyapalli Kayalpuram School Road	Alappuzha	Under Construction	4.83			6	0	0
2	Ramapuram Illathupadi Valiyathupadi Road	Pathanamthitta	Under Construction	0.92	0.626	0.652	95	0	0
3	Pulikeezhu Road	Pathanamthitta	Under Construction	3.04	2.14	2.26	15	0	0
4	Papanattupadi Panchayathupadi Road	Pathanamthitta	Under Construction	2.22	1.533	1.531	50	32	0.707
5	Thatttekallu Ponnezhuthan	Idukki	Under Construction	3.25	2.604	2.206	50	17	0.566
6	Bhoomiyamkulam Keshamini Road	Idukki	Under Construction	1.9	1.593	1.312	15	10	0.193
7	Araikkalpathi Ambikavilasam Estatepadi Road	Idukki	Under Construction	5.65	4.598	3.815	50	26	1.464
8	Sahi Rubber Ambalamukku Kattuman Road	Ernakulam	Completed	1.7	1.331	1.301	100	82	1.3937
9	Kuzhur Iranikulam Indira Gandhi Road	Thrissur	Under Construction	3.38	2.7	2.505	48	23	0.792
	Total			26.89	17.125	15.582			5.116

G.O.(Rt.)No.405/2022LSGD dated 22-02-2022(0.721Cr)

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress	Fin.progress (%)	Expenditure(Cr)
1	Consultancy Services for design and Preparation of DPR of Bridges	Alappuzha	DPR Preparation		0.0923	0.0905	In progress	17	0.0156
2	Consultancy Services for design and Preparation of DPR of Bridges	Ernakulam, Thrissur	DPR Preparation		0.0401	0.0397	In progress	26	0.0105
3	Consultancy Services for design and Preparation of DPR of Bridges	Idukki	DPR Preparation		0.0998	0.0978	In progress	19	0.0192
4	Consultancy Services for design and Preparation of DPR of Bridges	Kannur, Palakkad ,Wayanad	DPR Preparation		0.0579	0.0567	In progress	26	0.015
	Total				0.2901	0.2847			0.0603

G.O.(Rt.)No.422/2022/P&EA dated 10-11-2022(1.6Cr)

Sl No	Name of Work	District	Physical Status	AS Amt(Cr)	Tendered Amt(Cr)	Contract Amt(Cr)	Phy.progress (%)	Fin.progress (%)	Expenditure(Cr)
1	Reconstruction of Chembikkad Madrasappadi Road(Vayalodam Thadikkadavu Reach II)	Ernakulam	Completed	1.76	1.266	1.325	100	65	1.154
	Total			1.76					1.154



DETAILED REPORT OF WORKS- DISTRICT WISE

ALAPPUZHA

Sl No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Physical Status	AS Amt.	TS amt	Tendered Amt.	Contract Amt.	Phy. Progress (%)	Fin. Progress (%)	Expenditure(Cr)
1	Upgradation of Ennakkad Alumood Elanjimel Road	Budhanoor GP	Chengannoor	G.O.(Rt).No.22 4/2020/P&EA	3.225	Under Construction	6.39	6.39	4.9438	4.8004	80	29	1.8655
2	Upgradation of Budhanoor Ponnathara Road	Budhanoor GP	Chengannoor	G.O.(Rt).No.22 4/2020/P&EA	1.933	Under Construction	2.91	2.91	2.37	2.3	85	38	1.108
3	Renovation of Kulikkanpalam Shappumpadi Road	Cheriyana GP	Chengannoor	G.O.(Rt).No.22 4/2020/P&EA	1.4	Completed	2.78	2.78	2.06	1.8871	100	73	2.0351
4	Reconstruction of AV mukku - Sharangakkavu Road	Nooranad GP	Mavelikkara	G.O.(Rt).No.22 4/2020/P&EA	1.48	Completed	2.82	2.82	2.0495	1.873	100	71	1.9991
5	Reconstruction of Pennukkara Canal Jn. Nettuvaramcode Road	Ala GP	Chengannoor	G.O.(Rt).No.22 4/2020/P&EA	1.42	Completed	2.99	2.99	1.8603	1.6985	100	68	2.0411
6	Kanjikkalmukku Ganam Theatre Road	Bharanikavu GP	Kayamkulam	G.O.(Rt).No.40 4/2020/P&EA	1.62	Completed	2.14	2.14	1.6332	1.6294	100	64	1.3582
7	Reconstruction of AC Canal to Mankuzhy Road	Ramankary GP	Kuttanad	G.O.(Rt).No.40 4/2020/P&EA	0.8	Completed	1.25	1.15	0.9364	1.0205	100	95	1.097
8	Chirakkarappadi-Chetalapuncha-Pmattipuncha, Pazhamchira Road	Cheriyana GP	Chengannoor	G.O.(Rt).No.40 4/2020/P&EA	2.75	Under Construction	3.48	3.48	2.8405	2.6804	65	55	1.913
9	Reconstruction of Manathucadu-Puthuveedu Road	Chambakulam GP	Kuttanad	G.O.(Rt).No.40 4/2020/P&EA	1.15	Under Construction	2.13	2	1.6692	1.7855	70	61	1.229

10	Reconstruction of PWD Road to Araikalchira and Protection wall	Chambakkulam GP	Kuttanad	G.O.(Rt).No.62 /2021/P&EA	0.49	Completed	1.22	1.22	1.0262	1.025	100	81	0.987
11	Harbour road to Manaladi Jetty Road	Ramankary GP	Kuttanad	G.O.(Rt).No.40 4/2020/P&EA	2	Under Construction	1.36	1.24	1.0376	1.141	10	0	0.00
12	Upgradation of Madathekkathil Chalukkara Road	Mulakuzha GP	Chengannoor	G.O.(Rt).No.62 /2021/P&EA	0.375	Completed	0.29	0.27	0.2138	0.2316	100	89	0.259
13	Rehabilitation of Mithrapuzha Vyanasalapadi Vendoorpadi Road	Chengannoor GP	Chengannoor	G.O.(Rt).No.62 /2021/P&EA	2.78	Completed	3.6	3.32	2.6043	2.8365	100	93	3.3289
14	Upgradation of Kattanam Nambukulangara Road	Bharanikkavu GP	Kayamkulam	G.O.(Rt).No.62 /2021/P&EA	3.35	Completed	3.48	3.17	2.5671	2.8214	100	62	2.174
15	Reconstruction of Palangattupadi Mannarathara Road	Pondanad GP	Chengannoor	G.O.(Rt).No.62 /2021/P&EA	1.6	Under Construction	2.73	2.49	2.0215	2.2216	97	76	2.07
16	Reconstruction of Panachamoodu Kochuveettilmukku Road	Cheppad GP	Haripad	G.O.(Rt).No.62 /2021/P&EA	2.59	Under Construction	3.55	3.24	2.631	2.8892	95	80	2.853
17	Upgradation of Highschool Nannad Eradichira Road	Thiruvandoor Gp	Chengannoor	G.O.(Rt).No.62 /2021/P&EA	2.4	Under Construction	5.7	5.37	4.4847	4.7721	95	59	3.383
18	Upgradation of 45-il Puthuvellil Jetty Road	Thakazhy GP	Kuttanad	G.O.(Rt).No.34 8/2021/P&EA	1.295	Under Construction	2.18	2.01	1.6508	1.7983	60	41	0.818
19	Reconstruction of Govt. Hospital Road	Thakazhy GP	Kuttanad	G.O.(Rt).No.34 8/2021/P&EA	1.02	Under Construction	2.36	2.19	1.8226	1.9648	65	71	1.665
20	Construction of Nalenkalpadi to Kunnathuparambu Road	Thalavady GP	Kuttanad	G.O.(Rt).No.34 8/2021/P&EA	0.913	Under Construction	2.16	1.98	1.6008	1.7636	60	48	0.956

21	Construction of Manenkarypadi to Kodumkuthuparambu Road	Chambakkulam GP	Kuttanad	G.O.(Rt).No.34/2021/P&EA	0.742	Under Construction	1.46	1.35	1.0432	1.1407	95	79	1.155
22	Ambiyathupadi Ikkara Boat jetty Road	Edathva GP	Kuttanad	G.O.(Rt).No.34/2021/P&EA	2.55	Under Construction	3.94	3.6	2.8969	3.186	30	18	0.718
23	Upgradation of KE Carmel Pulickal Road	Kanjikkuzhy GP	Cherthala	G.O.(Rt).No.18/2022/P&EA	0.892	Completed	0.99	0.99	0.7717	0.7461	100	91	0.8972
24	Upgradation of Kavumpadi to Perumal Jetty Road	Kavalam GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	0.865	Under Construction	2.01	2.01	1.7106	1.5968	95	68	1.366
25	Karichira to Puthusseri Road	Ambalapuzha South GP	Ambalappuzha	G.O.(Rt).No.18/2022/P&EA	1.23	Under Construction	2.61	2.61	2.2172	2.1828	50	34	0.90
26	St. Therasas LPS to Nalpathil Kalinku Road	Kavalam GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	0.766	Completed	1.74	1.74	1.4799	1.4097	100	84	1.47
27	Anchalangadi Bridge to Mancomp Govt.LPS Road	Pulinkunnu GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	1.365	Under Construction	3.53	3.22	2.7025	2.9652	70	46	1.62
28	Construction of Amarathod Pathilchira Road	Chambakkulam GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	1.125	Under Construction	2.74	2.5	2.1142	2.3232	50	40	0.9904
29	Construction of Pekkali Bridge to Kadakom Road	Veliyanad GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	0.896	Under Construction	0.98	0.95	0.7924	0.8225	100	80	0.7596
30	Upgradation of PS Kavala chudukattumpuram Chooramana Road	Thycattussey GP	Aroor	G.O.(Rt).No.18/2022/P&EA	0.9	Under Construction	3.49	3.17	2.6942	2.9633	2	0	0.00
31	Construction of Kumaramkary Society road	Veliyanad GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	1.777	Under Construction	4.12	3.79	3.2144	3.492	30	15	0.5746
32	Therambilpadi Road	Thalavady GP	Kuttanad	G.O.(Rt).No.18/2022/P&EA	0.892	Under Construction	2.65	2.42	1.988	2.1868	40	0	0.00

33	Footpath Thottuvila First Bridge to Aattutheeram Road	Kainakary GP	Kuttanad	G.O.(Rt).No.18 /2022/P&EA	0.645	Completed	1.62	1.49			100	74	1.197
34	Kanichukulangara Kavala Kalathilveedu Road	Kanjikkuzhy GP	Cherthala	G.O.(Rt).No.18 /2022/P&EA	1.222	Completed	1.81	1.57	1.263		100	43	0.7734
35	Kainad Pally-Karumathra Kshethram Road	Neelamperoor GP	Kuttanad	G.O.(Rt).No.18 /2022/P&EA	0.974	Under Construction	1.98	1.81	1.5102		60	43	0.8472
36	Holy family school to Pazhoor temple road	Kainakary GP	Kuttanad	G.O.(Rt).No.18 /2022/P&EA	0.758	Under Construction	1.47	1.35			90	48	0.703
37	Valiyapalli Kayalpuram School Road	Pulinkunnu GP	Kuttanad	G.O.(Rt).No.30 0/2022/P&EA	1.275	Under Construction	4.83	4.3			6	0	0.00
38	Investigation/data collection			G.O.(Rt).No.11 5/2020/P&EA		Completed	0.82		0.8174	0.5449	100	24	0.1977
39	Soil Investigation in Alappuzha 10 Bridges			G.O.(Rt).No.23 4/2021/P&EA		Completed	0.25	0.25			100	34	0.0859
40	Moorthitta Mukkathery Vazhayi (Chackittapadi bridge)	Mannar GP	Chengannur	G.O.(Rt).No.22 1/2020/P&EA	4.2	Re-tendered	15.2				0	0	0.00
41	Naduvath Moon Bridge	Muttar GP	Kuttanad	G.O.(Rt).No.22 1/2020/P&EA	0.035	DPR Preparation					0	0	0.00
42	Nellanickal Ambalam Road	Muttar GP	Kuttanad	G.O.(Rt).No.22 1/2020/P&EA	0.035	DPR Preparation					0	0	0.00
43	SNDP to Nadukkod	Muttar GP	Kuttanad	G.O.(Rt).No.22 1/2020/P&EA	0.015	DPR Preparation					0	0	0.00
44	SNDP to Vadaparambu Culvert Road	Muttar GP	Kuttanad	G.O.(Rt).No.22 1/2020/P&EA	0.0105	DPR Preparation					0	0	0.00
45	Vallamkadavu Chillithuruth Swamithara road	Chengannoor-Thriperumthura Gp	Chengannoor	G.O.(Rt).No.22 1/2020/P&EA	0.02	DPR Preparation					0	0	0.00

46	SN Jn. to Tsunami smaraka road	Arattupuzha GP	Harippad	G.O.(Rt).No.22 1/2020/P&EA		DPR Preparation					0	0	0.00
TOTAL					55.19		115.37	93.42	76.11	78.202			47.395

PATHANAMTHITTA

SI No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Physical Status	AS Amt.	TS amt	Tendered Amt.	Contract Amt.	Phy. Progress (%)	Fin. Progress (%)	Expenditure(Cr)
1	Renovation of Kottomonpara Melekottomonpara Pandyanpara road	Seethathodu GP	Konni	G.O.(Rt.)No.62/2021/P&EA	1.79	Completed	2.48	2.48	2.0038	1.9291	100	64	1.5917
2	Rehabilitation of Adoor Gopalakrishnan Road	Erathu GP	Adoor	G.O.(Rt.)No.485/2019/P&EA	1.86	Under Construction	2.76	2.4	1.8977	1.9534	78	60	1.473
3	Renovation of CK Road	Kottangal GP	Ranni	G.O.(Rt.)No.485/2019/P&EA	2	Under Construction	2.81	2.25	1.7836	1.8925	70	28	0.657
4	Paivazhy Nediakala Road	Thekkekkara GP	Aranmula	G.O.(Rt.)No.485/2019/P&EA	2.7	Completed	4.202	3.46	2.7723	3.0208	100	72	3.025
5	Renovation of Panchayathpadi Pulluchani Radhapady Road	Aruvappulam GP	Konni	G.O.(Rt.)No.62/2021/P&EA	3.06	Under Construction	4.41	4.04	3.2808	3.597	95	77	3.414
6	Renovation of Police stationpadi TVM hospital Elangavattom Kshetra Road	Konni GP	Konni	G.O.(Rt.)No.62/2021/P&EA	2.89	Under Construction	2.78	2.57	1.9547	2.1454	60	23	0.643
7	Renovation of Chakrasalakadavu Panachimoottil Road	Kuttoor GP	Thiruvalla	G.O.(Rt.)No.485/2019/P&EA	2.4	Under Construction	2.95	2.55	2.094	2.2824	98	71	2.091
8	Improvement of Thannithodu Plantation Road	Thannithodu GP	Konni	G.O.(Rt.)No.485/2019/P&EA	4.32	Completed	5.9418	5.05	4.0737	4.2613	100	68	4.07
9	Reconstruction of Bangalamkadavu Stadium Valiyakulam Road	Vadasserikkar GP	Ranni	G.O.(Rt.)No.485/2019/P&EA	2.9	Under Construction	2.46	2.31	1.873	1.8728	100	50	1.24
10	Reconstruction of Bangalamkadavu Valiyakulam Road	Vadasserikkar GP	Ranni	G.O.(Rt.)No.485/2019/P&EA	2	Completed	2.14	2.05	1.6814	1.6433	100	91	1.94

11	Chana Kurumpanmoozhy Road	Naranamoozhy	Ranni	G.O.(Rt.)No.485/2019/P&EA	2	Under Construction	2.1974	2.18	1.7904	1.7007	90	79	1.736
12	Madukkamood Ayyappa Medical College Road	Vadasserikkar GP	Ranni	G.O.(Rt.)No.485/2019/P&EA	1	Completed	1.39	1.47	1.1821	1.0639	100	81	1.125
13	Rationkadapadi Mulanthanam Road	Perunadu GP	Ranni	G.O.(Rt.)No.485/2019/P&EA	1	Under Construction	1.49	1.36	1.0919	1.1288	35	0	0
14	Arummood-Chala Puthenchantha 14th mile road	Pallikkal GP	Adoor	G.O.(Rt.)No.485/2019/P&EA	1.29	Under Construction	2.068	1.73	1.3583	1.4787	95	16	0.2927
15	Rehabilitation of Athikkayam kadumeenchira Road	Naranamoozhy	Ranni	G.O.(Rt.)No.348/2021/P&EA	1.83	Under Construction	3.05	2.4	1.8423	1.8506	75	34	1.0342
16	Rehabilitation of Valiyaparambil Eetichuvadu Road	Pazhavangadi GP	Ranni	G.O.(Rt.)No.348/2021/P&EA	1.33	Completed	1.7	1.5	1.1769	1.1664	100	61	1.0448
17	Rehabilitation of Janaseva Road	Peringara GP	Thiruvalla	G.O.(Rt.)No.348/2021/P&EA	1.54	Under Construction	3.1	2.84	2.3319	2.3218	50	24	0.7588
18	Anthyalankavu Marthomapallipadi Karamvelipadi road	Narananganam GP	Aranmula	G.O.(Rt.)No.485/2019/P&EA	0.978	Completed	1.47	1.35	1.0759	1.1079	100	89	1.313
19	Kiliyanikal Thoolikulam Road	Cherukol GP	Ranni	G.O.(Rt.)No.485/2019/P&EA	1.4	Under Construction	1.73	1.45	1.1108	1.2585	100	59	1.02
20	Reconstruction of Parakkavu Valakuzhy Road	Ezhumattoor GP	Ranni	G.O.(Rt.)No.485/2019/P&EA	1.75	Completed	2.13	1.8	1.4124	1.5535	100	74	1.4521
21	Reconstruction of Melepadi Chellakadu Road	Pazhavangadi GP	Ranni	G.O.(Rt.)No.485/2019/P&EA	1.558	Under Construction	2.23	2.01	1.649	1.7181	80	56	1.25
22	Rehabilitation of Ushuspadi Vellaparamuruppu Kizhakkekkarapalli road	Ezhamkulam GP	Adoor	G.O.(Rt.)No.348/2021/P&EA	1.6	Under Construction	2.25	2.03	1.5712	1.6261	90	50	1.12
23	Erathodu Ashankuzhy Road	Niranam GP	Thiruvalla	G.O.(Rt.)No.485/2019/P&EA	1.2	Under Construction	2.0973	1.9	1.5591	1.6152	70	31	0.6039

24	Rehabilitation of Koipallimelethilpadi road	Ayroor GP	Ranni	G.O.(Rt.)No.18/2022/P&EA	0.86	Under Construction	1.44	1.43	1.1745	1.1146	4	0	0
25	Rehabilitation of Ozhukkuneettilpadi Paruthimoottilpadi Road	Peringara GP	Thiruvalla	G.O.(Rt.)No.18/2022/P&EA	0.93	Under Construction	3.47	2.82	2.3329	2.25	95	42	1.4719
26	Reconstruction of Kannankara Edamuri Road	Pazhavangadi GP	Ranni	G.O.(Rt.)No.348/2021/P&EA	0.82	Under Construction	1.232	1.13	0.8596	0.9451	95	63	0.776
27	Vattathenpadi Nallathupadi Road	Aranmula GP	Aranmula	G.O.(Rt.)No.485/2019/P&EA	1.17	Completed	1.15	1.01	0.704	0.8133	100	100	1.8411
28	Malayuman Vazhayilpadi Road	Aranmula GP	Aranmula	G.O.(Rt.)No.348/2021/P&EA	0.93	Under Construction	1.11	0.92	0.714		20	0	0
29	Ramapuram Illathupadi Valiyathupadi road	Ranni GP	Ranni	G.O.(Rt.)No.300/2022/P&EA	1.245	Under Construction	0.92	0.85	0.626	0.652	95	0	0
30	Pulikkeezhu Road	Kottangal GP	Thiruvalla	G.O.(Rt.)No.300/2022/P&EA	2.25	Under Construction	3.05	2.6	2.14	2.26	15	0	0
31	Papanattupadi Panchayathupadi Road	Kottangal GP	Ranni	G.O.(Rt.)No.300/2022/P&EA	2.02	Under Construction	2.22	2.22	1.533	1.531	50	32	0.707
32	Poovanmala Panamplackal Road	Angadi GP	Ranni	G.O.(Rt.)No.485/2019/P&EA	1.214	Under Construction	1.19				2	0	0
33	Reconstruction of Kalarikode Pallana Puthenvelipadi Road	Aranmula GP		G.O.(Rt.)No.485/2019/P&EA	1.222	Under Construction	1.96				5	0	0
34	Investigation/ Data collection			G.O.(Rt.)No.115/2020/P&EA		Completed	0.4152		0.4152	0.2768	100	30	0.1261
35	Design and DPR preparation of 218km Roads			G.O.(Rt.)No.138/2020/LSGD		Completed	0.3074		0.3074	0.3074	100	83	0.254
36	Soil investigation of 3 Bridges			G.O.(Rt.)No.234/2021/P&EA		Completed	0.06	0.06			100	0	0
	TOTAL				57.05		78.36	66.22	55.55	57.46			37.23

KOTTAYAM

SI No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Physical Status	AS Amt.	TS Amt	Tendered Amt.	Contract Amt.	Phy. Progress (%)	Fin. Progress (%)	Expenditure(Cr)
1	Improvement of Girideepam Kadathukadavu Road	Vijayapuram GP	Kottayam	G.O.(Rt.)No.224/2020/P&EA	1.86	Completed	1.75	1.75	1.2935	1.2392	100	85	1.4958
2	Improvement of Pathinanchilkadavu Illikkal Road	Kottayam GP	Kottayam	G.O.(Rt.)No.224/2020/P&EA	2	Completed	4	4	2.9446	2.9301	100	87	3.491
3	Improvement of Kunnumpuram Mahilaamajam Road	Thiruvarpur GP	Ettumanoor	G.O.(Rt.)No.224/2020/P&EA	1	Completed	1.84	1.84	1.3434	1.3247	100	78	1.4322
4	Renovation of kavanattinkara Manchira Road	Aymanam GP	Ettumanoor	G.O.(Rt.)No.224/2020/P&EA	1.3	Completed	0.93	0.93	0.6712	0.6501	100	90	0.8393
5	Renovation of TV Puram Theeradesam Road	TV Puram GP	Vaikom	G.O.(Rt.)No.224/2020/P&EA	3.79	Completed	3.84	3.5	2.9401	3.2337	100	100	3.5851
6	Malakkunnam Kannanthrappadi Road	Kurichy GP	Changanassery	G.O.(Rt.)No.224/2020/P&EA	1.125	Completed	1.27	1.19	0.8096	0.8898	100	87	1.0352
7	Olassa Cherthalli Road	Aymanam GP	Ettumanoor	G.O.(Rt.)No.404/2020/P&EA	0.968	Terminated	1.21	1.21	1.0104	0.9829	65	33	0.395
8	Kambanikkadavu Pattarmadon Road	Ettumanoor GP	Ettumanoor	G.O.(Rt.)No.404/2020/P&EA	1.32	Completed	1.14	1.14	0.9258	0.8885	100	90	1.0211
9	Reconstruction of Madathilkadavu Mahilasamajam Kandathilpalli Road	Thiruvarpur GP	Ettumanoor	G.O.(Rt.)No.404/2020/P&EA	0.85	Under Construction	1.54	1.45	1.2218	1.3046	0	0	0.00
10	Cheepunkal-Malikayalchira Road	Aymanam GP	Ettumanoor	G.O.(Rt.)No.404/2020/P&EA	1	Completed	1.48	1.48	1.2318	1.2195	100	94	1.386
11	Reconstruction of LPS Mukkam Kollori Road	Chempu GP	Vaikom	G.O.(Rt.)No.404/2020/P&EA	0.33	Under Construction	0.5618	0.52	0.4275	0.4683	45	1	0.0033

12	Reconstruction of Govt. HS Kochalivattom road	Kumarakom GP	Ettumanoor	G.O.(Rt.)No.62/2021/P&EA	0.4	Completed	0.306	0.28	0.2259	0.2482	100	98	0.299
13	Investigation / Data Collection			G.O.(Rt.)No.115/2020/P&EA		Completed	0.1208		0.1208	0.0951	100	13	0.0156
14	Soil Investigation of 2 Bridges			G.O.(Rt.)No.234/2021/P&EA		Completed	0.04	0.04			100	80	0.031
					15.94		20.03	19.33	15.16	15.47			15.03

IDUKKI

SI No.	Name of Work	Local Body	LAC	Length(Km)	AS No.	Physical Status	AS Amt.	TS amt	Tendered Amt.	Contract Amt.	Phy. Progress (%)	Fin. Progress (%)	Expenditure(Cr)
1	Improvement of Asramam Pottanpadi Road	Arakkulam GP	Idukki	1.5	G.O.(Rt.)No.485 /2019/P&EA	Terminated	1.594	1.63	1.3	1.1995	0	0	0
2	Improvement of Adivaram Ottalangalpady city Road	Rajakkad GP	Udumbanchola	0.878	G.O.(Rt.)No.485 /2019/P&EA	Completed	3.12	2.97	2.2782	2.2511	100	71	2.21
3	Improvement of Ambalappara Kadaplackal Road	Upputhara GP	Peerumedu	0.75	G.O.(Rt.)No.485 /2019/P&EA	Completed	0.877	1	0.8091	0.6709	100	33	0.3252
4	Improvement of Ellappallithottam bhagom Road	Arakkulam GP	Idukki	1.45	G.O.(Rt.)No.485 /2019/P&EA	Completed	1.732	1.93	1.556	1.308	100	88	1.53
5	Improvement of Ellappalli Chellikkal Road	Arakkulam GP	Idukki	5.225	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	4.67	4.33	3.4625	3.1298	72	28	1.322
6	Improvement of Pazhaya Kochira Road	Vandanmedu GP	Udumbanchola	0.55	G.O.(Rt.)No.485 /2019/P&EA	Completed	1.635	1.61	1.3136	1.2553	100	90	1.4557
7	Improvement of Vimalagiri - Enikuthu Road	Mariyapuram GP	Idukki	1.61	G.O.(Rt.)No.485 /2019/P&EA	Completed	2.385	2.5	2.027	1.8182	100	79	1.891
8	Improvement of Anachal Thokkupara Acherikunnu Asramam Road	Vellathooval GP	Devikulam	1.6	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	2.24	2.11	1.7144	1.5873	98	10	0.2128

9	Improvemnt of Murikkumthotti-Mathekkalpadi Shallyil Road	Rajakumari GP	Udumban chola	1.8	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	1.264	1.22	0.9643	0.8645	98	0	0.0026
10	Improvement of Kattekkanam Chelamoodu Road	Karunapuram GP	Udumban chola	1.9	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	0.981	0.89	0.685	0.737	60	0	0.0018
11	Improvment of Idinjamala Companyadi road	Erattayar GP	Udumban chola	8.1	G.O.(Rt.)No.485 /2019/P&EA	Completed	7.878	6.77	5.1368	5.5859	100	92	6.6792
12	Improvement of Perumbankuthu 6th mile Road	Mankulam GP	Devikulam	3.9	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	4.44	3.71	2.9094	3.1899	70	24	1.065
13	Improvement of Kurishupallipadi Thannikkandam Painavu Road	Vazhathoppu GP	Idukki	3.5	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	3.607	3.05	2.3698	2.6029	60	19	0.684
14	Improvement of Suryanelli Gundumala Road	Chinnakkanal GP	Devikulam	2.4	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	2.103	1.89	1.4479	1.5891	65	21	0.466
15	Reconstruction of Factoryadi karintharuvi Road	Upputhara GP	Peerumed u	3.3	G.O.(Rt.)No.348 /2021/P&EA	Completed	3.22	3.22	2.6584	2.4446	100	77	2.473
16	Reconstruction of Suryakanthikavala Old Post office Road	Upputhara GP	Peerumed u	1.3	G.O.(Rt.)No.348 /2021/P&EA	Under Construction	1.3	1.3	1.0761	0.9889	100	58	0.754
17	Improvemnt of Panachikuzhi road	Rajakkad GP	Udumban chola	5.1	G.O.(Rt.)No.485 /2019/P&EA	Completed	4.577	4.42	3.3761	3.2497	100	91	4.0154
18	Improvement of Padicup Plakkayam Kuttamudi Tribal Colony road	Adimaly GP	Devikulam	4.2	G.O.(Rt.)No.485 /2019/P&EA	Completed	4.668	5.06	4.0507	3.4994	65	18	0.9318

19	Improvement of Perikkankavala Kollamkulambadi Kaikavala Road	Vathikudy GP	Idukki	0.6	G.O.(Rt.)No.485 /2019/P&EA	Completed	1.982	2.06	1.709	1.5678	100	93	1.85
20	Improvement of Puthed Anoorhode Footbridge Road	Arakkulam GP	Idukki	5	G.O.(Rt.)No.485 /2019/P&EA	Terminated	3.957	3.83	2.9954	2.9012	0	0	0
21	Balagram Anyarthulu road	Pampadumpara GP	Udumbanchola	6.4	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	8.66	7.56	5.8442	5.9702	95	56	4.83
22	Naalumukku- Tunnelsite Road	Erattayar GP	Udumbanchola	2.75	G.O.(Rt.)No.485 /2019/P&EA	Completed	2.47	2.14	1.6137	1.7247	100	84	2.075
23	Improvement of pallikudicity Mangathupalam Road	Vathikudy GP	Idukki	1	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	2.62	2.7	2.1475	1.9673	98	53	1.4203
24	Rehabilitation of Kannamplackalpathi Puthenpalam Road	Nedumkandam GP	Udumbanchola	0.86	G.O.(Rt.)No.18/2022/P&EA	Under Construction	1.13	1.1	0.8631	0.8221	42	22	0.254
25	Thattakkallu Ponnezhuthan	Kanjikkuzhy GP	Idukki	2.205	G.O.(Rt.)No.300 /2022/P&EA	Under Construction	3.25	3.25	2.604	2.206	50	17	0.566
26	Bhoomiyamkulam Keshamini Road	Kanjikkuzhy GP	Idukki	1.95	G.O.(Rt.)No.300 /2022/P&EA	Under Construction	1.9	1.9	1.593	1.312	15	10	0.193
27	Araikkalpathi Ambikavilasam Estatepathi Road	Senapathy GP	Udumbanchola	1.95	G.O.(Rt.)No.300 /2022/P&EA	Under Construction	5.65	5.65	4.598	3.815	50	26	1.464
28	50th mile Kallakuttykudi Mankulam Road	Mankulam GP	Devikulam	2.5	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	3.868	3.602	2.85		2	0	0
29	Mangathotti Kanakapuzha NR City Road	Senapathy GP	Udumbanchola	4	G.O.(Rt.)No.485 /2019/P&EA	Under Construction	7.59	7.394	5.61		28	3	0.244

30	Investigation /Data collection				G.O.(Rt.)No.115 /2020/P&EA	Completed	1.90		1.9027	1.3148	100	33	0.6196
31	Design and DPR preparation of 218km Roads				G.O.(Rt.)No.138 9/2020/LSGD	Completed	0.64		0.648	0.648	100	66	0.4295
32	Soil investigation of 12 bridges				G.O.(Rt.)No.234 /2021/P&EA	Completed	0.34	0.341		0.21	100	53	0.1807
33	Kallarmukku bridge	Nedumkandom GP	Udumban chola	0.0125	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
34	Panthrandammile mezhukunnel palam and approach Road	Adimaly GP	Devikulam	0.0403	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
35	Thooval bridge	Nedumkandom GP	Udumban chola	0.022	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
36	Upputhodu Ponnachipadi Bridge	Vathikudy GP	Idukki	0.0133	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
37	Mulakuvalli-PulavanalluKokkarakulam Bridge	Vazhathoppu GP	Idukki	0.01	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
38	Moozhikkal - Thoppilkadavu Bridge	Peruvanthanam GP	Peerumedu	0.038	G.O.(Rt.)No.221 /2020/P&EA	DPR submitted to RKI for AS	7.65				0	0	0
39	Maniyanpara - Kanjiraveli bridge	Adimaly GP	Devikulam	0.078	G.O.(Rt.)No.221 /2020/P&EA	DPR submitted to RKI for AS	5				0	0	0
40	Hanging bridge in 11th ward	Munnar GP	Devikulam	0.06	G.O.(Rt.)No.221 /2020/P&EA	Taken by another project, so dropped					0	0	0

41	Chittoor- Madathinkadavu	Manakkad GP	Thodupuzha	0.055	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
42	Olamattom Thekkumbhagomkadavu bridge	Edavetty GP	Thodupuzha	0.066	G.O.(Rt.)No.221 /2020/P&EA	DPR Preparation					0	0	0
	TOTAL			78.67			111.03	91.14	74.11	68.42			40.14

ERNAKULAM

SI No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Physical Status	AS Amt.	TS amt	Tendered Amt.	Contract Amt.	Phy. Progress(%)	Fin. Progress (%)	Expenditure (Cr)
1	Upgradation of Pannikkuzhy Kavumthazhom Road	Vadavucode Puthencruz GP	Thrippunithura	G.O.(Rt.)No.224 /2020/P&EA	1.2	Completed	1.81	1.81	1.42	1.25	100	79	1.431
2	Rehabilitation of Pavamkulangara Kannankulangara Road	Thrippunithura	Thrippunithura	G.O.(Rt.)No.224 /2020/P&EA	1.953	Completed	1.32	1.32	0.97	0.95	100	41	0.539
3	Upgradation of Vayalodam Thadikkadavu Road	Karimannoor GP	Kalamasserry	G.O.(Rt.)No.224 /2020/P&EA	0.905	Completed	1.38	1.38	0.914	0.9138	100	72	0.988
4	Renovation of Valavazhy Road	Angamaly	Angamaly	G.O.(Rt.)No.224 /2020/P&EA	0.835	Under Construction	0.9596	0.87	0.658	0.648	6	0	0
5	Rehabilitation of Paduvathil Police station Road	Kadungalloor GP	Kalamasserry	G.O.(Rt.)No.224 /2020/P&EA	0.625	Tender excess received	0.66	0.66	0.5006	0.4947	0	0	0
6	Upgradation of Kadungalloor Masjid Road	Kadungalloor GP	Kalamasserry	G.O.(Rt.)No.224 /2020/P&EA	0.515	Completed	0.72	0.72	0.481	0.4809	100	66	0.4736
7	Upgradation of Anicadu Pravidakunnu Road	Avoly GP	Muvattupuzha	G.O.(Rt.)No.224 /2020/P&EA	1.166	Completed	1.3	1.3	1.0883	1.075	100	81	1.051
8	Renovation of Okkal Juma masjid Road	Okkal GP	Perumbavoor	G.O.(Rt.)No.224 /2020/P&EA	0.165	Completed	0.166	0.166	0.1409	0.1318	100	89	0.147
9	Reconstruction of BJP Kadavu Road	Okkal GP	Perumbavoor	G.O.(Rt.)No.224 /2020/P&EA	0.18	Completed	0.12	0.12	0.1	0.0928	100	82	0.098
10	Rehabilitation of St. Mary's Swaraj Road	Kumbalangi GP	Kochi	G.O.(Rt.)No.224 /2020/P&EA	0.567	Completed	0.6	0.6	0.501	0.501	100	51	0.272
11	Panjamkavala Ward18 Road	Chendamangalam GP	Paravur	G.O.(Rt.)No.404 /2020/P&EA	1.1	Completed	1.34	1.34	1.0426	0.997	100	74	0.992

12	Improvement of Edathod palli basilica road	Angamaly	Angamaly	G.O.(Rt.)No.62/2021/P&EA	1.04	Completed	0.52	0.52	0.4116	0.4039	100	88	0.455
13	Construction of Musiris Puzhayoram Road	Chendamangalam GP	Paravur	G.O.(Rt.)No.404/2020/P&EA	0.26	Completed	1.08	1	0.8399	0.9156	100	37	0.4035
14	Nadakkavu Ethiyerakavu road	Vazhakulam GP	Kunnathunadu LAC	G.O.(Rt.)No.62/2021/P&EA	0.705	Completed	0.43	0.41	0.2877	0.3161	100	62	0.268
15	Upgradation of Kallanchery Tharassery Road	Kumbalangi GP	Kochi	G.O.(Rt.)No.18/2022/P&EA	1.55	Under Construction	3.39	3.1	2.5728	2.83	90	39	1.205
16	Upgradation of Thiruvaniyoor Meppadom Road	Thiruvaniyoor GP	Kunnathunadu LAC	G.O.(Rt.)No.18/2022/P&EA	3.1	Under Construction	3.568	3.42	2.5597	2.6811	85	58	2.074
17	Sahi Rubber Ambalamukku Kattuman Road	Edathala GP	Aluva	G.O.(Rt.)No.300/2022/P&EA	1.325	Completed	1.7	1.7	1.331	1.301	100	82	1.3937
18	Investigation/ Data collection			G.O.(Rt.)No.115/2020/P&EA		Completed	0.2057		0.2057	0.1526	100	19	0.039
19	Soil Investigation of 9 bridges			G.O.(Rt.)No.234/2021/P&EA		Completed	0.275	0.271			100	0	0
20	Construction of Kaippettipalam	Karimannoor GP	Kalamasserry	G.O.(Rt.)No.221/2020/P&EA	0.028	DPR Submitted to RKI for AS	3.4				0	0	0
21	Construction of Varatupadi Colonypadi Palam	Alangad GP	Kalamasserry	G.O.(Rt.)No.221/2020/P&EA	0.017	DPR Submitted to RKI for AS	3.85				0	0	0
22	Reconstruction of Chembikkad Madrasappadi Road (Extension of Vayalodam Thadikkadavu Road)	Karimannoor GP	Kalamasserry	G.O.(Rt.)No.422/2022/P&EA	0.982	Completed	1.76	1.6	1.26	1.325	100	65	1.154
	TOTAL				18.81		31.58	23.34	18.05	18.25			12.98

THRISSUR

SI No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Physical Status	AS Amt.	TS Amt	Tendered Amt.	Contract Amt.	Phy. Progress(%)	Fin. Progress(%)	Expenditure(Cr)
1	Rehabilitation of Thandilam Manali Kecheri Road	Velur GP	Kunnamkulam	G.O.(Rt.)No.224/2020/P&EA	5	Completed	5	5	3.6692	3.6479	100	85	4.282
2	Improvement of Chittanda Padinjattumuri Road	Erumapetty GP	Kunnamkulam	G.O.(Rt.)No.224/2020/P&EA	5.4	Completed	6.72	6.72	5.4	5.09	100	85	5.74
3	Chillukarankunnu Road	Punnayurkulam GP	Guruvayoor	G.O.(Rt.)No.404/2020/P&EA	1.2	Completed	0.96	0.96	0.7093	0.6754	100	87	0.833
4	kuranchery Nayarangadi Road	Thekkumkara GP	Vadakkanchery	G.O.(Rt.)No.404/2020/P&EA	4.99	Under Construction	12.5	12.5	9.8568	9.8285	96	83	10.388
5	Improvement of Karoorchira Anchalangadi Road	Aloor GP	Irinjalakuda	G.O.(Rt.)No.404/2020/P&EA	1.65	Under Construction	2.12	1.95	1.5563	1.6963	58	28	0.601
6	Rehabilitation of Paris Road	Kandanassery GP	Manalur	G.O.(Rt.)No.404/2020/P&EA	1.31	Under Construction	1.85	1.7	1.3425	1.4642	30	13	0.2403
7	Improvement of Puthiyakavu pozhankavu Road	Mathilakom GP	Kaipamangalam	G.O.(Rt.)No.404/2020/P&EA	0.84	Completed	0.823	0.75	0.6129	0.6734	100	93	0.7618
8	Rehabilitation and Reconstruction of Ex-Servicemen Colony centre Road	Athirappilli GP	Chalakkudy	G.O.(Rt.)No.62/2021/P&EA	2.1	Under Construction	2.76	2.6	1.9077	2.044	98	81	2.24
9	Kuzhur Iranikulam Indhira gandhi Road	Kuzhur GP	Kodungalloor	G.O.(Rt.)No.300/2022/P&EA	1.92	Under Construction	3.38	3.38	2.7	2.505	48	23	0.792
10	Chottilappara Bridge	Choondal GP	Manalur	G.O.(Rt.)No.221/2020/P&EA	0.012	Under construction	3.087	2.9	2.203		4	0	0.0297
11	Investigation/Data collection			G.O.(Rt.)No.115/2020/P&EA		Completed	0.3854		0.3854	0.2802	100	13	0.0493
12	Thali Viruttanam Road	Varavoor GP	Vadakkanchery	G.O.(Rt.)No.221/2020/P&EA	0.013	DPR Preparation					0	0	0
	TOTAL				24.43		39.59	38.46	30.34	30.27			25.99

WAYANAD

SI No.	Name of Work	Local Body	LAC	AS No.	Length(Km)	Physical Status	AS Amt.	TS amt	Tendered Amt.	Contract Amt.	Phy. Progress(%)	Fin. Progress (%)	Expenditure(Cr)
1	Chakram Colony Road	Pozhuthana GP	Kalpetta	G.O.(Rt.)No.404 /2020/P&EA	0.83	Completed	0.93	0.93	0.758	0.000.6821	100	66	0.61114
2	Maravayal Chathothu Road	Pozhuthana GP	Kalpetta	G.O.(Rt.)No.404 /2020/P&EA	1.29	Under Construction	1.6	1.6	1.335	1.2127	93	66	1.054
3	Improvement of CheriyaMKolli Kalluvettumthazhe Road	Padinjarethara GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	1.9	Completed	1.5164	1.44	1.09	1.0591	100	66	0.9504
4	Improvement of Ediyamvayal Pinangodu Road	Pozhuthana GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	2.4	Completed	2.22	2.22	1.6774	1.5423	100	77	1.707
5	Improvement of Erumatherivu Choottakadavu Road	Mananthavady GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	1.8	Under Construction	2.8793	2.46	1.7896	1.9682	85	59	1.5475
6	Improvement of Karlad Manjoora Road	Thariod GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	2.1	Completed	1.89	1.89	1.4417	1.3084	100	53	0.9943
7	Improvement of Kuppadithura Millumukku Kurumani Road	Padinjarethara GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	1.5	Completed	1.4394	1.45	1.1	1.1	100	74	1.06
8	Improvement of Kottathara Kakkanchal Thekkumthara road	Kottathara GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	1.9	Completed	2.5791	2.74	2.2526	2.2526	100	57	1.5582
9	Improvement of Varyad Thekkumpadi Road	Muttill GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	1.3	Under Construction	1.9218	1.87	1.53	1.5	100	68	1.2681

10	Improvement of Chundel Chundel estate pappala Anoth Road	Vythiri GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	5.4	Completed	5.56	5.661	4.3236	3.8668	100	74	4.12
11	Improvement of MH Nagar - Cholapuram Road	Vengappally GP	Kalpetta	G.O.(Rt.)No.485 /2019/P&EA	2.7	Completed	2.3353	2.4	1.8558	1.6335	100	80	1.86
12	Improvement of Thazhe Arappetta Mankunnu Road	Muppianad GP	Kalpetta	G.O.(Rt.)No.62/ 2021/P&EA	3.656	Under Construction	4.2	4.2	3.274	3.0978	93	64	2.71
13	Rehabilitation of Thazhathangadi Thanitheruvu Road	Pulpalli GP	Sulthan Bathery	G.O.(Rt.)No.62/ 2021/P&EA	1.33	Completed	1.2	1.2	0.9441	0.9191	100	82	0.9858
14	Improvement of Varayal - Melevarayal Road	Thavinjal GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	1.5	Completed	1.3973	1.34	1.0106	0.979	100	67	0.9
15	Improvement of Kattimoola Aroola Kolathada Road	Thavinhal GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	3.7	Completed	2.9522	2.79	2.1266	2.0662	100	74	2.064
16	Improvement of Korome Karimbil Road	Thondernad GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	4.1	Completed	5.8201	5.6	4.4587	4.2993	100	84	4.87
17	Improvement of Orappu Evaranikkulam Kattimoola Road	Thavinjal GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	4.5	Completed	3.634	3.45	2.6093	2.5173	100	82	2.997
18	Improvement of Puthiyedam Makkimala Road	Thavinjal GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	4.2	Completed	4.085	3.89	2.902	2.813	100	78	3.0403
19	Improvement of 44th mile Makkimala Road	Thavinjal GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	5.5	Under Construction	3.3081	3.09	2.39	2.3545	80	3	0.1076
20	Improvement of Panamaram Keenjukuradavu Road	Panamaram GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	4.7	Under Construction	6.61	6.22	4.8684	4.7356	75	47	3.114

21	Improvement of Pilakkavu Pancharakolli Road	Mananthavady GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	3.1	Completed	3.3095	3.09	2.3803	2.3223	100	79	2.4295
22	Improvement of Kollikandam Kunneri Nelom Road	Thondernad GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	2	Completed	1.2383	1.1	0.7727	0.8213	100	9	0.1026
23	Improvement of Valliyurkavu Varadimoola Road	Mananthavady GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	1.6	Under Construction	1.3947	1.45	1.1336	0.9963	80	62	0.8622
24	Improvement of Vilanilam Pilakkavu Road	Mananthavady GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	2.6	Stay to re-tender	3.8466	3.89	3.0935	2.787	28	15	0.5943
25	Improvement of Thannikkal Payyampalli Road	Mananthavady GP	Mananthavady	G.O.(Rt.)No.485 /2019/P&EA	1.8	Under Construction	2.2606	1.91	1.46058	1.5557	75	8	0.1508
26	Improvement of Kalpetta Town Jilla Stadium Road	Kalpetta GP	Kalpetta	G.O.(Rt.)No.348 /2021/P&EA	3.6	Completed	3.026	2.97	2.1802	2.3231	100	78	2.35
27	Eranjoli pulikkal Road	Kaniyambetta GP	Kalpetta	G.O.(Rt.)No.18/ 2022/P&EA	2.269	Site handedover	3.38	3.38	2.7585	2.6115	0	0	0
28	Improvement of Changadakadavu Chamadipoyil Road	Edavaka GP	Mananthavady	G.O.(Rt.)No.18/ 2022/P&EA	1.757	Completed	3.04	3.04	2.3899	2.1842	100	57	1.7436
29	Investigation/ Data Collection			G.O.(Rt.)No.115 /2020/P&EA		Completed	0.7243		0.7243	0.5436	100	27	0.1943
30	Design and DPR Preparation of 218km Roads			G.O.(Rt.)No.138 9/2020/LSGD		Completed	0.3979		0.3979	0.3979	100	92	0.3647
31	CBR investigation of Roads			G.O.(Rt.)No.225 7/2020/LSGD		Completed	0.0546				100	87	0.0475
32	Topographic survey for Roads			G.O.(Rt.)No.166 9/2020/LSGD		Completed	0.0246				100	62	0.0153
33	41Mile Varayal Bridge	Thavinjal GP	Mananthavady	G.O.(Rt.)No.221 /2020/P&EA	0.015	Under Construction	2				2	0	0.099
	TOTAL				75.05		82.78	77.27	62.71	59.47			46.47

10.LIST OF BRIDGES

Sl. No.	District	LAC	Local Body	Name of bridge	Type of Bridge	Approximate span	Remarks	Amount (Lakhs)
1	Alappuzha	Chengannur	Mannar Gp	Moorthitta Mukkatheri Vazhayi(Chackittapady Bridge)	RCC	12	Tender excess received	1728
2	Alappuzha	Kuttanad	Neelamperoor GP	Naduvath moon bridge	RCC	20	Design work in progress by consultant Thixotropy	
3	Alappuzha	Kuttanad	Nellar GP	Nellanickal Ambalam Road	RCC	35	Design work in progress by consultant Thixotropy	
4	Alappuzha	Kuttanad	Muttar GP	SNDP to Nadukkodu	RCC	15	Design work in progress by consultant Thixotropy	
5	Alappuzha	Kuttanad	Muttar GP	SNDP to Vadaparambu Culvert Road	RCC	10.5	Design work in progress by consultant Thixotropy	
6	Alappuzha	Haripad	Arattupuzha GP	SN Junction Tsunami Smaraka Road			Design work in progress by consultant Thixotropy	
7	Alappuzha	Chenganoor	Chennithala GP	Vallamkadavu Chillithuruth Swamithara Road	RCC	21	Design work in progress by consultant Thixotropy	
8	Idukki	Udumbunchola	Nedumkandam	Kallarmukku Bridge	RCC	12.5	Design work in progress by consultant Thixotropy	
9	Idukki	Devikulam	Adimaly	Panthrandam mile mezhukunel palam and approach road	RCC	40.3	Design work in progress by consultant Thixotropy	
10	Idukki	Udumbunchola	Nedumkandam	Thooval Bridge	RCC	22	Design work in progress by consultant Thixotropy	
11	Idukki	Idukki	Vathikudy GP	Upputhodu-Ponnachipadi Bridge	RCC	13.3	Design work in progress by consultant Thixotropy	

12	Idukki	Idukki	Vazhathoppu GP	Mulakuvalli-PulavanalluKokkarakkulam Bridge	RCC	10	Design work in progress by consultant Thixotropy	
13	Idukki	Peermedu	Peruvanthanam GP	Moozhikkal-Thoppilkadavu Bridge	RCC	38	DPR Submitted to RKI for AS	765
14	Idukki	Devikulam	Adimaly GP	Maniyampara-Kanjiraveli Bridge	Steel footbridge	78	DPR submitted to RKI for AS	500
15	Idukki	Devikulam	Munnar GP	Hanging Bridge in 11th Ward	Steel footbridge	60	Taken under another project. Informed by MLA. Dropped.	
16	Idukki	Thodupuzha	Manakkad GP	Chittoor-Madathinkadavu	Steel footbridge	55	Tendered 3 times. No response. Decided to prepare DPR in-house.	
17	Idukki	Thodupuzha	Idavetty GP	OlamattomThekkumbhagom kadavu bridge	Steel footbridge	60	Tendered 3 times. No response. Decided to prepare DPR in-house.	
18	Ernakulam	Kalamaserry	Karimalur	Construction of kaipettipalam	RCC	28	DPR submitted to RKI for AS	340
19	Ernakulam	Kalamaserry	Alangad GP	Construction of Varatupadi Coloni padi palam	RCC	17	DPR submitted to RKI for AS	385
20	Palakkad	Nenmara	Vadavannur GP	Allambalampalam road	RCC	55	DPR submitted to RKI for AS	550
21	Thrissur	Vadakkanchery	Varavoor GP	Thali Viruttanam Road	RCC	13	Design work in progress	
22	Wayanad	Mananthavady	Thovinhal GP	41-mile varayal bridge	RCC	15	Selection notice issued, agreement executed, under construction	200
23	Kannur	Peravoor	Aralam GP	Manchuvadu bridge	RCC	12	DPR submitted to RKI for AS	310
24	Thrissur	Manalur	Choondal GP	Chottilappara Bridge	RCC	12	Selection notice issued, agreement executed, under construction	308.77

25	Alappuzha	Alappuzha	Mannancherry GP	Mannancherry Jn Puthanparambu Thaikkavu Road	RCC	9.6	Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km
26	Alappuzha	Haripad	Pallipad GP	Anjilimoodu Sudheesh Bhavanam road	RCC	10.2	Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km
27	Pathanamthitta	Aranmula	Mallapuzhaserry	Chakkittapadi korakodepadi road(kolakuzhy bridge)-walk way bridge	RCC	8.6	Bridge work taken up by other agency. Reported by EE PIU Kottayam
28	Pathanamthitta	Thiruvalla	Kalopara	Shastangal vakkayil kadavu thottipara(managed by irrigation department)	RCC	9.3	Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km
29	Ernakulam	Muvattupuzha	Ayavana GP	Suspension bridge at Keecherikadavu	Steel footbridge	66	Bridge work taken up by other agency (PMGSY). Reported by EE PIU Thrissur
30	Ernakulam	Kalamaserry	Eloor Municipality	Construction of pachamukku unthithodu palam and approach road	RCC	13.5	Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km
31	Ernakulam	Kothamangalam	Kuttampuzha	Manikandanchal Vellaramkuthu St Colony road	RCC	8.5	Transferred to CE LSGD. Road width less than 3m or Road length less than 1 km
32	Ernakulam	Kunnathuadu	Thiruvaniyoor GP	Thiruvaniyoor Mepadam Road	RCC	8.3	No new Bridge required. Reported by EE PIU Thrissur.
